


NORTH WESTERN RAILWAY

(As on 02.04.24)



SYSTEM MAP  
SANCTIONED NL/GC/DL WORKS ( IN PROGRESS )

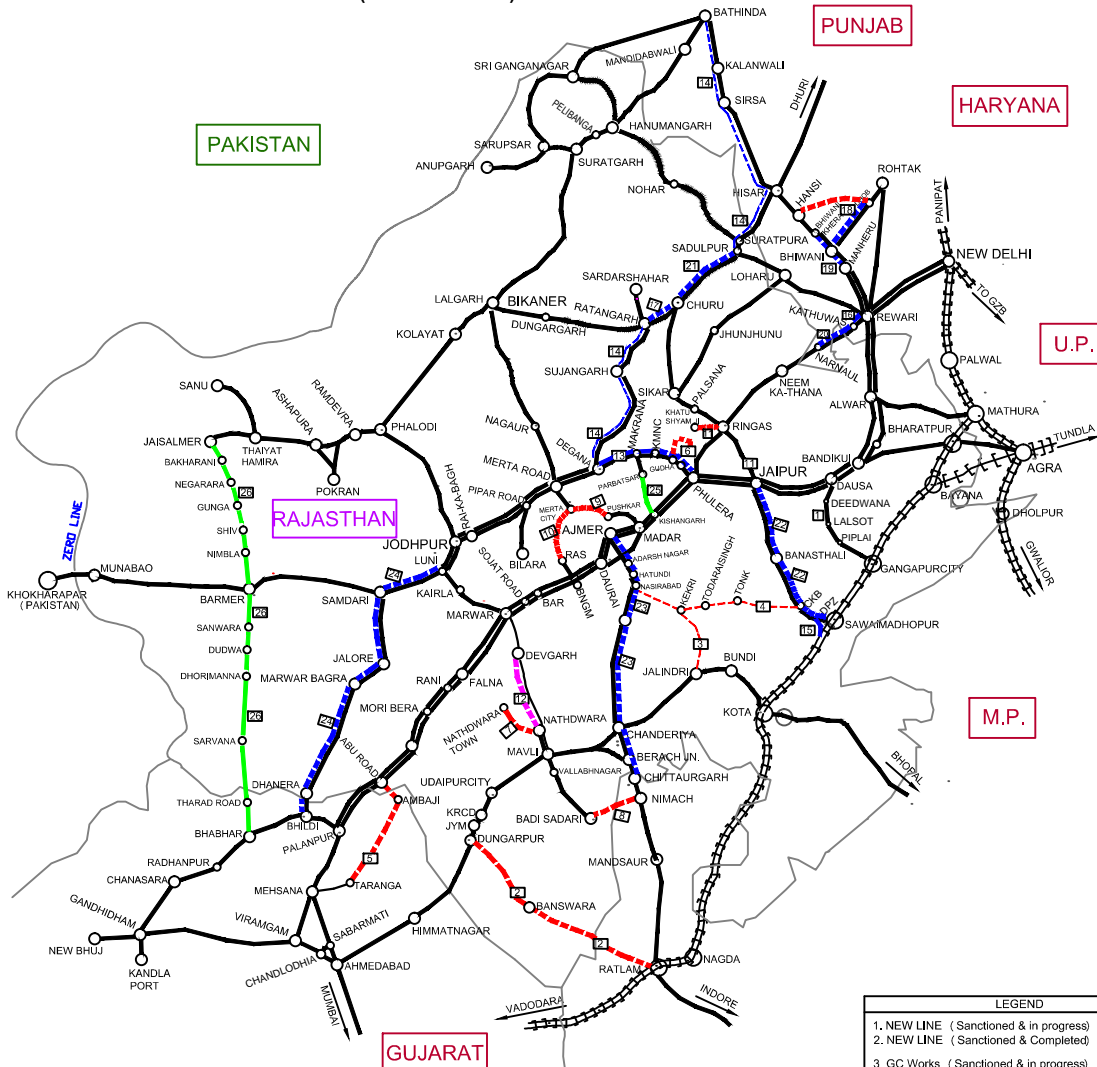

LIST OF SANCTIONED WORKS OVER NWR					
Sr. No.	NAME OF WORK	SALIENT FEATURES		PHYSICAL PROGRESS & TDC	
		YEAR OF SANCTION	COST IN CR.		LENGTH IN KM
<b>A. NEW LINE</b>					
1	DAUSA - GANGAPUR CITY NEW LINE Dausa-Deedwana, CRS done on 17 & 18.08.2017. GGC - Piplai, CRS done on 09.03.2021. Piplai - Lalsot, CRS done on 03.03.2023. Lalsot-Deedwana CRS done on 09.03.2024	1996-97	950.00	94.65	Lalsot-Deedwana = 100%
2	RATLAM - DUNGARPUR via BANSWARA Bankability study report sent to RB in Feb-2020 with ROR +12.73%.	2011-12	4500.00	191.80	Cost sharing with Govt. of Rajasthan. Execution of work kept in abeyance by RB vide letter dt. 24.03.2019. RB has de-frezed the project vide letter dt. 22.05.23. Tender awarded.
3	AJMER(NASIRABAD) - KOTA (JALINDRI)	2013-14	822.00	145.00	Execution of work kept in abeyance by RB on 24.09.2019.
4	AJMER (AI)- SAWAI MADHOPUR (SWM) via TONK Bankability study report sent to RB in July-2021 with ROR +7.85%.	2015-16	2215.27	165.00	Cost sharing with Govt. of Rajasthan. Execution of work kept in abeyance by RB.
5	TARANGA HILL- ABU ROAD (ABR) VIA AMBAJI	2017-18	2798.16	116.65	Land acquisition is in progress. Tender for 0 to 61 Km is awarded on 01.12.2023. Tender for 61-116.65 Kms invited & will be opened on 03.04.2024. (TDC: 31.12.26)
6	DEDICATED TEST TRACK FOR RDSO (i) GUDHA - THATHANA MITHRI NL (PHASE-I) (ii) RDSO DEDICATED TEST TRACK (PHASE-II) (iii) RDSO DEDICATED TEST TRACK (PHASE-III)	2018-19	353.48	22.80	75% (TDC: 31.03.24) 19.8 km Track completed
7	NATHDWARA - NATHDWARA TOWN NEW LINE	2018-19	166.33	9.60	Land acquisition is in progress (TDC: 30.03.26)
8	NIMACH-BADI SADRI NEW LINE	2017-18	495.18	48.35	Land acquisition is in progress. Tender awarded. (TDC: 30.09.26)
9	PUSHKAR -MERTA NEW LINE	2023-24	799.64	51.35	DPR sanctioned on 13.02.2024.
10	RAS -MERTA CITY NEW LINE (Incl. MTD bypass)	2023-24	947.00	55.90	DPR sanctioned on 13.02.2024.
11	RINGAS- KHATUSHYAM JI NL ( 17.49 KM)	2023-24	254.06	17.49	DPR sanctioned on 05.03.2024.
<b>B. GAUGE CONVERSION</b>					
12	DEVGARH-NATHDWARA (82.54 KM) GC PART OF MARWAR - MAVLI	2017-18	968.92	82.54	DPR sanctioned by RB on 24.01.23. Land acquisition is in progress. Tender awarded. (TDC: 31.12.26)
<b>C. DOUBLING</b>					
13	PHULERA - DEGANA DOUBLING (i) DNA-BOW : COMMISSIONED ON 27.10.2021. (ii) BOW-KMNC : COMMISSIONED ON 15.03.2022. (iii) GVNR-FL : COMMISSIONED ON 27.12.2023. (iv) KMNC-NAC : COMMISSIONED ON 21.02.2024	2015-16	701.81	108.00	(i) NAC-GVMR= 96% (TDC=April-24)
14	BHATINDA - DEGANA DOUBLING	2020-21	4800.00	480.00	Bhatinda-Degana Doubling (480 Km) work is kept in abeyance by RB vide letter dt. 26.10.2021.
15	SAWAI MADHOPUR -BYEPASS LINE	2020-21	239.54	13.54	DPR sanctioned by RB on 09.12.22. Land acquisition is in progress. Tender awarded. (TDC: 31.12.25)
16	REWARI-KATHUWAS DOUBLING	2022-23	352.41	27.73	DPR sanctioned by RB on 03.02.23. Tender invited. (TDC: 30.11.25)
17	CHURU-RATANGARH DOUBLING	2022-23	422.60	42.81	DPR sanctioned by RB on 03.02.23. Tender awarded. (TDC: 30.06.25)
18	BHIWANI - DHOB BAHALI DOUBLING	2022-23	471.06	42.30	DPR sanctioned by RB on 27.02.23. Tender awarded. (TDC: 30.06.25)
19	MANHERU - BHIWANI KHERA DOUBLING	2022-23	413.09	31.50	DPR sanctioned by RB on 10.04.23. Tender awarded. (TDC: 31.12.25)
20	KATHUWAS - NARNAUL DOUBLING	2022-23	313.31	24.12	DPR sanctioned by RB on 10.04.23. Tender awarded. (TDC: 30.06.25)
21	CHURU - SADULPUR DOUBLING	2023-24	468.64	57.82	DPR sanctioned by RB on 29.01.24.
22	JAIPUR - SAWAI MADHOPUR DOUBLING	2023-24	1203.89	131.27	DPR sanctioned by RB in 19.02.2024.
23	AJMER - CHANDERIYA DOUBLING	2023-24	1634.79	178.28	DPR sanctioned by RB in 19.02.2024.
24	LUNI - BHILDI DOUBLING	2023-24	3085.59	271.97	DPR sanctioned by RB in 19.02.2024.
<b>D. CAPITAL INVESTMENT (JV awaited with GOR)</b>					
25	KISHANGARH - PARBATSAR NEW LINE	2016-17	900.00	45.0	MoU with Rajasthan Government is yet to be signed for creation of SPV.
26	JAISALMER - BHABAR NEW LINE	2016-17	5000.00	339.0	MoU with Rajasthan Government is yet to be signed for creation of SPV.

LEGEND	
1. NEW LINE ( Sanctioned & in progress )	-----
2. NEW LINE ( Sanctioned & Completed )	-----
3. GC Works ( Sanctioned & in progress )	-----
4. GC Works ( Sanctioned & Completed )	-----
5. DOUBLING ( Sanctioned & in progress )	-----
6. DOUBLING ( Sanctioned & Completed )	-----
7. Kept in abeyance works :-	
NL Works	-----
GC Works	-----
DL Works	-----
8. CAPITAL INVESTMENT ( Sanctioned )	-----
