

**SUMMARY OF SANCTIONED WORKS OVER NWR**

AS ON 01.04.2021


S.N.	P.H.	SCOPE (KM)	TARGET 21-22 (KM)	TARGET 22-23 (KM)	BALANCE AS ON 01.04.2023 (KM)	KEPT IN ABEYANCE
1.	NL	748.74	0	32.51	716.23	557.85
2.	GC	323.00	171.0	0	152.00	152.00
3.	DL	849.22	175.0	80.0	594.22	271.97
TOTAL		1920.96	346.0	112.51	1462.45	981.82

**LIST OF SANCTIONED WORKS OVER NWR**

Sr. No.	NAME OF WORK	SALIENT FEATURES			PHYSICAL PROGRESS & TDC
		YEAR OF SANCTION	COST IN Cr.	LENGTH IN KM	
<b>I.0 NEW LINE</b>					
1.1	DAUSA (DO) - GANGAPUR CITY (GGC) DO-Deedwana CRS done on 17.08.17 & 18.08.17. GGC - PIPLAI CRS done on 09.03.21.	1996-97	780.98	94.65	90% Piplai - Deedwana TDC:30.06.2022.
1.2	RATLAM(RTM)-DUNGARPUR(DNRP) Via-BANSWARA(BNSW) Bankability study report sent to RB in Feb'20.	2011-12	2417.24	188.85	6.25% Execution of work kept in abeyance by RB.
1.3	AJMER(AII)-KOTA NASIRABAD(NSD)-JALINDRI CCEA sanction is yet to be obtained by Rly Bd.	2013-14	822.00	145.00	Execution of work kept in abeyance by RB.
1.4	PUSHKAR (POHT) - MERTA (MTD) CCEA sanction is yet to be obtained by Rly Bd.	2013-14	323.00	59.00	Execution of work kept in abeyance by RB.
1.5	AJMER (AII)- SAWAI MADHOPUR (SWM) VIA TONK	2015-16	873.71	165.00	Execution of work kept in abeyance by RB.
1.6	TARANGA HILL- ABU ROAD (ABR) VIA AMBAJI	2017-18	1695.72	89.38	Revised DPR Sent to RB on 22.11.2021
1.7	DEDICATED TEST TRACK FOR RDSO				
	(i) GUDHA - THATHANA MITHRI NL (PHASE-I)	2018-19	353.48	25.00	Work in progress.
	(ii) RDSO DEDICATED TEST TRACK (PHASE-II)	2019-20	466.42	34.00	DPR sanctioned on 18.11.2021
1.8	NATHDWARA - NATHDWARA TOWN NEW LINE	2018-19	166.33	10.00	FLS is in progress.
<b>2.0 GAUGE CONVERSION WORKS</b>					
2.1	MAVLI Jn (MVJ) - BARI SADRI (BI) Section closed on 01.11.2016 for GC works.	2013-14	295.02	82.01	96% TDC 15.01.2022
2.2	JAIPUR-SIKAR & SIKAR-CHURU SECTION COMMISSIONED (i) Sikar - Loharu (122.13 Km) : 01.09.2015. (ii) Sikar - Fatehpur Shekhawati (47.06 Km): 20.06.17. (iii) Fatehpur Shekhawati - Churu (43.40 Km): 09.12.17 (iv) Sikar-Palsana (27 Km) : 27.01.2019. (v) Palsana-Ringas (23 Km) : 27.01.2019. (vi) Jaipur - Ringas (60 Km) : 21.10.2019.	2008-09	658.07	320.04	100% (PROJECT ALREADY COMMISSIONED) Status of 05 new X-ing Stations :- Rashidpur Khori & Kayamsar stations commissioned.Work in progress at Baori Thikaria (Jan-22), Goriyan (Mar-22) & Chhota Gudha(Apr-22)
2.3	HIMMATNAGAR (HMT) - UDAIPUR (UDZ) (i).RGQ-HMT, CRS DONE ON 26.05.19. (ii).UDZ-KRCD, CRS DONE ON 15.01.2020. (iii).RGQ - DNRP, CRS Done on 19-21.12.2020.	2008-09	829.74	208.08	92% DNRP-JYM 21.01.2022 JYM-KRCD 28.02.2022
2.4	MARWAR (MJ) - MAVLI (MVJ) (NATHDWARA)	2017-18	1597.12	152.00	Project kept in abeyance by RB.
<b>3.0 DOUBLING</b>					
3.1	PHULERA (FL) - DEGANA (DNA) (i) DNA-BOW : COMMISSIONED ON 27.10.2021.	2015-16	611.53	108.00	67% BOW-KMNC 28.02.2022 KMNC-NAC 31.03.2022 NAC-FL 31.10.2022
3.2	DEGANA (DNA)-RAIKA BAGH (RKB)	2018-19	808.85	145.00	62% DNA-MTD 24.12.2021 MTD-KXG 31.01.2022 KXG-PPR 28.02.2022 PPR-RKB 30.11.2022
3.3	JAIPUR - SAWAI MADHOPUR DOUBLING	2019-20	1053.24	131.27	Revised DPR sent to RB on 15.11.2021
3.4	BHATINDA - BHILDI VIA HISAR, RATANGARH DEGANA, LUNI, SAMDARI ( EXCL. DEGANA -RAI KA BAGH )	2020-21	7522.00	752.00	Work is Kept in abeyance For LN-BLDI (271.97 KM). DPR of BTI-DNA sent to RB on 04.06.21.
3.5	AJMER-CHITTORGARH DOUBLING	2020-21	1860.00	186.00	DPR sent to RB on 14.06.2021
3.6	SAWAI MADHOPUR -BYPASS LINE	2020-21	252.00	6.98	DPR under preparation

**NORTH WESTERN RAILWAY  
SYSTEM MAP  
SANCTIONED WORKS ( IN PROGRESS )**

AS ON 15.12.2021

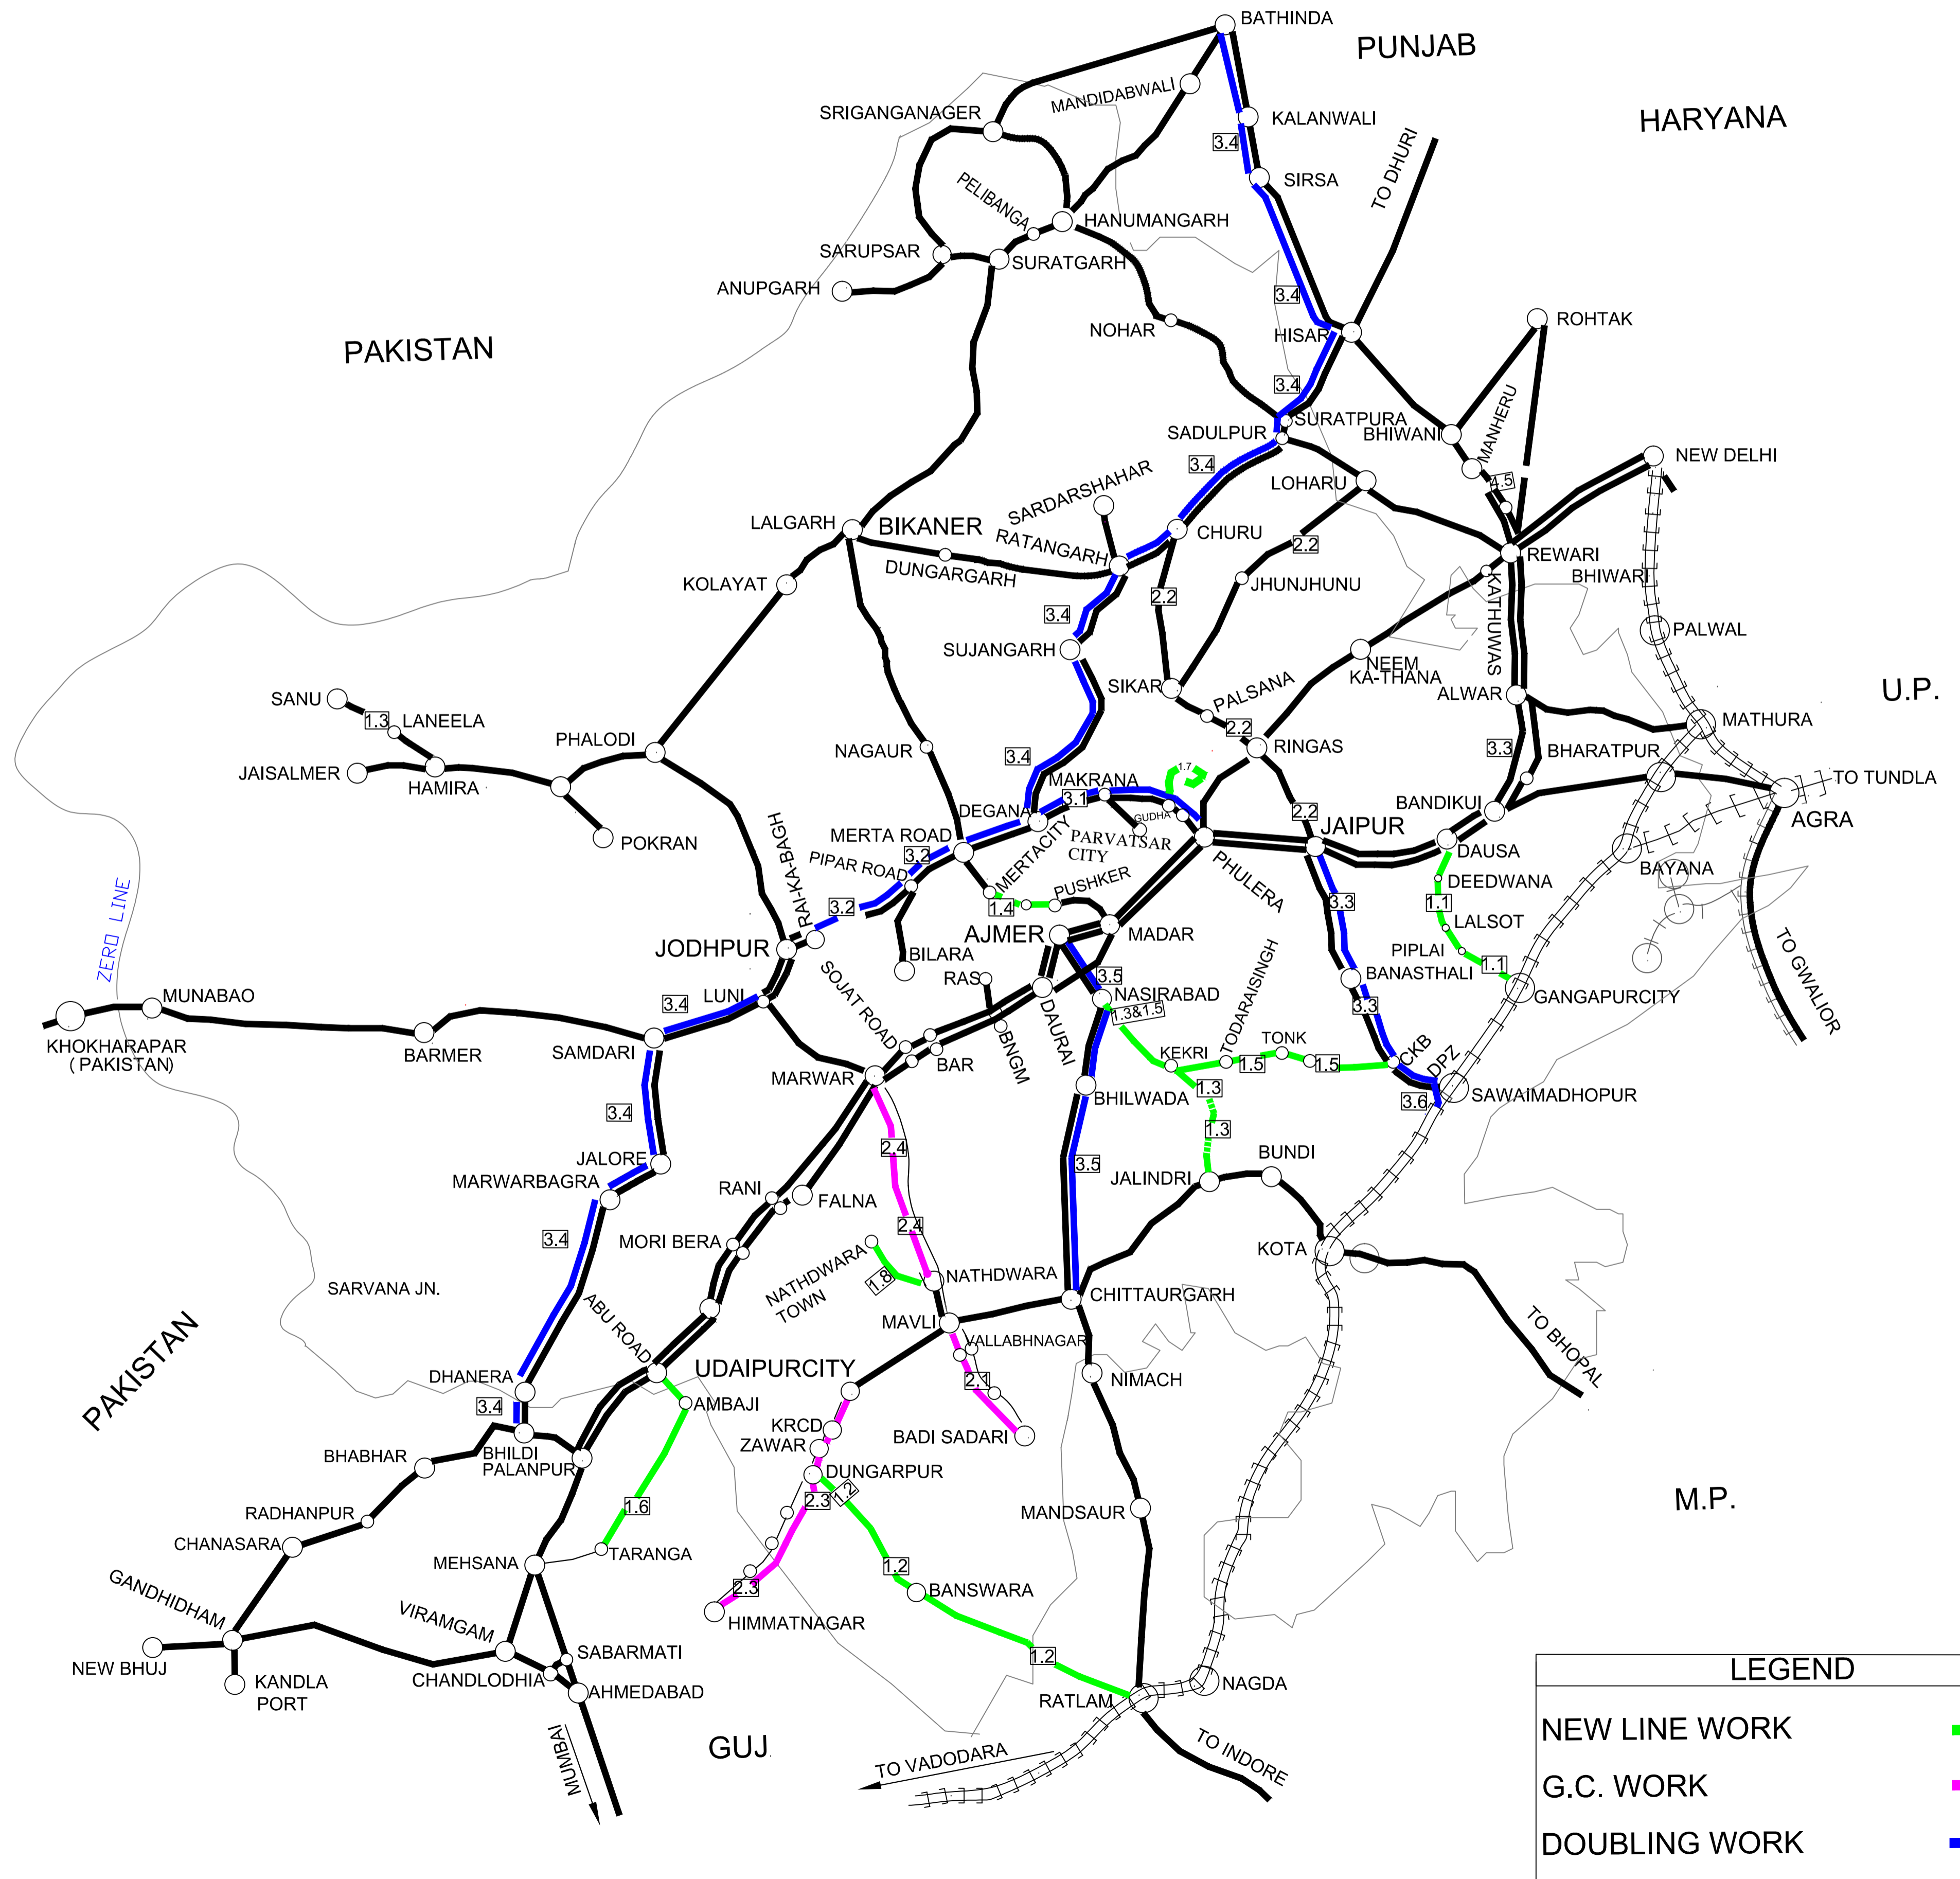

LEGEND	
NEW LINE WORK	<span style="color: green;">—</span>
G.C. WORK	<span style="color: magenta;">—</span>
DOUBLING WORK	<span style="color: blue;">—</span>
