

**SUMMARY OF SANCTIONED WORKS OVER NWR**

AS ON 01.04.2022

S.N.	P.H.	SCOPE (KM)	TARGET 22-23 (KM)	BALANCE AS ON 01.04.2023 (KM)	KEPT IN ABEYANCE
1.	NL	748.74	34.51	714.23	557.85
2.	GC	189.00	37.00	152.00	152.00
3.	DL	721.22	127.00	594.22	271.97
<b>TOTAL</b>		<b>1658.96</b>	<b>198.51</b>	<b>1460.45</b>	<b>981.82</b>

**LIST OF SANCTIONED WORKS OVER NWR**


Sr. No.	NAME OF WORK	SALIENT FEATURES		PHYSICAL PROGRESS & TDC	
		YEAR OF SANCTION	COST IN Cr.		LENGTH IN KM
<b>1.0 NEW LINE</b>					
1.1	DAUSA (DO) - GANGAPUR CITY (GGC) DO-Deedwana CRS done on 17.08.17 & 18.08.17. GGC - PIPLAI CRS done on 09.03.21.	1996-97	950.00	94.65	82% Piplai - Deedwana TDC: 31.12.2022.
1.2	RATLAM(RTM)-DUNGARPUR(DNRP) Via-BANSWARA(BNSW) Bankability study report sent to RB in Feb'20.	2011-12	4500.00	188.85	6.25% Execution of work kept in abeyance by RB.
1.3	AJMER(AII)-KOTA NASIRABAD(NSD)-JALINDRI CCEA sanction is yet to be obtained by Rly Bd.	2013-14	822.00	145.00	Execution of work kept in abeyance by RB.
1.4	PUSHKAR (POHT) - MERTA (MTD) CCEA sanction is yet to be obtained by Rly Bd.	2013-14	323.00	59.00	Execution of work kept in abeyance by RB.
1.5	AJMER (AII)- SAWAI MADHOPUR (SWM) VIA TONK	2015-16	2215.27	165.00	Execution of work kept in abeyance by RB.
1.6	TARANGA HILL- ABU ROAD (ABR) VIA AMBAJI	2017-18	2928.29	89.38	Revised DPR Sent to RB on 22.11.2021
1.7	DEDICATED TEST TRACK FOR RDSO (i) GUDHA - THATHANA MITHRI NL (PHASE-I) (ii) RDSO DEDICATED TEST TRACK (PHASE-II)	2018-19 2019-20	353.48 466.42	25.00 34.00	Work in progress. DPR sanctioned on 18.11.2021
1.8	NATHDWARA - NATHDWARA TOWN NEW LINE	2018-19	166.33	10.00	FLS is in progress.
<b>2.0 GAUGE CONVERSION WORKS</b>					
2.1	MAVLI Jn (MVJ) - BARI SADRI (BI) Section closed on 01.11.2016 for GC works.	2013-14	480.00	82.01	100% Section commissioned on 11.02.2022
2.2	JAIPUR-SIKAR & SIKAR-CHURU SECTION COMMISSIONED (i) Sikar - Loharu (122.13 Km) : 01.09.2015. (ii) Sikar - Fatehpur Shekhawati (47.06 Km): 20.06.17. (iii) Fatehpur Shekhawati - Churu (43.40 Km): 09.12.17 (iv) Sikar-Palsana (27 Km) : 27.01.2019. (v) Palsana-Ringas (23 Km) : 27.01.2019. (vi) Jaipur - Ringas (60 Km) : 21.10.2019.	2008-09	658.07	320.04	100% (PROJECT ALREADY COMMISSIONED) Status of 05 new X-ing Stations :- Rashidpur Khori, Kayamsar & Baori Thikaria stations commissioned. Work in progress at Goriyan (Apr-22) & Chhota Gudha (Jun-22)
2.3	HIMMATNAGAR (HMT) - UDAIPUR (UDZ) (i).RGQ-HMT, CRS done on 26.05.19. (ii).UDZ-KRCD, CRS done on 15.01.2020. (iii).RGQ - DNRP, CRS done on 19-21.12.2020. (iv) DNRP-JYM, CRS done on 05 & 06.03.2022.	2008-09	1648.18	208.08	95% JYM-KRCD 31.05.2022
2.4	MARWAR (MJ) - MAVLI (MVJ) (NATHDWARA)	2017-18	2654.03	152.00	Project kept in abeyance by RB.
<b>3.0 DOUBLING</b>					
3.1	PHULERA (FL) - DEGANA (DNA) (i) DNA-BOW : COMMISSIONED ON 27.10.2021. (ii) BOW-KMNC : COMMISSIONED ON 15.03.2022.	2015-16	701.81	108.00	72% KMNC-NAC 31.07.2022 NAC-FL 31.01.2023
3.2	DEGANA (DNA)-RAIKA BAGH (RKB) (i) DNA-MTD : COMMISSIONED ON 24.12.2021. (ii) MTD-KXG : COMMISSIONED ON 25.02.2022.	2018-19	808.85	145.00	77% KXG-PPR 31.05.2022 PPR-RKB 31.12.2022
3.3	JAIPUR - SAWAI MADHOPUR DOUBLING	2019-20	1046.30	131.27	Revised DPR sent to RB on 15.11.2021.
3.4	BHATINDA - BHILDI VIA HISAR, RATANGARH DEGANA, LUNI, SAMDARI ( EXCL. DEGANA -RAI KA BAGH )	2020-21	7522.00	752.00	Work is Kept in abeyance For LN-BLDI (271.97 KM), DPR of BTI-DNA sent to RB on 04.06.21.
3.5	AJMER-CHITTORGARH DOUBLING	2020-21	1860.00	186.00	DPR sent to RB on 14.06.2021
3.6	SAWAI MADHOPUR -BYEPASS LINE	2020-21	252.00	6.98	DPR under preparation

**NORTH WESTERN RAILWAY**

**SYSTEM MAP**

**SANCTIONED WORKS ( IN PROGRESS )**

AS ON 13.05.2022

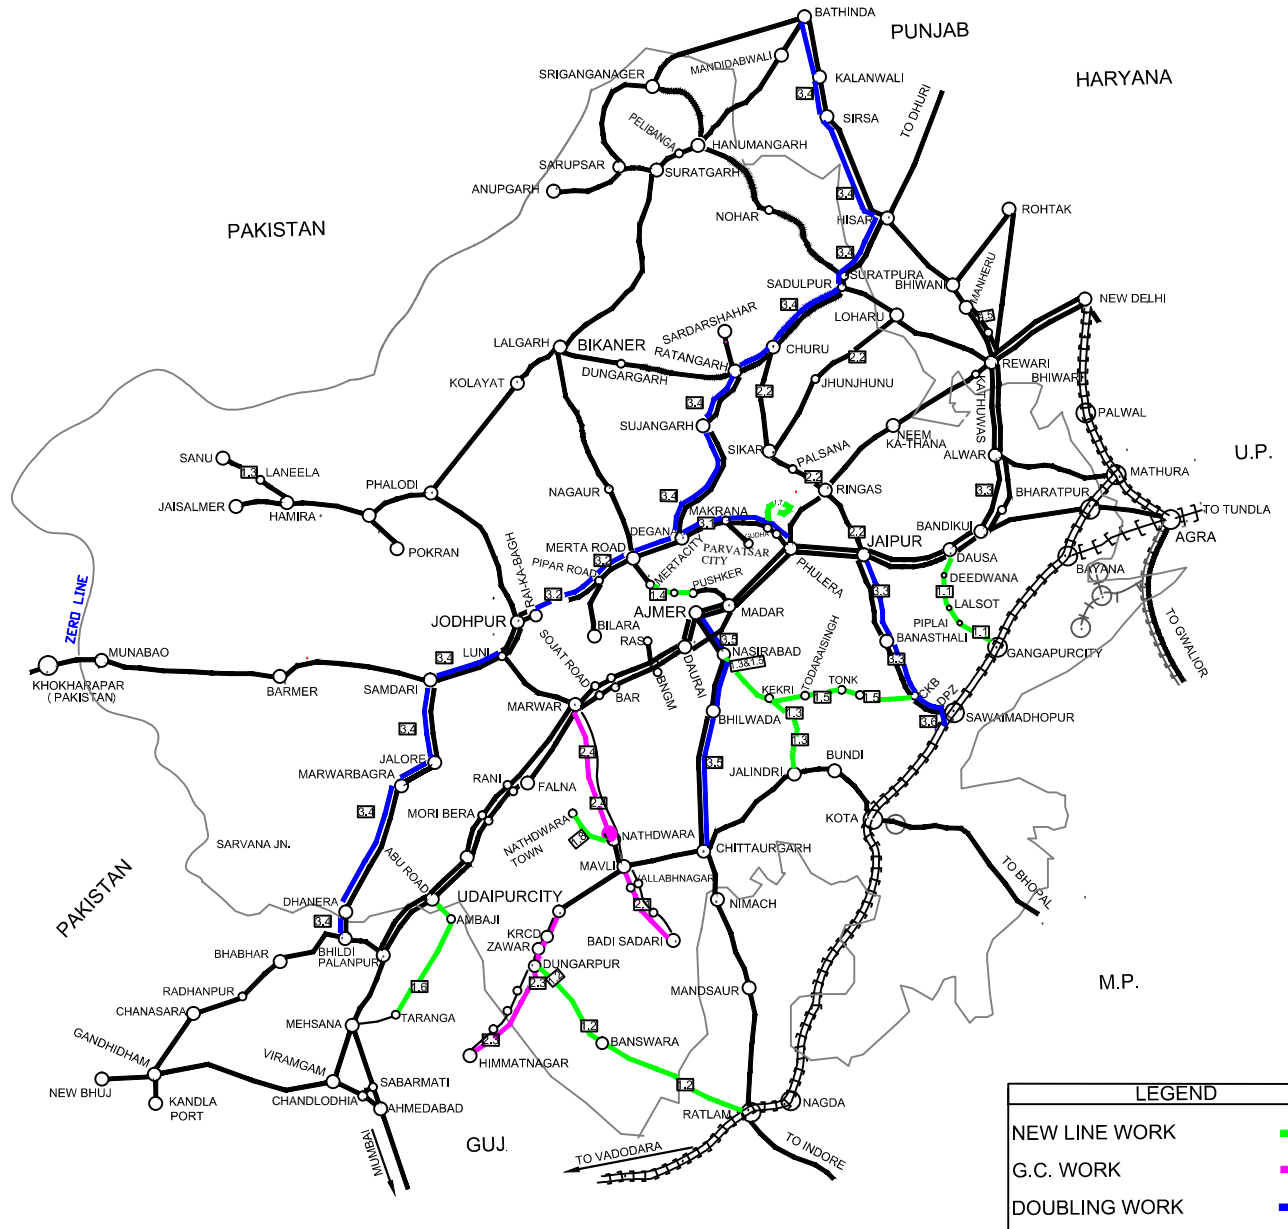

LEGEND	
NEW LINE WORK	<span style="color: green;">—</span>
G.C. WORK	<span style="color: pink;">—</span>
DOUBLING WORK	<span style="color: blue;">—</span>
