


**NORTH WESTERN RAILWAY
SYSTEM MAP
SANCTIONED NL/GC/DL WORKS (IN PROGRESS)**



(2023-24)

LIST OF SANCTIONED WORKS OVER NWR

Sr. No.	NAME OF WORK	SALIENT FEATURES			PHYSICAL PROGRESS & TDC
		YEAR OF SANCTION	COST IN Cr.	LENGTH IN KM	
A. NEW LINE					
1	DAUSA - GANGAPUR CITY NEW LINE Dausa-Deedwana, CRS done on 17 & 18.08.2017. GGC - Piplai, CRS done on 09.03.2021. Piplai - Lalsot, CRS done on 03.03.2023.	1996-97	950.00	94.65	Lalsot-Deedwana = 80% (TDC: Sept-23)
2	RATLAM - DUNGARPUR via BANSWARA Bankability study report sent to RB in Feb-2020 with ROR (+)2.73%.	2011-12	4500.00	188.85	Cost sharing with Govt. of Rajasthan Execution of work kept in abeyance by RB vide letter dt. 24.09.2019. RB has de-frozen the project vide letter dt. 22.05.2023.
3	AJMER(NASIRABAD) - KOTA (JALINDRI)	2013-14	822.00	145.00	Execution of work kept in abeyance by RB on 24.09.2019.
4	AJMER (All)- SAWAI MADHOPUR (SWM) via TONK Bankability study report sent to RB in July-2021 with ROR (-)7.85%.	2015-16	2215.27	165.00	Cost sharing with Govt. of Rajasthan. Execution of work kept in abeyance by RB.
5	TARANGA HILL- ABU ROAD (ABR) VIA AMBAJI	2017-18	2798.16	116.65	Land acquisition is in progress. (TDC: 31.12.26)
6	DEDICATED TEST TRACK FOR RDSO (i) GUDHA - THATHANA MITHRI NL (PHASE-I) Twisted track (4.5 Km) commissioned on 30.12.20. (ii) RDSO DEDICATED TEST TRACK (PHASE-II)	2018-19	353.48	22.80	62% (TDC: 31.12.23)
7	NATHDWARA - NATHDWARA TOWN NEW LINE	2018-19	166.33	9.60	Land acquisition is in progress. (TDC: 31.12.25)
8	NIMACH-BADI SADRI NEW LINE	2017-18	495.18	48.35	Land acquisition is in progress. (TDC: 30.06.25)
B. GAUGE CONVERSION					
9	DEVGARH-NATHDWARA (82.54 KM) GC PART OF MARWAR - MAVLI	2017-18	968.92	82.54	DPR sanctioned by RB on 24.01.23, Land acquisition is in progress. Tender awarded. (TDC: 31.01.27)
C. DOUBLING					
10	PHULERA - DEGANA DOUBLING (i) DNA-BOW : COMMISSIONED ON 27.10.2021. (ii) BOW-KMNC : COMMISSIONED ON 15.03.2022.	2015-16	701.81	108.00	(i) KMNC-NAC = 65% (TDC= Jan-24) (ii) NAC-GVMR= 64% (TDC= Feb-24) (iii) GVMR-FL = 73% (TDC= Oct-23)
11	BHATINDA - DEGANA DOUBLING	2020-21	4800.00	480.00	Bhatinda-Degana Doubling (480 Km) work is kept in abeyance by RB vide letter dt. 26.10.2021.
12	SAWAI MADHOPUR -BYEPASS LINE	2020-21	239.54	13.54	DPR sanctioned by RB on 09.12.22. Land acquisition is in progress. Tender invited. (TDC= 31.12.25)
13	REWARI-KATHUWAS DOUBLING	2022-23	352.41	27.73	DPR sanctioned by RB on 03.02.23. Tender invited. (TDC: 30.06.25)
14	CHURU-RATANGARH DOUBLING	2022-23	422.60	42.81	DPR sanctioned by RB on 03.02.23. Tender awarded. (TDC: 30.06.25)
15	BHIWANI - DHOB BAHALI DOUBLING	2022-23	471.06	42.30	DPR sanctioned by RB on 27.02.23. Tender work in process. (TDC: 30.06.25)
16	MANHERU - BHIWANI KHERA DOUBLING	2022-23	413.09	31.50	DPR sanctioned by RB on 10.04.23. Tender work in process. (TDC: 30.06.25)
17	KATHUWAS - NARNAUL DOUBLING	2022-23	313.31	24.12	DPR sanctioned by RB on 10.04.23. Tender invited. (TDC: 30.06.25)
D. CAPITAL INVESTMENT (JV awaited with GOR)					
18	KISHANGARH - PARBATSAR NEW LINE	2016-17	900.00	45.0	MoU with Rajasthan Government is yet to be signed for creation of SPV.
19	JAISALMER - BHABAR NEW LINE	2016-17	5000.00	339.0	MoU with Rajasthan Government is yet to be signed for creation of SPV.

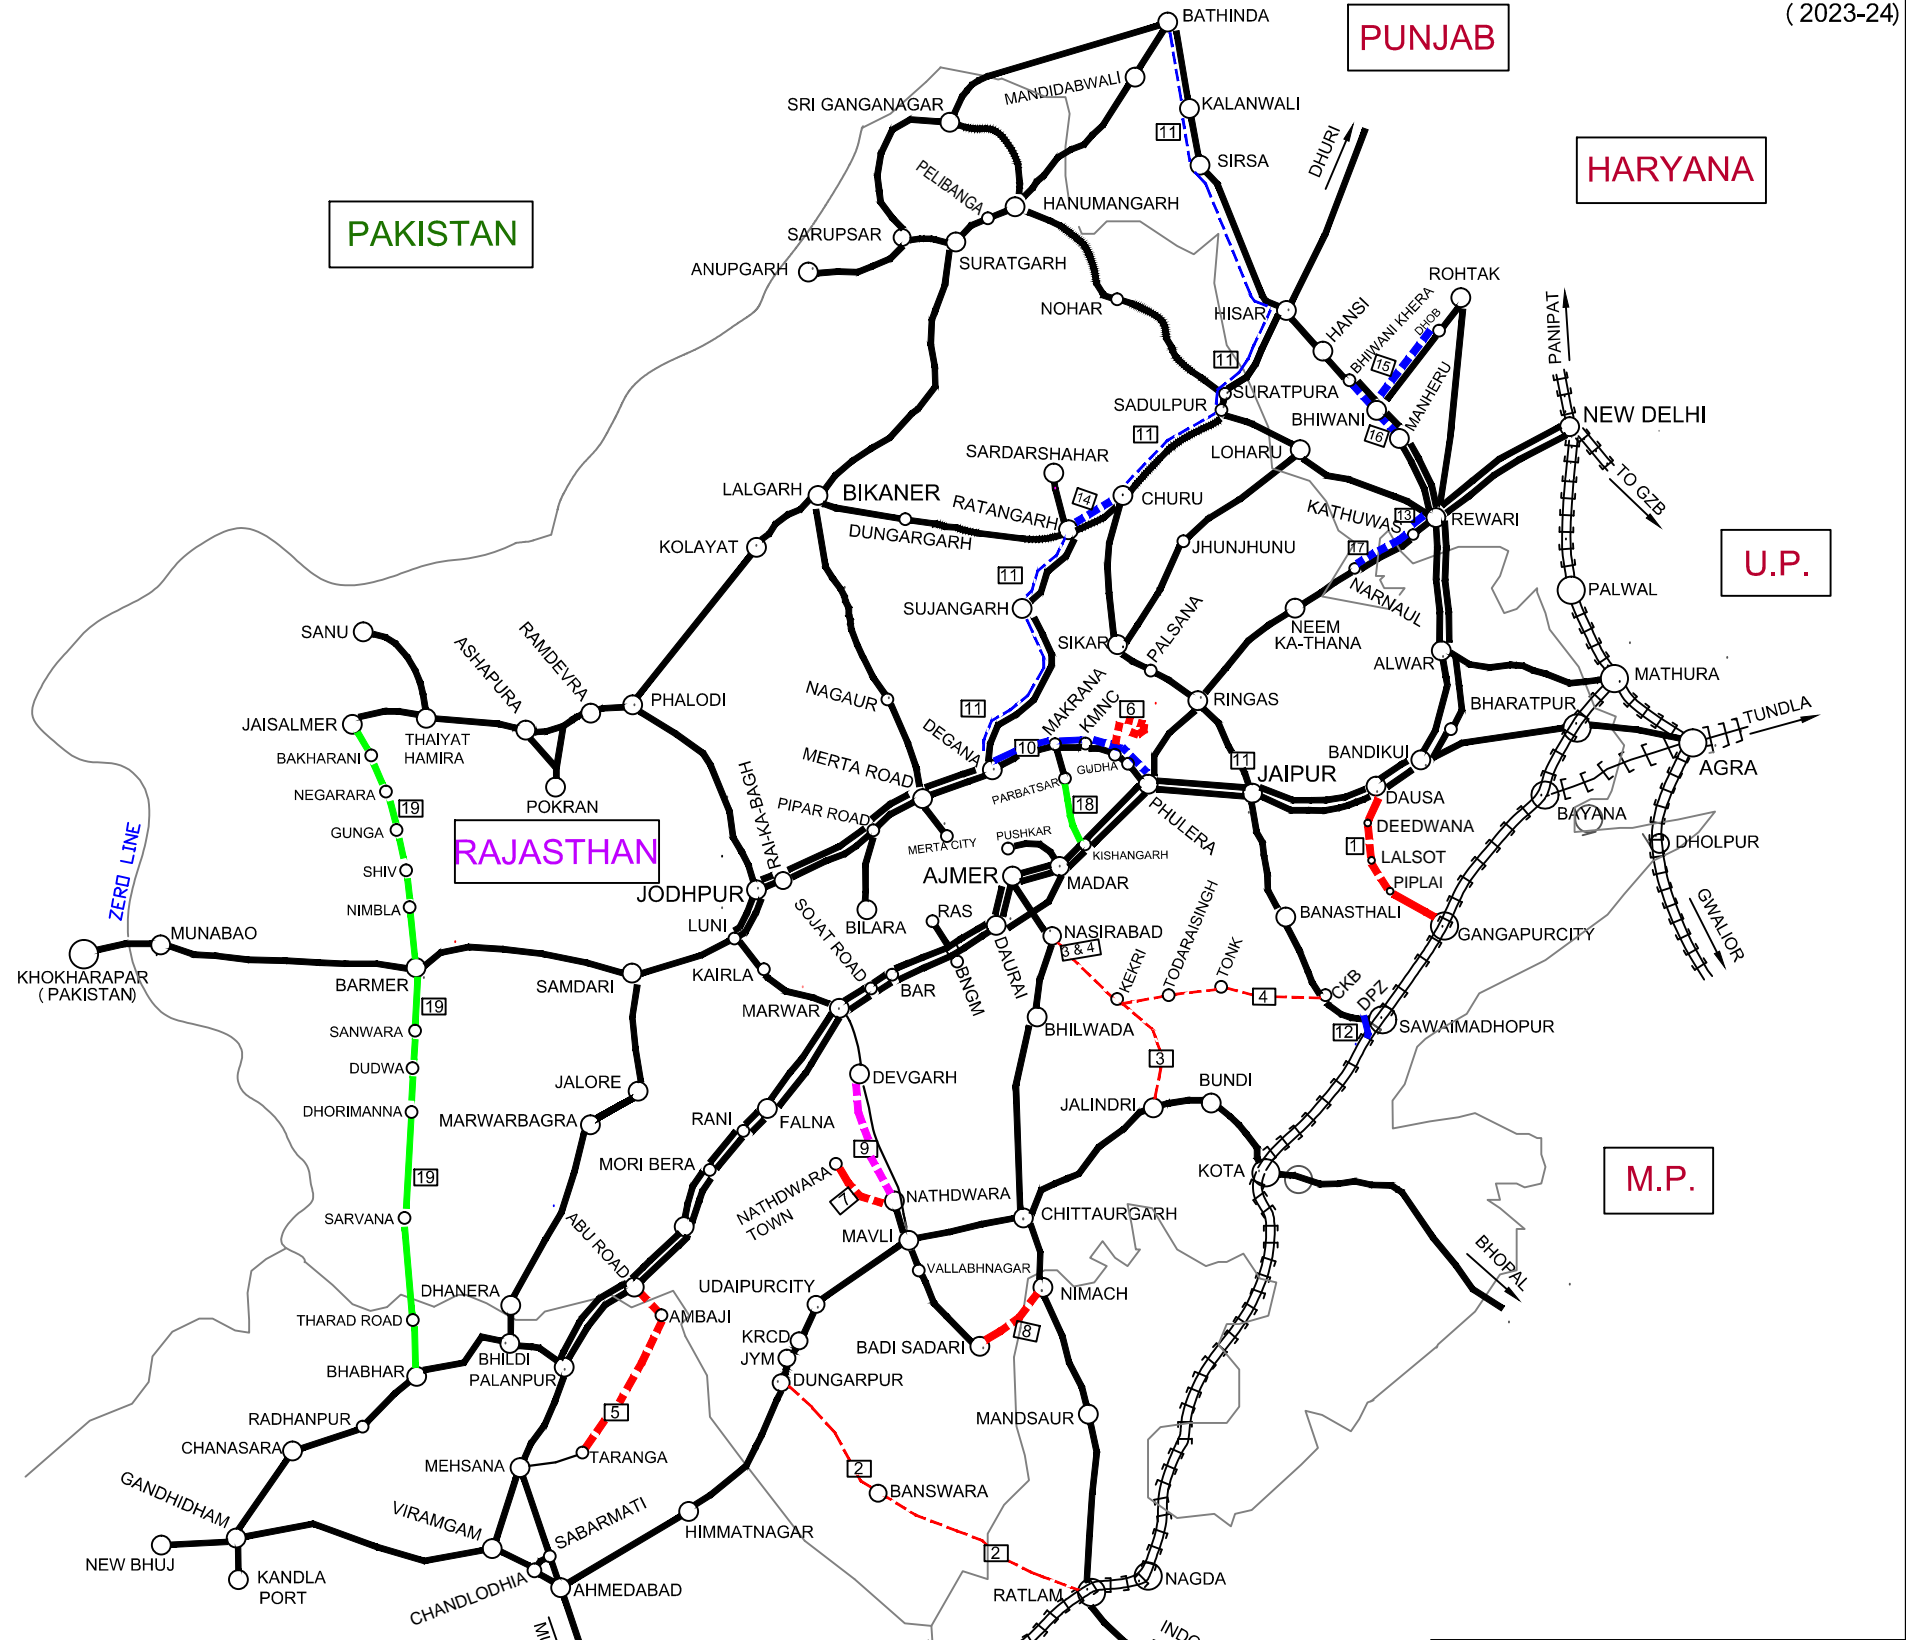

LEGEND

1. NEW LINE (Sanctioned & in progress)	---
2. NEW LINE (Sanctioned & Completed)	—
3. GC Works (Sanctioned & in progress)	---
4. GC Works (Sanctioned & Completed)	—
5. DOUBLING (Sanctioned & in progress)	---
6. DOUBLING (Sanctioned & Completed)	—
7. Kept in abeyance works :-	
NL Works	---
GC Works	---
DL Works	---
8. CAPITAL INVESTMENT (Sanctioned)	—
