NORTH WESTERN RAILWAY

GENERAL MANAGER'S ANNUAL REPORT 2023-24

G L O S S A R Y OF T E R M S

Capital-at-charge (Para 308 of F-I)

Capital-at-Charge represents the Central Government's investment in the Railways by way of loan capital and value of the assets created there from.

Capital Outlay (Statistical Manual-Glossary of terms-(item no. 5)

Expenditure of capital nature incurred during the period with the object of increasing concrete assets of a material character.

Working Expenses (Para 308 of F-I)

True expenses in an accounting period whether or not actually disbursed which includes ordinary working Expenses, Appropriation to Pension Fund and the contribution made to the Depreciation Reserve Fund.

Gross Earnings (Para 308 of F-I)

The true or accrued earnings in an accounting period whether actually realized or not.

Gross Receipts (Para 308 of F-I)

The true or accrued gross earnings in an accounting period whether actually realized or not plus Suspense earnings. That means Earnings actually realized during an accounting period.

Net Earnings (Para 308 of F-I)

The difference between the gross earning and the working expenses excluding suspense but including appropriation to DRF and Pension fund.

Net Revenue (Statistical Manual-Glossary of terms-(item no. 38)

The difference between gross earnings and working expenses after the payment of dividend to General Revenue, payment to worked lines and other net miscellaneous expenditure.

Operating Ratio (Statistical Manual-Glossary of terms-(item no. 42)

The ratio of working expenses (excluding suspense but including Appropriation to Pension fund and the contribution made to the Depreciation Reserve Fund) to Gross earnings.

Route Kilometers (Statistical Manual-Glossary of terms-(item no.54) the distance of each gauge owned by a railway including its worked lines treated as a single line.

Wagon turn round (Statistical Manual-Appendix-I-Significance of important Statistics-

(Item no. (P).

This is equal to the effective wagon holdings divided by Wagon loadings, where the effective Wagon holdings represents Wagon owned by a railway less the daily average number of Wagons out of service modified by the daily Wagon balance. Wagon loadings in this context include (1) average daily loading, (2) average number of Wagons received loaded from other railways daily, (3) average daily number of Wagons carrying military traffic and (4) daily average number of Wagons into which goods are transshipped from Wagons of the same gauge. In short, Wagon turn round is interval of time (in days) between two successive loadings of a wagon.

Density (Statistical Manual-Glossary of terms-(item no. 10)

The volume of traffic moving between any two points on the Railway system. It is expressed in terms of passenger kilometers or net tone kilometers and train kilometers per running track kilometer or route kilometer.

Track Kilometers (Statistical Manual-Glossary of terms-(item no. 70) The distance of each gauge owned by a railway including its worked lines treated as a single line and the extra distance due to double, triple, etc. tracks as also the length of siding etc.

Gross tone Kilometers (Statistical Manual-Glossary of terms-(item no. 24)

Unit of measure of work which corresponds to the movement, over a distance of one kilometer, of one tonne, including/excluding the weight of the motive unit.

Net tone kilometers (Statistical Manual-Glossary of terms-(item no. 39)

Unit of measure of goods traffic which represents the transport of one tone of goods *(including the weight of any packing, but excluding the weight of vehicle use for transport)* over a distance of one kilometer.

Passengers originating (Statistical Manual-Glossary of terms-(item no. 45). The number of passenger booked from each gauge of railway.

Passengers carried (Statistical Manual-Glossary of terms-(item no. 43)

The number of passenger originating on each railway as well as the number of passengers received from other railways and also those crossing the railway.

Passenger kilometers (Statistical Manual-Glossary of terms - (item no. 44) Unit of measure of passenger traffic corresponding to the conveyance of a passenger over a distance of one kilometer.

Revenue earning traffic (Statistical Manual-Glossary of terms-(item no. 49) the traffic conveyed by rail and for which commercial tariffs are applied i.e. for transportation of which the railway is paid by either consigner or the consignee.

Suspense (Statistical Manual-Glossary of terms-(item no. 64)

Difference between true earnings/ working expenses in an accounting period whether or not actually realized/disbursed and earnings/working expenses actually realized/disbursed during an accounting period.

* * * * * * *

KEY STATISTICS FOR THE YEAR 2023-2024

DESCRIPTION	Units		2022-23	2023-24
1. FINANCIAL POSITION :				
Capital-at-charge	Rs. in Crores	...	13524.88	18723.34
Gross Earnings	Rs. in Crores	...	10351.80	11200.27
Total Working Expenses (Excl. Suspense)	Rs. in Crores	...	11431.48	12930.15
Net Revenue Receipts	Rs. in Crores	...	-1062.53	-1665.40
Operating Ratio	% age	...	110.43	115.44
2. PASSENGER STATISTICS :				
No. of Passengers Originating	Millions	...	140.54	166.44
No. of Passenger Carried on the system	Millions	...	190.45	224.50
Passenger Kilometers	Millions	--	38095	44413.73
Earnings from passengers carried	Rs. in Crores	...	2764.92	3258.71
Average earnings per passenger per kilometer	Paise	...	72.57	73.37
Average lead per passenger	KMs	...	200.02	197.83
3. FREIGHT STATISTICS :				
Tonnes Originating (Rev.+Non-Rev)	Millions	---	32.75	29.46
Tonnes carried on the system	Millions	...	115.19	116.26
NTKMs of freight traffic carried	Millions	...	54256	52538
Earnings from Goods carried	Rs. in Crores	...	6805.61	6995.74
Average rate per tonne per kilometer	Paise	...	125.43	133.15
Average lead of tonnes carried	KMs.	...	471	452
4. TRAIN STATISTICS :				
Goods train kilometers include. deptt	Thousands	--	21421	18541
Passenger train kilometers	Thousands	...	35889	41553
Total train kilometers	Thousands	---	57310	60094
Gross earnings per train kilometer	Rupees	...	1806.28	1863.79
GTKMs of Passenger traffic	Thousands	...	39245939	45183456
GTKMs of Goods traffic	Thousands	...	80475067	75113040
5AVG. NO. OF COACHING TRAINS RUN (p/d):				
(a) Mail/Express trains	Nos.	BG	404	422
		MG	0	0
(b) Ordinary Passenger trains	Nos.	BG	148	200
		MG	02	02
6. STATIONS AND ROUTE KILOMETERS :				
No. of stations as on 31st March	Nos.	...	589	599
Route Kilometers as on 31st march	KMs.	BG	5538.823	5560.813
		MG	151.650	151.650
		Total	**5705.473**	**5712.463**
Total Track Kilometers	KMs.	BG	7899.073	7969.194
		MG	162.771	162.771
		Total	**8061.844**	**8131.965**
7. STAFF STATISTICS :				
No. of staff as on 31st March			45344	50512
Total cost of staff for the year	Rs. In crores		7292.41	7945.71
Average annual cost per employee	Rupees		1608243	1573035

CONTENTS

Chapter No		Page No.
	Glossary	2-4
	Key Statistics -2023-24	5
1	General Review- 2023-24	7-12
2	Accounts Department	13-32
3	Transportation Operating	33-45
4	Transportation Commercial	46-57
5	Engineering Department	58-171
6	Survey & Construction	172-173
7	Mechanical Department	174-194
8	Electrical Department	195-202
9	Signal & Telecommunication	203-222
10	Stores Department	223-229
11	Medical Department	230-259
12	Personnel Department	260-277
13	Safety Department	278-292
14	Security Department	293-294
15	Raj Bhasha	295-296
16	Vigilance Department	297-302
17	General Department	303-310
18	NWR System Map 2023-24	311

*****

Chapter-1

General Review- 2023-24

1.1 General :

North Western Railway with its headquarters office at Jaipur is spread over 4 states consist of 4 Divisions became operational w.e.f 1st October'2002. It was carved out of two Divisions each from Northern Railway and Western Railway. The formation of this zone along with five other new zones was first approved by Railway Board on 16th September'1996 and foundation stone for this zone was laid on 17th October'1996 by the then Prime Minister Shri H. D. Deve Gowda at K. P. Singh Stadium, Jaipur.

The impetus for formation of New Zone came with the Government of India notification No. 97/E&R/700/1/Notification dated 14.06.2002 wherein it was decided that North Western Railway with its jurisdiction over existing Jaipur and Ajmer divisions of Western Railway and Jodhpur and Bikaner divisions of Northern Railway was to come into effect from 01.10.2002.

North Western Railway consists of four divisions i.e. Jaipur, Ajmer, Jodhpur and Bikaner. This Zonal Railway covers four states viz. Rajasthan, Haryana, Punjab and Gujarat. North Western Railway territory is up to Munabao station of Pakistan border.

This is the Twenty one edition of GM's Annual Narrative Report on NWR being published after the successful publication of first Narrative Report in 2003-04.

1.2 Brief outlines of Divisions :

Jaipur Division - This Division was formed after merging part of BB&CI, Jaipur State Railways and Rajputana Malwa Railway. This division serves the states of Rajasthan, and Haryana. This division consist of cities which include tourist destination such as Jaipur and Alwar Being a predominately passenger earning division, it deals primarily with cross traffic consisting of fertilizer, cement, oil, salt, food grain, oil seeds traffic. The following major commodities are loaded from this division: -

1. Mustard oil is loaded from Alwar Goods Shed.
2. **Container loading** is done from this division in bulk by-
    1. ICD Kanakpura (KKU), Khatuwas (CMLK) station.
    2. Adani Logistics ICD from Mandawaria station near Kishangarh station. (ALIK)
    3. M/s Sanjvik terminals Bawal (MSTB)
    4. Kribhco Infrastructure, Pali (KIIP)
    5. NMG from M/s Sanjvik terminals, Bawal.
    6. Inward POL at Asalpur Jobner.
    7. Gati Shakti Multi model Cargo Terminal New Rewari.
    8. Dhanakya

Ajmer Division - This Division is spread over the states of Rajasthan and Gujarat. This division is prominent on the religious and tourist map of India as it witnesses large amount of passenger traffic to Ajmer Sharief, Pushkar-having the only Bharhma temple in the world, Jain Temples of Dilwara at Mount Abu and Ranakpur Temples .It is predominantly cement loading division as many cement plants of Rajasthan are located within the jurisdiction of this division. Rock phosphate and Single Super Phosphate (SSP) powder are also loaded from Udaipur area. Container loading is also being done from this division from Daurai station. The following major commodities are loaded from this division: -

1. Cement and Clinkar.
    - JK Laxmi Cement, Siding served by Banas.
    - 'Ultratech Cement, Nathdwara Siding served by Keshavganj.
    - 'Shri Cement Siding served by Bangurgram, Shree Mega Power siding, Ras,Udaipur cement works,khemli, Ambuja Cement ltd, Rabriyawas.

2. Fertilizer-
    - Rana Pratap Nagar station.
    - Debari station.
    - DET station.
    - Hamir Garh
3. Container-
    - Daurai station.
    - Khemli station.
    - Nathdwara
    - CONCOR PFT New swaroop ganj

Jodhpur Division - This division was set up in the year 1882 and it consists primarily of semi-urban districts of Rajasthan. It covers area of Jodhpur, Pali Marwar, Nagaur, Jalore, Barmer, Jaisalmer- (Sand Dunes) etc. It also covers certain districts of Gujarat state. This division also serves certain sensitive areas of Rajasthan such as Jaisalmer, Barmer touching the Pakistan border and Pokran, The main commodities loaded on this division are limestone and salt. Container loading is being done by 'CONCOR 'from Bhagat Ki Kothi, Gotan and Khariya Khangar stations of this division. The following major commodities are loaded from this division:-

1. **Lime stone-**
    - Sonu,badwasi,Parvatsar city
2. **Gypsum -**Thaiyat Hamira
3. **Salt**-
    - Nawa City
4. Container-
    - Bhagat Ki Kothi.
    - Kharia Khangar.
    - Deshnoke station.
    - White Cement- Gotan,
    - M/sHasti Petro Chemicals & Shiping Ltd , Hanwant

Bikaner Division - This Division was established in 1924 and it serves the states of Rajasthan, Punjab and Haryana. There is a unique Karni Mata temple at Deshnoke Station which is known the world over for the presence of kabas (Rats) that roam freely within the temple precincts. This division has an equal amount of passenger and goods traffic. The main outward goods traffic of this

division is food grain, china clay and gypsum. The following major commodities are loaded from this division:-

1. **Food grain**-
   - Raman
   - Mandi dabwali.
   - Kalanwali.
   - Sirsa
   - Bhattu
   - Kanasar.
   - Lal Garh, Anup Garh, Sri Vijay Nagar, Surat Garh
2. **POL & Pet Coke**
   - HMEL siding
3. Container-
   - Satrod, HMEL Siding
4. Gypsum
   - Anupgarh Suratgarh
5. Mustard Oil
   - Banwali
6. Stone
   - Zerpur Pali, Bhiwani City, Manheru

1.3 Railway Kilometrage :

Route Kilometers and Track Kilometers -The route kilometers and track kilometers of the North Western Railway as on 31.03.2024 is as under :-

	Broad Gauge	**Meter Gauge**	**Total**
Route Kilometers			
Electrified	5101.944	----	5101.944
Non-Electrified	458.869	151.650	610.519
Total	**5560.813**	**151.650**	**5712.463**
Track Kilometers	7969.194	162.771	8131.965

1.4 General Highlights during the year-2023-24 :

⇒ The gross earnings and the total working expenses *(Excl. suspense)* for the year amounted to Rs. 11200.27 Crs.and Rs 12930.15 Crs, respectively.

⇒ The Number of passengers originating was 166.44 Millions and number of passengers carried was 224.50 Million during the year 2023-24.

⇒ The goods Tonnes originating traffic was 29.46 Million tonnes and goods traffic Tonnes carried was 116.26 Million tons during the year 2023-24.

⇒ The passenger kilometers and freight tones kilometers in respect of traffic carried were 44414 and 52538 Million respectively during the year.

⇒ Operating ratio remained at 115.44 during the year 2023-24.

⇒ During the year, apportioned Passenger earnings remained at Rs 3258.71 crores registered a Increase 17.86% as compared to previous year (2764.92 crores) but Decrease of target (3386.28 crores) by -3.77%.

⇒ Apportioned Freight earnings remained at Rs.7024.17 crores registered a Increase of 2.68 % as compared to previous year (6840.71 crores) Freight earnings were Increase of target 6853.87 crores by 2.48%.

⇒ OCH earnings remained at Rs 298.10 crores, showing Increase of 20.55% as compared to previous year (247.29 crores) OCH earnings were Increase of target 283.80 crores by 5.04%.

⇒ Sundry earnings remained at Rs 619.28 crores showing a Increase of 24.13% as compared to previous year (498.88crores) Sundry earnings were Increase of target (609.98 crores) by 1.53%.

⇒ Total apportioned earnings for 2023-24 (including suspense) remained at Rs.11223.50 crores as against 10372.95 crores up to end of march'2023, showing a increase of 8.20%, However, the target of apportioned earnings 11142.93 crores , Total apportioned earnings were Increase of target by 0.72%

1.5.4 Principle Statistics of working :

		Units	***2023-24***
1.	No. of Passengers Originating	Millions	166.44
2.	No. of Passenger Carried on the system	Millions	224.50
3.	Passenger Kilometers	Millions	44413.73
4.	Earnings from passengers carried	Rs. in Crores	3258.71
5.	Avg. earnings per passenger per km.	Paisa	73.37
6.	Average length of passenger journey	KMs	197.83
7.	Tonnes Originating	Millions	29.46
8.	Tonnes carried on the system	Millions	116.26
9.	NTKMs of freight traffic carried	Millions	52538
10.	Earnings from Goods carried	Rs. in Crores	6995.74
11.	Average rate per tonne per kilometer	paisa	133.15
12.	Average lead of tonnes carried	KMs.	452

Chapter-2
ACCOUNTS - DEPARTMENT
FINANCIAL RESULTS FOR THE YEAR 2023-24

2.1 FINANCIAL RESULTS OF WORKING :- The financial results of working of North Western Railway for the year 2023-24 is as under :-

DESCRIPTION	*(Rs. in crores)*	
	2022-23	**2023-24**
(i) Capital-at-charge	13524.88	18723.34
(ii) Capital Outlay	2322.81	5197.95
(iii) Gross Earnings	10351.80	11200.27
(iv) Suspense	21.15	23.23
(v) Gross Traffic Receipts (iii+iv)	**10372.95**	**11223.50**
(vi) Ordinary Working Expenses	9225.48	10510.15
(vii) Appropriation to Depreciation Reserve Fund	24.00	27.00
(viii) Appropriation to Pension Fund	2182.00	2393.00
(ix) Total Ordinary Working Expenses *(Excl. Suspense)* (vi to viii)	**11431.48**	**12930.15**
(x) Suspense	4.10	-41.24
(xi) Total Ordinary Working Expenses (Incl. Suspense) (ix+x)	**11435.58**	**12888.91**
(xii) Net Traffic Receipts (v-xi)	-1062.53	-1665.40
(xiii) Net Misc. Receipts	0.10	0.01
(xiv) Net Revenue Receipts (xii +xiii)	1062.63	-1665.39
(xv) Operating Ratio (ix/iii*100)	110.43	115.44
%age of Net Revenue Receipts to Capital-at-charge		
(xvi) Dividend to General Revenue	0.00	0.00
(xvii) Surplus(+)/Shortfall(-) (xiv-xvi)	-1062.53	-1665.39
(xviii) %age of gain/loss to Capital-at-charge (xvii/i*100)	-7.86	-8.86

2.2 GROSS TRAFFIC RECEIPTS :- The details of Gross Traffic Receipts of 'North Western Railway for the year 2023-24 are as below :-

Heads	Earnings	
	(Rs. in crores)	
	2022-23	**2023-24**
Passenger Earnings	2764.92	3258.71
Other Coaching Earnings	247.29	298.10
Goods Earnings	6840.71	7024.17
Sundry Earnings	498.88	619.29
Total Gross Earnings	**10351.80**	**11200.27**
Suspense	21.15	23.23
Gross Traffic Receipts	**10372.95**	**11223.50**

2.3 DEMAND WISE WORKING EXPENDITURE :- The details of demand wise working expenditure for the year 2023-24 are as under :-

Description	*(Demand No.)*	*(Rs. in crores)*	
		2022-23	*2023-24*
1- General superintendnce and services	03	482.55	506.59
2- Repairs and maintenance - Permanent Way and Works	04	768.83	901.30
3- Repairs and maintenance - Motive Power	05	152.65	167.17
4- Repairs and maintenance - Carriage and Wagons	06	699.72	927.64
5- Repairs and maintenance - Plants and Equipments	07	395.86	479.14
6- Operating Expenses - Rolling stock and Equipments	08	745.48	855.48
7- Operating Expenses - Traffic	09	1803.99	2301.34
8- Operating Expenses - Fuel	10	3269.27	3273.44
9- Staff welfare and amenities	11	405.61	489.64
10- Miscellanous working expenses	12	272.92	340.59
11- Provident fund, Pension and other retirement benefits	13	228.60	267.82
12- Total Ordinry working expenses		**9225.48**	**10510.15**
13- Appropriation to DRF and Pension Fund	14	2206.00	2420.00
14- Working expenses *(incl. App. to DRF & Pension Fund but excl. Suspense)*		**11431.48**	**12930.15**
15- Suspense		4.10	-41.24
16- Total Working Expenses *(including Suspense)*		**11435.58**	**12888.91**

2.4 EARNINGS FROM PASSENGERS CARRIED - NON-SUBURBAN :-

The number of passengers carried and earnings thereof under the different classes for the year 2023-24 is as under :-

Heads	No. of passengers carried (In thousands)		Earnings (Rs. in Crores)	
	2022-23	2023-24	2022-23	2023-24
Executive Class	116.63	195.41	9.74	18.89
Ist AC	304.58	404.47	35.76	47.44
IInd AC	3471.9	3988.92	246.35	285.19
IIIrd AC	18822.57	22309.13	965.97	1169.87
ACC	2648.70	3537.37	98.77	146.98
Ist Class :-				
Mail/Exp	0.29	0.71	0.02	0.03
Season tickets	0.00	0.29	0.00	0.00
Ordinary	0.30	0.00	0.00	0.01
Total	**0.59**	**1.00**	**0.02**	**0.04**
Sleeper Class :-				
Mail/Exp	33930.39	33715.94	672.61	686.24
Ordinary	162.66	523.99	0.05	12.06
Total	**34093.05**	**34239.93**	**672.66**	**698.30**
IInd Class :-				
Mail/Exp	106497.16	124956.53	715.17	863.44
Season tickets	0.00	0.00	0.00	0.00
Ordinary	24494.86	34864.91	20.48	28.56
Total	**130992.02**	**159821.44**	**735.65**	**892.00**
Grand Total all classes	**190450.04**	**224497.67**	**2764.92**	**3258.71**

2.5 EARNINGS FROM GOODS CARRIED :- The earnings from goods traffic under important commodities for the year 2023-24 is as under :-

Description	Tonnes carried on system		Earnings	
Revenue Earning Traffic :-	*(In millions)*		*(Rs. in Crores)*	
	2022-23	2023-24	2022-23	2023-24
1. Products of agriculture	6.73	3.41	436.34	249.30
2. Animals & products of animals	0.00	0.00	0.00	0.00
3. Product of mines :-				
(i) Coal	26.02	28.07	1265.10	1169.54
(ii) Lime stone and dolomite	3.69	3.17	460.94	419.61
(iii) Gypsum	0.39	0.22	31.94	17.13
(iv) Others	1.62	1.2	54.04	43.82
(v) Total	**31.72**	**32.66**	**1812.02**	**1650.10**
4. Mineral oils	4.11	5.88	427.32	636.37
5. Product of forests	0.11	0.21	6.51	12.90
6. Manufactures :-				
(i) Sugar	0.39	0.00	30.65	0.00
(ii) Salt	3.84	3.66	222.62	226.28
(iii) Edible Oils	0.57	0.87	34.73	55.44
(iv) Cement	15.93	14.93	963.16	908.76
(v) Iron & Steel	2.90	3.89	143.69	195.41
(vi) Others	0.53	0.38	19.53	13.46
(vii) Total	**24.16**	**23.73**	**1414.38**	**1399.35**
7. Other Miscelleneous :-				
(i) Fertilizers	8.86	7.99	780.78	703.74
(ii) Domestic containers	6.61	7.23	296.65	364.10
(iii) ISO containers	29.75	32.72	1499.53	1868.23
(iv) Others	2.92	2.04	132.08	111.65
(iv) Total	**48.14**	**49.98**	**2709.04**	**3047.72**
8. Total Revenue Earning Traffic	**114.97**	**115.87**	**6805.61**	**6995.74**

Statistical Information

ANALYSIS OF COACHING EARNINGS

PARTICULARS OF EARNINGS		2022-23	2023-24
I. PASSENGER TRAFFIC :-		*(Amount in Rs.)*	*(Amount in Rs.)*
(a) Season Tickets	…	100982219	136943608
(b) Ordinary *(Full fares, reduced fares and other concession fares)*	…	27548221325	32450192515
Total Passenger Earnings	…	**27649203544**	**32587136123**
II. OTHER COACHING TRAFFIC :-			
(a) Special trains and Resereved Carriages	…	586527355	711131388
(b) Luggage including millitary	…	16923590	24157293
(c) Parcels	…	452107977	741964559
(d) Misc. Coaching Traffic	…	0	0
(e) Transport of Post office Mails	…	31114424	7289842
(f) Misc. Coaching Receipts	…	1386267086	1496479525
TOTAL OTHER COACHING EARNINGS	…	**2472940432**	**2981022607**
Less- Refund from Other Coaching Earnings		0	0
TOTAL	…	**2472940432**	**2981022607**
TOTAL COACHING EARNINGS*(I+II)(including refund)*		**30122143976**	**35568158730**

STATEMENT OF COACHING EARNINGS

PARTICULARS OF EARNINGS		2022-2023 No. of Pass. Carried on system	2022-2023 Earnings (In Rupees)	2023-2024 No. of Pass. Carried on system	2023-2024 Earnings (In Rupees)
Executive Class	…	116634	97386379	195413	188890630
AC First Class	…	304577	357633512	404470	474394255
AC 2 Tier Sleeper	…	3471902	2463457554	3988919	2851863503
AC 3 Tier Sleeper	…	18822570	9659683213	22309127	11698699786
AC Chair Car	…	2648697	987735927	3537373	1469792699
First Class :-					
(a) Mail & Exp.	…	291	217567	715	285103
(b) Season tickets	…	0	0	0	0
(c) Ordinary	…	301	67072	291	139444
(d) Total first class	…	**592**	**284639**	**1006**	**424547**
Sleeper Class :-					
(a) Mail & Exp.	…	34087962	6726027109	34237873	6982895978
(b) Ordinary	…	5090	475509	2057	185261
(c) Total sleeper class	…	**34093052**	**6726502618**	**34239930**	**6983081239**
2nd Class :-					
(a) Mail & Exp.	…	106497164	7151739262	124956531	8634436269
(b) Season tickets	…	0	0	0	0
(c) Ordinary	…	24494861	204780440	34864897	285553195
(d) Total second class	…	**130992025**	**7356519702**	**159821428**	**8919989464**
Reservation Charges	…				
Total Passenger Traffic :-					
(a) Season tickets	…	0	0	0	0
(b) Ordinary	…	190450049	27649203544	224497666	32587136123
(c) Grand Total	…	**190450049**	**27649203544**	**224497666**	**32587136123**
Luggage, Military Luggage & Parcels	…		469031567		766121852
Special Trains & Msc. (Incl. Horses & Dogs)	…		1972794441		2207610913
Post Office (Extra Service)	…		31114424		7289842
TOTAL COACHING TRAFFIC *(Incld Refund)*	…		**30122143976**		**35568158730**
Deduct Refunds	…		0		0
TOTAL COACHING TRAFFIC *(Excld Refund)*	…		**30122143976**		**35568158730**

Analysis of Passenger Traffic for the Year 2022-2023 as Compared with 2023-2024

2023-24

Particulars	No. of Passenger Carried on System				Earnings in Rupees			
	Full Fares	Concessional Fare	Season Ticket	Total	Full Fares	Redueced fare	Season Ticket	Total
Executive Class	177859	17554	0	195413	176347084	12543546	0	188890630
A C First Class	332686	71784	0	404470	404005797	70388458	0	474394255
A C 2 Tier Sleeper	3077380	911539	0	3988919	2477929341	373934162	0	2851863503
A C 3 Tier Sleeper	19487324	2821803	0	22309127	10651527305	1047172481	0	11698699786
A C Chair Car	3271014	266359	0	3537373	1386798367	82994332	0	1469792699
First Class :-								
(a) Mail & Exp.	713	2	0	715	284971	132	0	285103
(c) Ordianary	291	0	0	291	139444	0	0	139444
(d) Total first class	1004	2	0	1006	424415	132	0	424547
Sleeper Class :-								
(a) Mail & Exp.	30411955	3825918	0	34237873	6390229631	592666347	0	6982895978
(b) Ordianary	1947	110	0	2057	176972	8289	0	185261
(c) Total Sleeper class	30413902	3826028	0	34239930	6390406603	592674636	0	6983081239
2nd Class :-								
(a) Mail & Exp.	124435458	521073	0	124956531	8602212764	32223505	0	8634436269
(c) Ordianary	3678167	380	31186350	34864897	123751257	10985	161790953	285553195
(d) Total second class	128113625	521453	31186350	159821428	8725964021	32234490	161790953	8919989464
Total Passenger Traffic	**184874794**	**8436522**	**31186350**	**224497666**	**30213402933**	**2211942237**	**161790953**	**32587136123**

2022-23

Particulars	No. of Passenger Carried on System				Earnings in Rupees			
	Full Fares	Concessional Fare	Season Ticket	Total	Full Fares	Redueced fare	Season Ticket	Total
Executive Class	99938	16696	0	116634	84577838	12808541	0	97386379
A C First Class	246255	58322	0	304577	301181053	56452459	0	357633512
A C 2 Tier Sleeper	2663136	808766	0	3471902	2134992171	328465383	0	2463457554
A C 3 Tier Sleeper	16451998	2370572	0	18822570	8771930891	887752322	0	9659683213
A C Chair Car	2407478	241219	0	2648697	910423409	77312518	0	987735927
First Class :-								
(a) Mail & Exp.	291	0	0	291	217567	0	0	217567
(c) Ordianary	151	0	150	301	65772	0	1300	67072
(d) Total first class	442	0	150	592	283339	0	1300	284639
Sleeper Class :-								
(a) Mail & Exp.	30221633	3866329	0	34087962	6141733725	584293384	0	6726027109
(b) Ordianary	4846	244	0	5090	455414	20095	0	475509
(c) Total Sleeper class	30226479	3866573	0	34093052	6142189139	584313479	0	6726502618
2nd Class :-								
(a) Mail & Exp.	105951666	545498	0	106497164	7114278146	37461116	0	7151739262
(c) Ordianary	1171956	5	23322900	24494861	88374907	167	116405366	204780440
(d) Total second class	107123622	545503	23322900	130992025	7202653053	37461283	116405366	7356519702
Total Passenger Traffic	**159219348**	**7907651**	**23323050**	**190450049**	**25548230893**	**1984565985**	**116406666**	**27649203544**

REVENUE EARNING TRAFFIC (STATEMENT NO 7C) ON CARRIED BASIS.UPTO END OF MARCH'2023COMPARED TO END OF MARCH'2024
Broad Gauge

Description	Tonnes carried (In thousands)		NTKMs (In thousands)		Earnings (In thousands)	
	2022-23	2023-24	2022-23	2023-24	2022-23	2023-24
I. REVENUE EARNING TRAFFIC :						
1. Product of Agriculture :-						
(i) Foodgrain	6627	3383	3705675	1949078	4317122	2485622
(ii) Oil Seeds	1	1	222	210	201	379
(iii) Cotton Raw (pressed+unpressed)	2	0	1747	0	965	0
(iv) Fruits and vegetable fresh	40	15	27808	7293	18868	4877
(v) Fodder	1	1	26	500	46	369
(vi) Oil Cakes	11	0	6444	0	6353	0
(vi) Others	50	7	16158	1315	19812	1735
Total	**6732**	**3407**	**3758080**	**1958396**	**4363367**	**2492982**
2. Animals and product of animals	0	0	0	0	0	0
3. Prodect of mines :-						
(i) Coal :-						
(a) Coal booked from collieries -						
(i) For thermal power houses	3951	4058	611288	611557	1072460	1130022
(ii) For cement factories	0	0	0	0	0	0
(iii) For other users	12	143	3212	6223	5326	17596
(iv) Total coal from collieries	**3963**	**4201**	**614500**	**617780**	**1077786**	**1147618**
(b) Coal booked from other points -						
(i) For thermal power houses	19402	21085	5779071	4763271	9916004	8579337
(ii) For cement factories	15	12	3801	3923	8782	7536
(iii) For other users	2643	2773	897332	1068046	1648446	1960917
(iv) Total coal booked from other points	**22060**	**23870**	**6680204**	**5835240**	**11573232**	**10547790**
(c) Total Coal Excluding containers-						
(i) For thermal power houses	23353	25143	6390359	5374828	10988464	9709359
(ii) For cement factories	15	12	3801	3923	8782	7536
(iii) For other users	2655	2916	900544	1074269	1653772	1978513
(iv) Total Coal (excl. containers)	**26023**	**28071**	**7294704**	**6453020**	**12651018**	**11695408**
(ii) Marbles & Stones :						
(a) Lime stones and dolomite	3689	3165	3185508	2740921	4609421	4196088
(b) Marble and other stones	1473	1073	174987	95203	332532	209829
Total Marbles & Stones	**5162**	**4238**	**3360495**	**2836124**	**4941953**	**4405917**
(iii) Gypsum	393	224	207460	101796	319325	171337
(iv) Mettallic Ores :						
(a) Manganese ore	0	0	0	0	0	0
(b) Iron ore	20	0	12061	0	22675	0
(v) Others Misc. products	128	126	87222	86900	185227	228332
Total product of mines	**31726**	**32659**	**10961942**	**9477840**	**18120198**	**16500994**
4. Mineral Oils :-						
(a) Diesel Oil	1887	2594	1053124	1433781	1887840	2609899
(b) Kerosene Oil	11	38	1392	11403	2871	21360
(c) Petrol Oil	1061	1227	600530	662228	1052995	1264049
(d) Petroleum Gases	637	822	456156	591702	822613	1064862
(e) Other Mineral Oils	509	1199	285357	750786	506873	1403569
Total Mineral Oil	**4105**	**5880**	**2396559**	**3449900**	**4273192**	**6363739**
5. Product of forests	**106**	**208**	**89678**	**170422**	**65082**	**128972**
6. Manufactures :-						
(a) Suger including gur shakkar	394	0	296848	27	306561	28
(b) Salt	3839	3662	2537560	2462295	2226153	2262838

REVENUE EARNING TRAFFIC (STATEMENT NO 7C) ON CARRIED BASIS.UPTO END OF MARCH'2023COMPARED TO END OF MARCH'2024

Broad Gauge

Description	Tonnes carried (In thousands)		NTKMs (In thousands)		Earnings (In thousands)	
	2022-23	2023-24	2022-23	2023-24	2022-23	2023-24
(c) Edible Oils	572	870	308616	532340	347361	554381
(d) Cement	15930	14926	7210224	6377734	9631579	9087589
(e) Iron & steel	2897	3892	1067351	1499071	1436860	1954087
(f) Other Manufectures	529	385	188104	105888	195330	134624
Total Manufactures	**24161**	**23735**	**11608703**	**10977355**	**14143844**	**13993547**
7. Othre Miscellaneous :-						
(a) Fertilizers	8860	7985	5974813	5075708	7807818	7037359
(b) Domestic container	6607	7234	3076251	3377232	2966480	3641013
(c) ISO containers *handled by CONCOR*	29759	32718	15265149	17157792	14995342	18682314
(d) Railway Matarial In GSW	943	806	120545	122218	436311	387268
(d) Other Misc.	1975	1231	953963	702655	884449	729182
Total Miscelleneous	**48144**	**49974**	**25390721**	**26435605**	**27090400**	**30477136**
8. Total Revenue Traffic	**114974**	**115863**	**54205683**	**52469518**	**68056083**	**69957370**
II. NON-REVENUE TRAFFIC :						
1. Coal for Railways	0	0	0	0	0	0
2. Diesel for Railways	0	0	0	0	0	0
3. Rly. General stores & Materials	218	402	47514	69268	0	0
4.Carriedfor other Govt.Rly Ect.	0	0	0	0	0	0
Total Non-Revenue Traffic	**218**	**402**	**47514**	**69268**	**0**	**0**
Total Revenue & Non-Revenue Traffic	**115192**	**116265**	**54253197**	**52538786**	**68056083**	**69957370**

REVENUE EARNING LOADING (Statement 7-A) ON ORIGINATING BASIS
Upto end of March'2023 Compared with the Upto end of March'2024


Commodities	***No. of wagons*** *(in Unit)*		***Tonnes Originating*** *(in Thousand)*		***Tonnes Kms*** *(in Thousand)*		***Earnings (Excl.GST)*** *(in Thousand)*		***Average Lead*** *(in Kms)*		***All Gauge Avg. Rate per Tonne Kms*** *(in Rupees)*	
	2022-23	**2023-24**	**2022-23**	**2023-24**	**2022-23**	**2023-24**	**2022-23**	**2023-24**	**2022-23**	**2023-24**	**2022-23**	**2023-24**
Coal for Steel Plants	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0.00*	*0.00*
Coal for Washeries	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0.00*	*0.00*
Coal for Thermal Power Houses	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0.00*	*0.00*
Coal for Public Use	*1834*	*1421*	*130*	*100*	*63440*	*31240*	*136000*	*81300*	*488*	*312*	*1046.15*	*813.00*
Total Coal	*1834*	*1421*	*130*	*100*	*63440*	*31240*	*136000*	*81300*	*488*	*312*	*1046.15*	*813.00*
Raw Material for Steel plants	*37737*	*32397*	*2640*	*2280*	*5164810*	*4456170*	*8162700*	*7495600*	*1956*	*1954*	*3091.93*	*3287.54*
Pig Iron & Finished Steel from S/P	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*		
Pig Iron & Finished Steel from Other points	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0.00*	*0.00*
Total of Pig Iron & Finished Steel	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0.00*	*0.00*
Iron ore booked for Steel Plants	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*		
Iron Ore Booked for Other Domestic users	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0.00*	*0.00*
Total Iron Ore	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0*	*0.00*	*0.00*
Cement	*124792*	*120133*	*8320*	*8020*	*4686390*	*4267220*	*7414500*	*7125700*	*563*	*532*	*891.17*	*888.49*
Foodgrain	*31771*	*18131*	*1970*	*1140*	*3158300*	*1802080*	*4008100*	*2365100*	*1603*	*1581*	*2034.57*	*2074.65*
Fertilizers	*8521*	*7396*	*540*	*470*	*636080*	*570220*	*911200*	*853700*	*1178*	*1213*	*1687.41*	*1816.38*
Mineral Oils	*14101*	*18780*	*700*	*960*	*543300*	*711780*	*1080400*	*1492400*	*776*	*741*	*1543.43*	*1554.58*
Total of Containers Service	*432106*	*398745*	*12940*	*12410*	*8845850*	*8461270*	*9879600*	*10055000*	*684*	*682*	*763.49*	*810.23*
Balance Other Goods	*90191*	*66104*	*5460*	*3720*	*3392580*	*2482940*	*5230100*	*4240900*	*621*	*667*	*957.89*	*1140.03*
Total Revenue Traffic	***741053***	***663107***	***32700***	***29100***	***26490750***	***22782920***	***36822600***	***33709700***	*810*	*783*	***1126.07***	***1158.41***


Commodity wise break up of originating goods traffic(on originating basis) for the year 2023-24 (7A)


(In Thousands)


Description	**Broad Gauge**				**All Gauges**			
					Tonnes		**Earnings**	
	tonnes 2022-23	**tonnes 2023-24**	**Earnings-2022-23(Cr.)**	**Earnings-2023-24(Cr.)**	**tonnes 2022-23**	**tonnes 2023-24**	**Earnings-2022-23(Cr.)**	**Earnings-2023-24(Cr.)**
RMSP	2640	2280	816	750	2640	2280	816	750
Cement	8320	8020	741	713	8320	8020	741	713
Foodgrain	1970	1140	401	236	1970	1140	401	236
Fertilizer	540	470	91	85	540	470	91	85
containers	12940	12410	988	1005	12940	12410	988	1005
Coal	130	100	14	8	130	100	14	8
Mineral oil	70	96	108	149	70	96	108	149
Others	6090	4584	523	424	6090	4584	523	424
Total	**32700**	**29100**	**3682**	**3370**	32700	29100	3682	3370

This sheet is not to be printed. It is made for graphs only

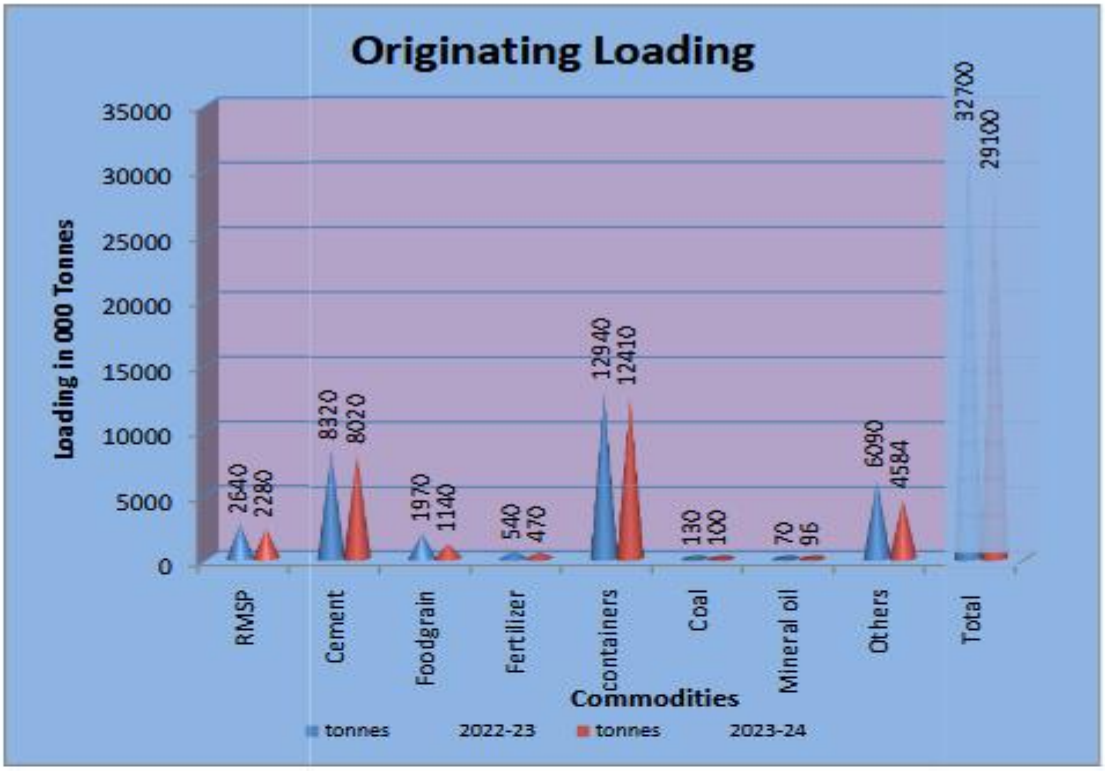
Originating Loading
Loading in 000 Tonnes
35000
30000
25000
20000
15000
10000
5000
0
2640
2280
8320
8020
1970
1140
540
470
12940
12410
130
100
70
96
6090
4584
32700
29100
RMSP
Cement
Foodgrain
Fertilizer
containers
Coal
Mineral oil
Others
Total
Commodities
tonnes 2022-23
tonnes 2023-24

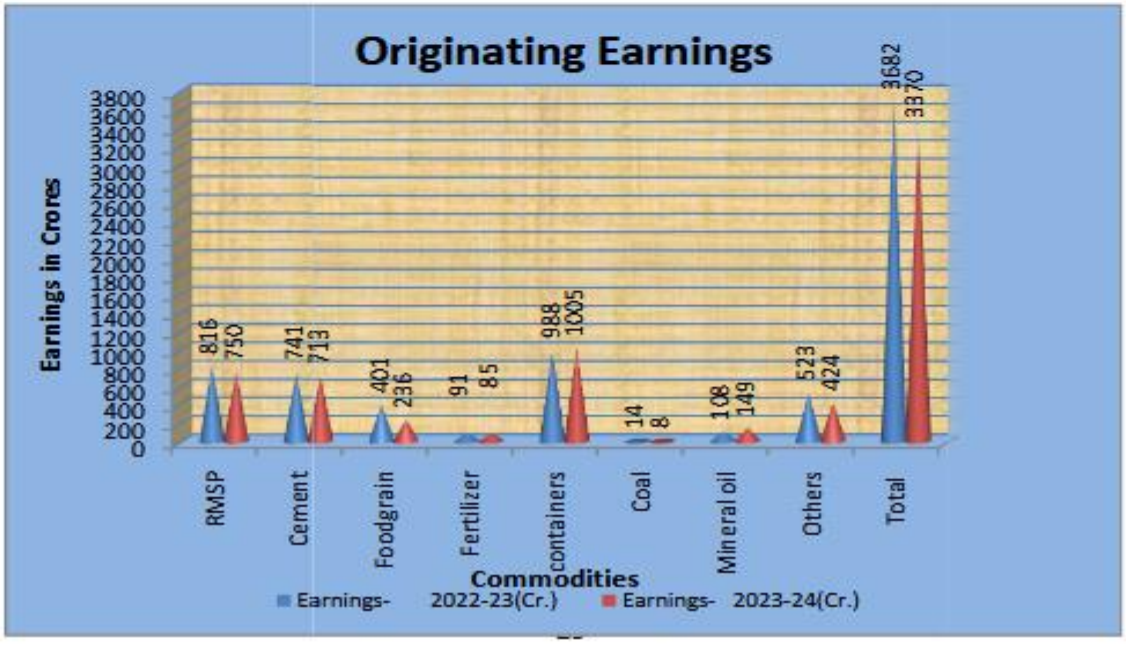
Originating Earnings
Earnings in Crores
816
750
741
713
401
236
91
85
988
1005
14
8
108
149
523
424
3682
3370
RMSP
Cement
Foodgrain
Fertilizer
containers
Coal
Mineral oil
Others
Total
Commodities
Earnings- 2022-23(Cr.)
Earnings- 2023-24(Cr.)

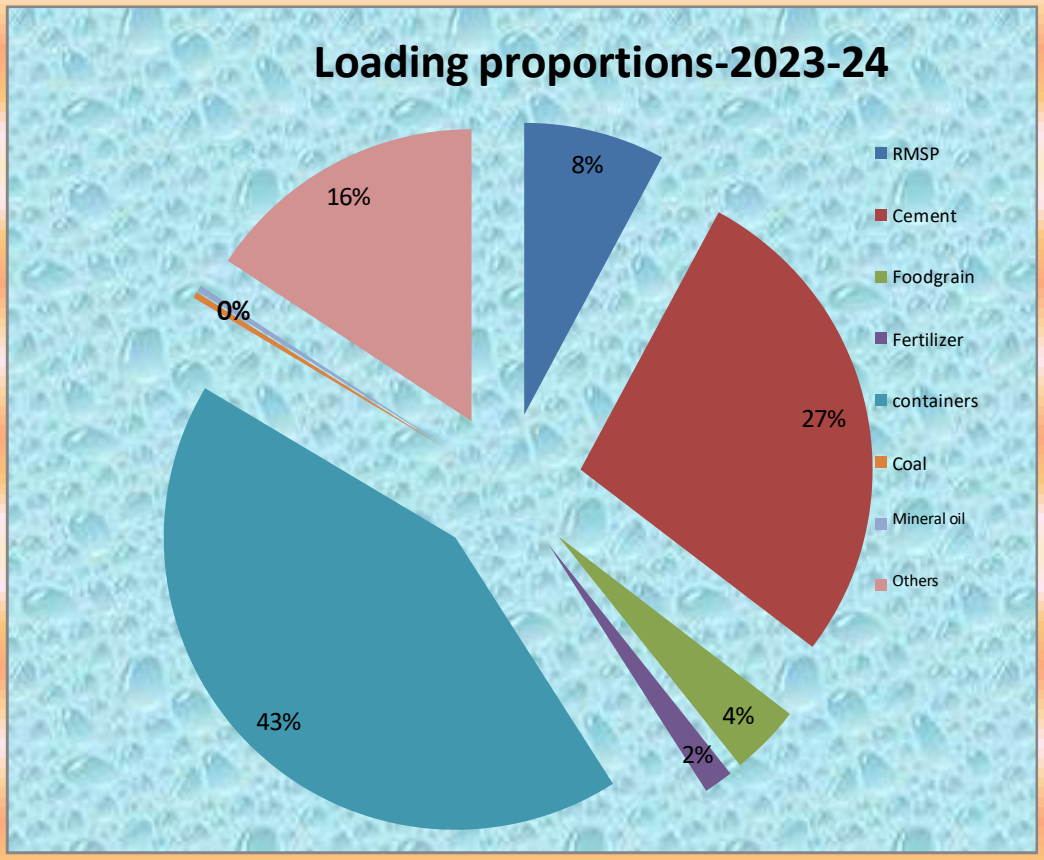
Loading proportions-2023-24
8%
27%
4%
2%
43%
0%
16%
RMSP
Cement
Foodgrain
Fertilizer
containers
Coal
Mineral oil
Others

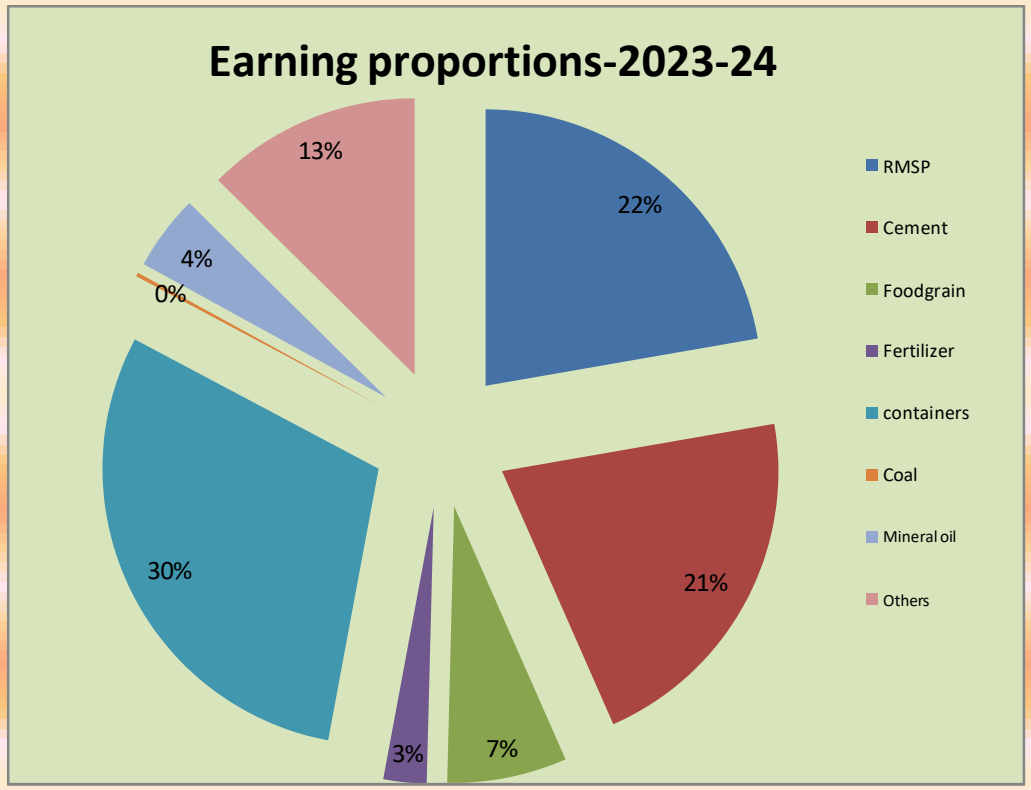
Earning proportions-2023-24
22%
21%
7%
3%
30%
0%
4%
13%
RMSP
Cement
Foodgrain
Fertilizer
containers
Coal
Mineral oil
Others

Transportaion - Operating

Volume of Traffic handled and transportaion output		**2022-23**	**2023-24**
1. Passenger Service :-			
(i) Passenger Originating (In millions)			
Broad Gauge	…	140.00	165.13
Meter Gauge	…	1.08	1.31
Total	…	141.08	166.44
(ii) Passenger Kilometres (In millions)			
Broad Gauge	…	37982	44270
Meter Gauge	…	113	143
Total	…	38095	44413
(iii) Passenger Train Kilometrs including proportion of mixed ,DMU ,Rail Bus and EMU but excluding departmental trains (In thouasands)			
Broad Gauge	…	35761	41430
Meter Gauge	…	118	108
Total	…	35879	41538
(iv) Coaching Vechicle KMs excluding Deptt. trains DMU and EMU Trains (In millions)			
Broad Gauge	…	1224.43	1379
Meter Gauge	…	1.17	1.23
Total	…	1225.60	1380.23
2. Goods Services :-			
(i) Tonnes Originating (In thousands) (Rev.+ Non-Rev.)			
Broad Gauge	…	32745	29461
Meter Gauge	…	0	0
Total	…	32745	29461
(ii) Net Tonne KMs (In millions) (Rev.+ Non-Rev.)			
Broad Gauge	…	26692	22859
Meter Gauge	…	0	0
Total	…	26692	22859
(iii) Goods Train KMs Including proportion of mixed but excluding departmental (In thousands)			
Broad Gauge	…	21412	18535
Meter Gauge	…	0	0
Total	…	21412	18535
(iv) Wagons KMs excluding departmental (In millions)			
Broad Gauge	…	1012	858
Meter Gauge	…	0	0
Total	…	1012	858

Transportaion - Operating
Volume of Traffic handled and transportaion output

3. Operating Efficiency Statistics :		**2022-23**	**2023-24**
(i) Wagon Kms Per Wagon Day			
Broad Gauge	…	312	267
Meter Gauge	…	0	0
(ii) Turn Round of Wagons (In days)			
Broad Gauge	…	1.04	1.30
Meter Gauge	…	0	0
(iii) Net Tonne KMs per wagon days			
Broad Gauge	…	16720	16306
Meter Gauge	…	0	0
(iv) Speed of all goods trains (all tractions)			
Broad Gauge	…	35.03	28.78
Meter Gauge	…	0	0
(v) Coaching vechicle Kms pe Vechicle Day :			
(a) Passenger Vechicles			
Broad Gauge	…	568	550
Meter Gauge	…	54	56
(b) Other Coaching Vechic le			
Broad Gauge	…	600	477
Meter Gauge	…	0	0
(vi) Percentage of loaded wagons kms to total wagon kms.			
Broad Gauge	…	73.00%	69.00%
Meter Gauge	…	0.00%	0.00%
(vii) Average starting wagon load (in tonnes)			
Broad Gauge	…	73.74	89.09
Meter Gauge	…	0	0
(viii) Load of goods trains (tonnes)			
(a) Net or freight load			
Broad Gauge	…	2532	2831
Meter Gauge	…	0	0
(b) Gross load (including weight of engine)			
Broad Gauge	…	3750	4045
Meter Gauge	…	0	0
(c) Gross load (excluding weight of engine)			
Broad Gauge	…	3588	3877
Meter Gauge	…	0	0
(ix) Net tonne Kms per engine Hour			
Broad Gauge	…	61010	60496
Meter Gauge	…	0	0
(x) Gross tonne Kms per train engine Hour			
Broad Gauge	…	90509	86516
Meter Gauge	…	0	0

Figures of Passenger and Goods Working :-

DESCRIPTION		Broad Gauge		Metre Gauge	
		2022-23	2023-24	2022-23	2023-24
A - Passenger Trains Kms including proportion of mixed (Steam, Diesel & Electric locos)					
1. Train Kilometres :					
(including Paas,DMU deptt and Rail Bus	Steam			0	0
	Diesel	27745809	27880845	117502	107532
	Electric	8024854	13565066	0	0
	Total	35770663	41445911	117502	107532
2. Engine Kilometers :					
(Excl.Demu+Rail bus)	Steam	0	0	0	0
	Diesel	27834525	27956073	117886	107964
	Electric	8056186	13611830	0	0
	Total	35890711	41567903	117886	107964
3. Total Gross Tonne Kms. :					
(Incl.Demu+Rail bus)	Steam	0	0	0	0
	Diesel	28894524857	28671112101	35661482	38240356
	Electric	10341332384	16512343393	0	0
	Total	39235857241	45183455494	35661482	38240356
4. Average Gross Load per train (In tonnes) :					
	Steam	0	0	0	0
	Diesel	1105	1028	303	356
	Electric	1289	1217	0	0
	Total	1097	1090	303	356
5. Passenger Net Tonne Km's					
(Incl.Demu+Rail bus)	Steam	0	0	0	0
	Diesel	2592797077	2605376664	9581798	12107042
	Electric	963851862	1536740964	0	0
	Total	3556648939	4142117628	9581798	12107042
6. No. of Passengers carried including season tickets equivalents					
(excluding electric multiple unit)		189364700	223191204	1085400	1306462
B - Goods Trains including proportion of mixed (Steam, Diesel & Electric locosand Incl.Deptt.).					
1. Train Kilometres :					
	Steam	0	0	0	0
	Diesel	19569508	15250000	0	0
	Electric	1850892	3291058	0	0
	Total	21420400	18541058	0	0
2. Engine Kilometers :					
	Steam	0	0	0	0
	Diesel	24911475	19021126	0	0
	Electric	2297295	3967328	0	0
	Total	27208770	22988454	0	0

DESCRIPTION		Broad Gauge		Metre Gauge	
		2022-23	2023-24	2022-23	2023-24
3. Wagon Kms. (Excl. brake van Kms.) :					
	Steam	0	0	0	0
	Diesel	919424730	696803668	0	0
	Electric	93011119	161261923	0	0
	Total	1012435849	858065591	0	0
4. Shunting Kilometres :					
	Steam	0	0	0	0
	Diesel	501073	544173	0	0
	Electric	1923	3196	0	0
	Total	502996	547369	0	0
5. Ratio of Engine Kms. to Train Kms.		1.27	1.24	0	0
6. Ratio of Shunting Kms. to Train Kms.		0.02	0.03	0	0
7. Freight Tonne Kms. :(icluding Departmental)					
	Steam	0	0	0	0
	Diesel	49496118151	42784741723	0	0
	Electric	4760078262	9754044309	0	0
	Total	54256196413	52538786032	0	0
8. Tare Tonne Kms. :(icluding Departmental)					
	Steam	0	0	0	0
	Diesel	3289191232	2596087504	0	0
	Electric	314810036	576868699	0	0
	Total	3604001268	3172956203	0	0
9. Wagon Tare tonne Kms. (Dead weight) :(including Departmental)					
	Steam	0	0	0	0
	Diesel	20595662342	15823447171	0	0
	Electric	2019207125	3577880165	0	0
	Total	22614869467	19401327336	0	0
10. Total Gross Tonne Kms. :(including Departmental)					
	Steam	0	0	0	0
	Diesel	73380971725	61204276398	0	0
	Electric	7094095423	13908763173	0	0
	Total	80475067148	75113039571	0	0
11. Brake Van Kms. ::					
	Steam	0	0	0	0
	Diesel	17783337	14312450	0	0
	Electric	1616834	2957685	0	0
	Total	19400171	17270135	0	0

Operating results :-

DESCRIPTION		Broad Gauge 2022-23	Broad Gauge 2023-24	Metre Gauge 2022-23	Metre Gauge 2023-24
A. Goods and Prop. of Mixed ***(Steam, Diesel and Electric Locos) :***					
1. Net Tonne Kms per route kms per day		26741	25779	0	0
2. Loads of trains (In tonnes) :-					
(a) Freight					
	Steam	0	0	0	0
	Diesel	2528	2803	0	0
	Electric	2572	2961	0	0
(b) Engines(Incl. Wt. Of engine)					
	Steam	0	0	0	0
	Diesel	3743	4007	0	0
	Electric	3825	4218	0	0
(c) Total(Excl. wt of engine)					
	Steam	0	0	0	0
	Diesel	3580	3840	0	0
	Electric	3663	4048	0	0
3. Average freight load per wagon (in tonnes)					
	Steam	0	0	0	0
	Diesel	73.61	88.66	0	0
	Electric	75.1	91.02	0	0
4. Wagon kilometres per wagon day		312	267	0	0
5. Percentage of loaded to total wagon Kms.					
	Steam	0	0	0	0
	Diesel	73	69	0	0
	Electric	68	66	0	0
6. Speed of Goods Trains (Km per hour)					
	Steam	0	0	0	0
	Diesel	35.83	29.80	0	0
	Electric	28.34	24.84	0	0
7. Train Kms per engine day (all traction)		366.79	308.8	0	0

8. Engine Kms per train Kms. (all traction)		1.27	1.24	0	0
9. Train Kms per Engine hrs. (all traction)		16.44	14.75	0	0
10. Fuel Cosumption per 1000 GTKms (in terms of Coal)		16.28	16.10	0	0
B. Passenger and Prop. of mixed *(Steam, Diesel and Electric Locos) :*					
1. Train Kms per route Kms per day		16.49	20.36	2.12	1.93
2. Average No. of vechicle per train					
	Steam	0	0	0	0
	Diesel	35	34	10	11
	Elect.	41	39	0	0
	Total	36	36	10	11
3. Average train Speed.					
	Steam	0	0	0	0
	Diesel	49.74	48.89	24.07	24.00
	Elect.	58.98	55.44	0	0
	Total	51.68	50.93	24.07	24
4. Vechicle Kms per Vechicle day (All Traction)		568	550	54	56
5. Train Kms per engine day (All Traction)		789.5	857	64.38	58.92
6. Engine Kms Per train kms "" "		1.00	1.00	1.00	1.00
7. Train Kms per engine Hrs. " '		51.68	50.93	23.58	23.45
8. Fuel Cosumption per 1000 GTKms (interms of Coal)		34.59	34.35	73.32	79.63

Information regarding No. of Goods Trains run during the year by tractions seperately for through and shunting goods is given below :-

Number of Goods Trains Run during the year :-

	Diesel	Elecric	Electric		Total	
	2022-23	2023-24	2022-23	2023-24	2022-23	2023-24
Broad Gauge						
Through	105032	81314	20448	32534	125480	113848
Shunting	0	0	0	0	0	0
Total	105032	81314	20448	32534	125480	113848
Metre Gauge						
Through	0	0	0	0	0	0
Shunting	0	0	0	0	0	0
Total	0	0	0	0	0	0

Chapter-3

Operating Department

Asset Utilization
Up to the Month of MAR-2024 (BG)

S. NO.	Indices	Target	Actual performance		% age variation over	
			Previous Year	Current Year	Target	Previous Year
1	Freight loading in MT	28.51	32.7	29.1	2.1	-11.0
2	Freight Loading in Wagons	1800	2030.3	1811.8	0.7	-10.8
3	Freight Earnings in Crores	-	3682.3	3371.0	-	-8.5
4	Diesel Utilization	504	506.7	462.4	-8.3	-8.7
5	Electric Utilization	388	368.5	344.9	-11.1	-6.4
6	Wagon Holding	9000	8878.2	8793.6	-2.3	-1.0
7	Wagon Turn Round	1.00	0.99	1.21	21.0	22.2
8	Zonal Interchange	300.00	325.4	249.1	-17.0	-23.4
9	Punctuality (M/Exp.)	95.0	96.88	90.56	-4.7	-6.5
10	Lead (in KM's)		810.11	782.92	-	-3.4
11	Throughput	13500	15130.5	11533.5	-14.6	-23.8
12	Loaded Wagons received		6163.0	4593.1	-	-25.5
13	Inward PU released		1639.0	1733.0	-	5.7
14	Average speed of freight trains including yarding & stabling	22.6	21.54	19.07	-15.6	-11.5
15	Wagon Kms. Per Wagon day	326	312	267	-18.1	-14.4
16	NTKM's per Wagon day	13886	16720	16306	17.4	-2.5
17	NTKM's per Engine hour		61010	60496	-	-0.8
18	Apportioned Earning	6853.9	6840.71	7020.95	2.4	2.6

COMPARATIVE LOADING OF OVER NWR

S.N.	Commodity	Up to the Month						% Variation Over			
		Target		2022-23		2023-24		Target		Last Year MT	
		WGNS	MT	WGNS	MT	WGNS	MT	WGNS	MT	WGNS	MT
1	P-COKE	1803	0.12	1834	0.13	1421	0.1	-21.2	-17	-22.5	-23.1
2	RMSP (LST)	37369	2.65	37737	2.64	32397	2.28	-13.3	-14	-14.2	-13.6
3	CEMENT	66394	4.38	73068	4.77	73129	4.78	10.1	9.1	0.1	0.2
4	CLINKER	46802	3.25	51724	3.55	47004	3.24	0.4	-0.3	-9.1	-8.7
5	FOODGRAIN	15964	1	31771	1.97	18131	1.14	13.6	14	-42.9	-42.1
6	FERTLIZER	7619	0.49	8521	0.54	7396	0.47	-2.9	-4.4	-13.2	-13
7	POL	20680	1.04	14101	0.7	18780	0.96	-9.2	-7.7	33.2	37.1
8	CONTAINER	409250	12.37	432,106	12.94	398,745	12.4	-2.6	0.3	-7.7	-4.1
9	OTHERS	52607	3.21	90191	5.46	66104	3.72	25.7	16	-26.7	-31.9
	G/Total	658489	**28.51**	**741,053**	**32.7**	**663,107**	**29.1**	0.7	2.1	-10.5	-11

PERFORMANCE HIGHLIGHTS OF DIVISIONS-NWR

S. NO	Highlights	2022-23	2023-24	%Var over Last year
		AJMER DIVISION		
1	TL Loading (Avg/Day)	477.6	434.9	-8.9
	Wagon Holding	1030.6	855.0	-17.0
	Wagon Turn Round	0.34	0.54	58.5
	Diesel Utilisation	596.4	549.4	-7.9
	Electric Utilisation	589.3	537.1	-8.9
		BIKANER DIVISION		
2	TL Loading (Avg/Day)	165.5	155.5	-6.0
	Wagon Holding	2665.9	2998.2	12.5
	Wagon Turn Round	0.78	0.93	19.6
	Diesel Utilisation	548.8	481.5	-12.3
	Electric Utilisation	321.9	317.8	-1.3
		JAIPUR DIVISION		
3	TL Loading (Avg/Day)	1016.3	901.7	-11.3
	Wagon Holding	3258.0	2958.9	-9.2
	Wagon Turn Round	0.61	0.69	13.1
	Diesel Utilisation	425.7	368.9	-13.3
	Electric Utilisation	398.8	352.4	-11.6
		JODHPUR DIVISION		
4	TL Loading (Avg/Day)	370.9	319.6	-13.8
	Wagon Holding	1923.8	1981.6	3.0
	Wagon Turn Round	0.99	1.16	17.0
	Diesel Utilisation	601.8	517.6	-14.0
	Electric Utilisation	-	406.8	-

In connection with the above, Operating /planning details for publication of GM 's Narrative report for the period from 01.04.2023- to 31.03.2024(FY 2023-24) are given below :-

S.N	Name of the work(PH-16 Works)	Divn	Work completion date
1	Phulera- 2 Additional stabling line	JP	06.04.2023
2	Satroad- Deveplopment of freight terminal facility	BKN	17.05.2023
3.	Jenal-Bhildi (Odhava) New Block station	JU	02.07.2023
4	Siwani station - STD IIR (SDLP-HSR section)	BKN	23.07.2023.
5	Madar-Ladpura Automatic Block Signal	AII	06.09.2023
6	Siras Additional Loop commissioned on.	JP	31.10.2023
7	Charaud Station - STD IIR (SDLP-HSR section)	BKN	02.11.2023
8	Kishan Garh – Madar section automatic block signaling	JP	05.12.2023
9	Gandhi Nagar – Getor Jagatpura section automatic block signaling	JP	20.01.2024.
10	Jhunpa station (SDLP-HSR section) STD IIR	BKN	06.02.2024
11	Kishan Garh – Sakhun automatic block signaling commissioned on	BKN	03.03.2024
12	Sudsar – Additional loop line (Bikaner Division)	BKN	15.03.2024
13	Bhimal - Additional loop line (Ajmer Division)	AII	17.03.2024
14	Lahli - (Bikaner Division) shifting of Goods shed from Rohtak	BKN	07.03.2024
Gati Shakti Terminal (GCTs)			
1	M/s Wonder Cement Limited Sonu	JU	31.08.2023
2	M/s Unipro Agro Infra Rohtak Pvt. Ltd.	BKN	30.01.2024
3	M/s Hasti petro Chemical and shipping ltd.(HPCSL)	JU	28.03.2024

In connection with the above, Operating/ Time Table details for publication of GM's Narrative Report for the period from 01.04.2023 to 31.03.2024 (FY 2023-24) are given below-

NEW TRAINS

S.N.	Train No.	From	To	Type	Frequency	w.e.f.	Rly
1	20977/20978	AII	DEC	Vande Bharat	Six Day a Week	Ex AII 13.04.23	NWR
2	14527/14528	BTI	SGNR	EXP	Six Day a Week	Ex BTI 15.04.23	NR
3	09635/09636	JP	RE	PSPC	Daily	Ex JP 25.05.23	NWR
4	20475/20476	BKN	PUNE	SF EXP	Weekly	Ex PUNE 05.06.23	NWR
5	12461/12462	JU	SBIB	Vande Bharat	Six Days a Week	Ex JU & SBIB on 09.07.23	NWR
6	19271/19272	BVC	HW	EXP	Weekly	06.09.2023	WR
7	20979/20980	UDZ	JP	Vande Bharat	Six Days a Week	25.09.2023	NWR
8	14087/14088	DLI	JSM	EXP	Daily	06.10.2023	NR
9	14719/14720	BKN	ASR	EXP	Weekly	12.10.2023	NWR
10	12997/12998	BDTS	BME	HUMSAFAR	Weekly	Ex, BDTS 03.01.24 & Ex. BME 04.01.24	WR
11	19009/19010	BDTS	BME	HUMSAFAR	Weekly	Ex, BDTS 05.01.24 & Ex. BME 06.01.24	WR

12	04489/04490	ROK	HNS	PSPC	Daily	Ex-ROK 17.02.24 & Ex-HNS 17.02.24	NR
13	04487/04488	ROK	HNS	PSPC	Daily	Ex-ROK 17.02.24 & Ex-HNS 18.02.24	NR

EXTENSION

S.N.	Train No.	From	To	Type	Extended upto	w.e.f.	Rly
1	09603/09604	JP	LHU	PASS	BTI	11.05.23	NWR
2	09543/09544 (79403/04)	ASV	DNRP	DEMU	COR	04.07.23	WR
3	14724/14723 14118/14117 (new)	BNW	CNB	EXP	PRYJ	05.08.23	NWR/ NCR
4	19225/19226	JAT	JU	EXP.	BGKT	23.07.23	NWR
5	14807/14808	DDR	BGKT	EXP.	JU	23.07.23	NWR
6	12465/12466	JU	INDB	SF	BGKT	31.07.23	NWR
7	19791/14825 14734/14733	JP	HSR	EXP.	BTI	13.09.23	NWR
8	17020/17019	HYB	JP	EXP.	HSR	26.09.23	SCR
9	20973/20974	AII	RMM	H.S. SF	FZR	03.10.23	NR
10	19713/19714	JP	KCG	EXP.	KRNT	07.10.23	NWR
11	19807/19808	KOTA	HSR	EXP.	SSA	09.03.24	WCR
12	19813/19814	KOTA	HSR	EXP.	SSA	09.03.24	WCR
13	20977/20978	AII	DEC	VB Exp.	CDG	14.03.24	NWR
14	09605/06 (79601/02)	AII	JP	DEMU	GGC	16.03.24	NWR

INCREASE IN FREQUENCY

S.N.	Train No.	From	To	Type	Existing Frequency	Revised Frequency	w.e.f.	Rly
1	14661/14662	BME	JAT	EXP	Tri-Weekly	Daily	01.02.24	NWR

STOPPAGES

S.N.	Train No.	From	To	Type	Stoppage Provided at	w.e.f.
1	12323/12324	HWH	BME	Exp.	LHU	01.04.23
2	19333/19334	INDH	BKN	Exp.	LNH	01.04.23
3	22965/22966	BGKT	BDTS	Exp.	PMY	01.04.23
4	22977/22978	JP	JU	Exp.	KKU	03.04.23
5	19735/19736	JP	MJ	Exp.	HDA	03.04.23
6	11089/11090	BGKT	PUNE	Exp.	RANI	04.04.23
7	11089/11090	BGKT	PUNE	Exp.	JWB	04.04.23
8	12719/12720	JP	HYB	Exp.	BJNR	07.04.23
9	16311/16312	SGNR	KCVL	Exp.	FA	10.04.23
10	22483/22484	JU	GIMB	Exp.	SMR	08.04.23

11	12467/12468	JSM	JP	Exp.	POK	08.04.23
12	14703/14704	JSM	LGH	Exp.	POK	08.04.23
13	22931/22932	JSM	BDTS	Exp.	POK	14.04.23
14	15013/15014	JSM	KGM	Exp.	POK	07.04.23
15	19223/19224	ADI	JAT	Exp.	PDWA	14.04.23
16	14813/14814	JU	BPL	Exp.	JAC	22.04.23
17	14813/14814	JU	BPL	Exp.	GOTN	22.04.23
18	12489/12490	BKN	DDR	Exp.	MTD	22.04.23
19	12323/12324	HWH	BME	Exp.	DNA	23.04.23
20	19225/19226	JU	JAT	Exp.	GOTN	22.04.23
21	22483/22484	JU	GIMB	Exp.	MON	26.04.23
22	14803/14804	JSM	SBIB	Exp.	OSN	07.05.23
23	14803/14804	JSM	SBIB	Exp.	MMY	07.05.23
24	14645/14646	JSM	JAT	Exp.	MWT	11.05.23
25	14803/14804	JSM	SBIB	Exp.	MWT	11.05.23
26	15013/15014	JSM	KGM	Exp.	MWT	11.05.23
27	14887/14888	BME	RKSH	Exp.	MNSR	14.05.23
28	22987/22988	AII	AF	Exp.	BKI	24.05.23
29	14645/14646	JSM	JAT	Exp.	KMNC	12.06.23
30	14661/14662	JAT	BME	Exp.	KMNC	18.06.23
31	14887/14888	RKSH	BME	Exp.	DSO	17.07.23
32	14707/14708	BKN	DDR	Exp.	DSO	17.07.23
33	19415/19416	SVDK	ADI	Exp.	CKD	07.08.23
34	20977/20978	AII	DEC	VB EXP.	RE	06.08.23
35	14801/14802	INDB	JU	Exp.	GGR	20.08.23
36	12439/12440	NED	SGNR	Exp.	SDS	18.08.23
37	22981/22982	KOTA	SGNR	Exp.	NAC	18.09.23
38	22997/22998	JLWC	SGNR	Exp.	NAC	18.09.23
39	14721/14722	JU	BTI	Exp.	KJW	20.09.23
40	22497/22498	SGNR	TPJ	Exp.	NGO	22.09.23
41	19027/19028	BDTS	JAT	Exp.	GOTN	30.09.23
42	19333/19334	INDB	BKN	Exp.	RNW	30.09.23
43	19401/19402	ADI	LKO	Exp.	FL	02.10.23
44	19807/19808	KOTA	HSR	Exp.	DKBJ	29.09.23
45	19813/19814	KOTA	HSR	Exp.	DKBJ	28.09.23
46	20471/20472	BKN	PURI	Exp.	MTD	01.10.23
47	20813/20814	PURI	JU	Exp.	FL	27.09.23
48	14721/14722	JU	BTI	Exp.	KXG	29.09.23
49	14813/14814	JU	BPL	Exp.	UMED	29.09.23
50	16311/16312	SGNR	KCVL	Exp.	LGH	26.09.23

51	14887/14888	RKSH	BME	Exp.	DOR	01.10.23
52	22483/22484	JU	GIM	Exp.	DOR	01.10.23
53	15631/15632	BME	GHY	Exp.	LUNI	02.10.23
54	22723/22724	NED	SGNR	Exp.	LUNI	05.10.23
55	19027/19028	BDTS	JAT	Exp.	LUNI	02.10.23
56	22931/22932	BDTS	JSM	Exp.	MMY	29.09.23
57	19615/19616	UDZ	KYQ	Exp.	KSG	25.09.23
58	12555/12556	GKP	BTI	Exp.	BHT	14.10.23
59	14733(14825)	BTI	JP	Exp.	BWK	03.10.23
60	14733(14825)	BTI	JP	Exp.	KSI	03.10.23
61	19415/19416	SVDK	ADI	Exp.	KSI	03.10.23
62	14085/14086	TKBJ	SSA	Exp.	JTS	04.10.23
63	19611/19612	ASR	AII	Exp.	CKD	05.10.23
64	19613/19614	ASR	AII	Exp.	CKD	04.10.23
65	12983/12984	CDG	AII	Exp.	CKD	06.10.23
66	20473/20474	DEE	UDZ	Exp.	AEL	08.10.23
67	12981/12982	JP	ASV	Exp.	SES	06.10.23
68	19821/19822	ASV	KOTA	Exp.	SES	06.10.23
69	19665/19666	KURJ	UDZ	Exp.	GTJT	06.10.23
70	19735	JP	MJ	Exp.	DNK	07.10.23
71	19735	JP	MJ	Exp.	DHND	07.10.23
72	14853/14854	BYC	JU	Exp.	DNK	07.10.23
73	14863/14864	BYC	JU	Exp.	DNK	06.10.23
74	14865/14866	BYC	JU	Exp.	DNK	11.10.23
75	14813/14814	JU	BPL	EXP	SURL	10.01.24
76	20977/78	AII	DEC	VB EXP.	GADJ	18.01.24
77	14086	SSA	TKJ	Exp.	DING	26.01.24
78	4083	JIND	HSR	PSPC	DING	25.01.24
79	14701/14702	SGNR	BDTS	Exp.	Bissau	20.02.24
80	19223/19224	ADI	JAT	Exp.	JWB	16.02.24
81	12547/12548	AGC	SBIB	Exp.	RANI	16.02.24
82	22547/22548	GWL	SBIB	Exp.	RANI	16.02.24
83	04703/04704	BTI	JP	PSPC	SHRG	21.02.24
84	04705/04706	SGNR	JP	TOD Spl	DPLN	21.02.24
85	22481/22482	JU	DEE	Exp.	MHRG	20.02.24
86	14721/14722	JU	BTI/ABS	Exp.	JWL	24.02.24
87	14721/14722	JU	BTI/ABS	Exp.	UMED	24.02.24
88	14813/14814	JU	BPL	Exp.	AAS	24.02.24
89	14813/14814	JU	BPL	Exp.	KXG	24.02.24
90	14813/14814	JU	BPL	Exp.	GA	27.02.24

91	19225/19226	BGKT	JAT	Exp	LKS	07.03.24
92	14716	JP	HSR	Exp	KSI	02.03.24
93	14888/14887	BME	RKSH	Exp	GOTN	09.03.24
94	14701/14702	SGNR	BDTS	Exp	DKBJ	29.02.24
95	12719/12720	JP	HYB	Exp	KSG	01.03.24
96	22451/22452	CDG	BDTS	Exp	KSG	06.03.24
97	12239/12240	MMCT	HSR	Exp	RGS	29.02.24
98	14721/14722	JU	BTI/ABS	Exp.	GOTN	09.03.24
99	14661/14662	BME	JAT	Exp.	JOB	12.03.24
100	14853/14854	JU	BCY	Exp.	REN	09.03.24
101	14863/14864	JU	BCY	Exp.	REN	10.03.24
102	14865/14866	JU	BCY	Exp.	REN	13.03.24
103	19411/19412	SBIB	DLPC	Exp	SOD	07.03.24
104	20491/20492 (14803/14804)	JSM	SBIB	Exp	TIW	06.03.24
105	14087/14088	DLI	JSM	Exp	OSN	06.03.24
106	22481/22482	JU	DLI	Exp	PPR	07.03.24
107	14705/14706	BNW	DKBJ	Exp	JLLO	09.03.24
108	14705/14706	BNW	DKBJ	Exp	BAGA	09.03.24
109	14705/14706	BNW	DKBJ	Exp	KHRA	09.03.24
110	04705/04706	SGNR	JP	TOD Spl	PLSN	08.03.24
111	14701/14702	SGNR	BDTS	Exp	PLSN	08.03.24
112	12467/12468	JSM	JP	EXP	NAC	12.03.24
113	22987/22988	AII	AF	Exp	KSG	12.03.24
114	82653/82654	YPR	JP	Exp	KSG	16.03.24
115	14727/14728	SGNR	TKJ	Exp	BWC	14.03.24
116	19225/19226	BGKT	JAT	Exp	DBI	14.03.24
117	14888/14887	BME	RKSH	Exp	DABN	14.03.24
118	14721/14722	JU	BTI/ABS	Exp	RJS	14.03.24
119	12323/12324	BME	HWH	Exp	MTD	13.03.24
120	22483/22484	JU	GIM	Exp	DQN	14.03.24
121	22483/22484	JU	GIM	Exp	MKSR	15.03.24
122	14888/14887	BME	RKSH	Exp	AS	19.03.24
123	14721/14722	JU	BTI/ABS	Exp	AS	19.03.24
124	20403/20404	PRYJ	BKN	Exp	SDF	21.03.24
125	12403/12404	PRYJ	BKN	Exp	SDF	19.03.24
126	14807/14808	JU	DDR	Exp	MKSR	19.03.24
127	14807/14808	JU	DDR	Exp	MON	19.03.24
128	20491/20492	JSM	SBIB	Exp	DQN	19.03.24
129	19271/19272	BVC	HW	Exp	RNV	19.03.24

TRAINS RUN WITH 130 KMPH (PNU-AII-FL-JP-AWR-RE Section)

S.N.	Train No.	From	To	Nature	Existing Speed	Revised Speed	w.e.f.	Section (from-To)	Rly (P/M)
1	12990	AII	DDR	SF	110	130	27.10.23	AII-PNU	NWR
2	12989	DDR	AII	SF	110	130	28.10.23		
3	19601	UDZ	NJP	EXP	110	130	04.11.23	AII-RE	NWR
4	19602	NJP	UDZ	EXP	110	130	06.11.23		
5	20977	AII	DEC	VB	110	130	17.11.23	AII-RE	NWR
6	20978	DEC	AII	VB	110	130	17.11.23		
7	20979	UDZ	JP	VB	110	130	17.11.23	AII-JP	NWR
8	20980	JP	UDZ	VB	110	130	17.11.23		
9	12461	JU	SBIB	VB	110	130	17.11.23	MJ-PNU	NWR
10	12462	SBIB	JU	VB	110	130	17.11.23		
11	12413	AII	JAT	SUF	110	130	31.12.23	RE-AII	NR
12	12414	JAT	AII	SUF	110	130	30.12.23		
13	12957	ADI	NDLS	RAJ	110	130	31.12.23	RE-PNU	WR
14	12958	NDLS	ADI	RAJ	110	130	31.12.23		
15	12015	NDLS	AII	SHT	110	130	31.12.23	RE-AII	NR
16	12016	AII	NDLS	SHT	110	130	31.12.23		
17	20939	ADI	SLN	SUF	110	130	02.01.24	PNU-RE	WR
18	20940	SLN	ADI	SUF	110	130	03.01.24		
19	22451	BDTS	CDG	SUF	110	130	08.01.24	PNU-FL	NR
20	22452	CDG	BDTS	SUF	110	130	07.01.24		
21	22987	AII	AF	SUF	110	130	07.01.24	AII-BKI	NWR
22	22988	AF	AII	SUF	110	130	07.01.24		
23	12479	JU	BDTS	SUF	110	130	07.01.24	MJ-PNU	NWR
24	12480	BDTS	JU	SUF	110	130	07.01.24		
25	20951	OKHA	JP	SUF	110	130	08.01.24	PNU - JP	WR
26	20952	JP	OKHA	SUF	110	130	09.01.24		
27	12977	ERS	AII	SUF	110	130	14.01.24	JP - AII	NWR
28	12978	AII	ERS	SUF	110	130	12.01.24		
29	19609	UDZ	YNRK	EXP	110	130	11.01.24	AII - RE	NWR
30	19610	YNRK	UDZ	EXP	110	130	12.01.24		
31	19615	UDZ	KYQ	EXP	110	130	15.01.24	AII - BKI	NWR
32	19616	KYQ	UDZ	EXP	110	130	18.01.24		
33	19715	JP	GTNR	EXP	110	130	12.01.24	JP - BKI	NWR
34	19716	GTNR	JP	EXP	110	130	13.01.24		
35	22949	BDTS	DEE	SUF	110	130	17.01.24	PNU - FL	WR
36	22950	DEE	BDTS	SUF	110	130	18.01.24		
37	12991	UDZ	JP	SUF	110	130	11.01.24	AII - JP	NWR
38	12992	JP	UDZ	SUF	110	130	11.01.24		
39	20973	FZR	RMM	HS	110	130	13.01.24	JP - AII	NR
40	20974	RMM	FZR	HS	110	130	16.01.24		
41	12181	JBP	AII	SF	110	130	06.02.24	JP-AII	WCR

42	12182	AII	JBP	SF	110	130	06.02.24		
43	12315	KOAA	UDZ	SF	110	130	08.02.24	JP-AII	ER
44	12316	UDZ	KOAA	SF	110	130	12.02.24		
45	12395	RJPB	AII	SF	110	130	07.02.24	JP-AII	ECR
46	12396	AII	RJPB	SF	110	130	09.02.24		
47	12403	PRYJ	BKN	SF	110	130	06.02.24	AWR-JP	NCR
48	12404	BKN	PRYJ	SF	110	130	06.02.24		
49	12987	SDAH	AII	SF	110	130	06.02.24	BKI-AII	NWR
50	12988	AII	SDAH	SF	110	130	07.02.24		
51	15269	MFP	SBIB	EXP	110	130	08.02.24	BKI-PNU	ECR
52	15270	SBIB	MFP	EXP	110	130	10.02.24		
53	18207	DURG	AII	EXP	110	130	12.02.24	JP-AII	SECR
54	18208	AII	DURG	EXP	110	130	06.02.24		
55	18213	DURG	AII	EXP	110	130	11.02.24	JP-AII	SECR
56	18214	AII	DURG	EXP	110	130	12.02.24		
57	19401	ADI	LKO	EXP	110	130	12.02.24	PNU-BKI	WR
58	19402	LKO	ADI	EXP	110	130	06.02.24		
59	19409	ADI	GKP	EXP	110	130	08.02.24	PNU-BKI	WR
60	19410	GKP	ADI	EXP	110	130	10.02.24		
61	19407	ADI	BSB	EXP	110	130	08.02.24	PNU-RE	WR
62	19408	BSB	ADI	EXP	110	130	10.02.24		
63	14311	BE	NBVJ	EXP	110	130	06.02.24	RE-PNU	NR
64	14312	NBVJ	BE	EXP	110	130	06.02.24		
65	14321	BE	NBVJ	EXP	110	130	07.02.24	RE-PNU	NR
66	14322	NBVJ	BE	EXP	110	130	08.02.24		
67	12307	HWH	JU	SF	110	130	06.02.24	BKI-FL	ER
68	12308	JU	HWH	SF	110	130	06.02.24		
69	14853	BCY	JU	EXP	110	130	07.02.24	FL - BKI	NWR
70	14854	JU	BCY	EXP	110	130	08.02.24		
71	14863	BCY	JU	EXP	110	130	06.02.24	FL - BKI	NWR
72	14864	JU	BCY	EXP	110	130	06.02.24		
73	14865	BCY	JU	EXP	110	130	08.02.24	FL - BKI	NWR
74	14866	JU	BCY	EXP	110	130	07.02.24		
75	20403	PRYJ	BKN	SF	110	130	07.02.24	AWR-JP	NCR
76	20404	BKN	PRYJ	SF	110	130	08.02.24		
77	22307	HWH	BKN	SF	110	130	08.02.24	BKI-FL	ER
78	22308	BKN	HWH	SF	110	130	07.02.24		
79	20943	BDTS	BGKT	SF	110	130	09.05.24	PNU-MJ	WR
80	20944	BGKT	BDTS	SF	110	130	10.05.24	MJ-PNU	WR
81	22965	BDTS	BGKT	EXP	110	130	03.05.24	PNU-MJ	WR
82	22966	BGKT	BDTS	EXP	110	130	04.05.24	MJ-PNU	WR
83	82653	YPR	JP	EXP	110	130	09.05.24	AII-JP	SWR
84	82654	JP	YPR	EXP	110	130	11.05.24	JP-AII	SWR
85	14801	JU	INDB	EXP	110	130	05.05.24	MJ-AII	NWR
86	14802	INDB	JU	EXP	110	130	05.05.24	AII-MJ	NWR
87	16311	SGNR	KCVL	EXP	110	130	07.05.24	MJ-PNU	SR

88	16312	KCVL	SGNR	EXP	110	130	04.05.24	PNU-MJ	SR
89	19027	BDTS	JAT	EXP	110	130	04.05.24	PNU-MJ	WR
90	19028	JAT	BDTS	EXP	110	130	06.05.24	MJ-PNU	WR
91	19415	SBIB	SVDK	EXP	110	130	05.05.24	PNU-RE	WR
92	19416	SVDK	SBIB	EXP	110	130	07.05.24	RE-PNU	WR
93	20823	PURI	AII	SF	110	130	06.05.24	PNU-AII	ECOR
94	20824	AII	PURI	SF	110	130	07.05.24	AII-PNU	ECOR
95	22473	BKN	BDTS	EXP	110	130	06.05.24	MJ-PNU	NWR
96	22474	BDTS	BKN	EXP	110	130	07.05.24	PNU-MJ	NWR
97	22931	BDTS	JSM	SF	110	130	03.05.24	PNU-MJ	WR
98	22932	JSM	BDTS	SF	110	130	04.05.24	MJ-PNU	WR
99	19055	BL	JU	EXP	110	130	07.05.24	PNU-MJ	WR
100	19056	JU	BL	EXP	110	130	08.05.24	MJ-PNU	WR
101	22985	UDZ	DEE	EXP	110	130	05.05.24	AII-FL	NWR
102	22986	DEE	UDZ	EXP	110	130	05.05.24	FL-AII	NWR
103	19107	BVC	MCTM	EXP	110	130	05.05.24	PNU-MJ	WR
104	19108	MCTM	BVC	EXP	110	130	06.05.24	MJ-PNU	WR
105	22475	HSR	CBE	EXP	110	130	08.05.24	MJ-PNU	NWR
106	22476	CBE	HSR	EXP	110	130	04.05.24	PNU-MJ	NWR
107	22915	BDTS	HSR	EXP	110	130	06.05.24	PNU-MJ	WR
108	22916	HSR	BDTS	EXP	110	130	07.05.24	MJ-PNU	WR
109	12463	DEE	JU	SUF	110	130	08.05.24	RE-FL	NWR
110	12464	JU	DEE	SUF	110	130	09.05.24	FL-RE	NWR
111	12465	INDB	BGKT	SUF	110	130	05.05.24	JP-FL	NWR
112	12466	BGKT	INDB	SUF	110	130	05.05.24	FL-JP	NWR
113	12495	BKN	KOAA	SUF	110	130	09.05.24	FL-BKI	NWR
114	12496	KOAA	BKN	SUF	110	130	10.05.24	BKI-FL	NWR
115	12719	JP	HYB	SUF	110	130	08.05.24	JP-AII	SCR
116	12720	HYB	JP	SUF	110	130	06.05.24	AII-JP	SCR
117	15631	BME	GHY	MEX	110	130	06.05.24	FL-BKI	NFR
118	15632	GHY	BME	MEX	110	130	09.05.24	BKI-FL	NFR
119	16209	AII	MYS	MEX	110	130	05.05.24	AII-PNU	SWR
120	16210	MYS	AII	MEX	110	130	07.05.24	PNU-AII	SWR
121	16507	JU	SBC	MEX	110	130	09.05.24	MJ-PNU	SWR
122	16508	SBC	JU	MEX	110	130	06.05.24	PNU-MJ	SWR
123	16531	AII	SBC	MEX	110	130	06.05.24	AII-PNU	SWR
124	16532	SBC	AII	MEX	110	130	10.05.24	PNU-AII	SWR
125	16533	JU	SBC	MEX	110	130	08.05.24	MJ-PNU	SWR
126	16534	SBC	JU	MEX	110	130	05.05.24	PNU-MJ	SWR
127	16587	YPR	BKN	MEX	110	130	05.05.24	PNU-MJ	SWR
128	16588	BKN	YPR	MEX	110	130	05.05.24	MJ-PNU	SWR
129	17019	HSR	HYB	MEX	110	130	07.05.24	JP-AII	SCR
130	17020	HYB	HSR	MEX	110	130	11.05.24	AII-JP	SCR
131	18573	VSKP	BGKT	MEX	110	130	09.05.24	JP-FL	ECOR
132	18574	BGKT	VSKP	MEX	110	130	11.05.24	FL-JP	ECOR
133	20471	BKN	PURI	SUF	110	130	05.05.24	FL-JP	NWR

134	20472	PURI	BKN	SUF	110	130	08.05.24	JP-FL	NWR
135	20481	BGKT	TPJ	SUF	110	130	08.05.24	FL-JP	NWR
136	20482	TPJ	BGKT	SUF	110	130	11.05.24	JP-FL	NWR
137	20813	PURI	JU	SUF	110	130	08.05.24	JP-FL	ECOR
138	20814	JU	PURI	SUF	110	130	11.05.24	FL-JP	ECOR
139	20843	BSP	BGKT	SUF	110	130	06.05.24	JP-FL	SECR
140	20844	BGKT	BSP	SUF	110	130	09.05.24	FL-JP	SECR
141	20845	BSP	BKN	SUF	110	130	09.05.24	JP-FL	SECR
142	20846	BKN	BSP	SUF	110	130	05.05.24	FL-JP	SECR
143	22463	DEE	BKN	SUF	110	130	05.05.24	RE-FL	NWR
144	22464	BKN	DEE	SUF	110	130	07.05.24	FL-RE	NWR
145	22497	SGNR	TPJ	SUF	110	130	06.05.24	MJ-PNU	NWR
146	22498	TPJ	SGNR	SUF	110	130	10.05.24	PNU-MJ	NWR
147	22631	MDU	BKN	SUF	110	130	09.05.24	JP-FL	SR
148	22632	BKN	MDU	SUF	110	130	05.05.24	FL-JP	SR
149	22723	NED	SGNR	SUF	110	130	09.05.24	PNU-MJ	SCR
150	22724	SGNR	NED	SUF	110	130	11.05.24	MJ-PNU	SCR
151	20487	BME	DLI	SUF	110	130	06.05.24	FL - RE	NWR
152	20488	DLI	BME	SUF	110	130	07.05.24	RE-FL	NWR
153	20489	BME	MTJ	SUF	110	130	05.05.24	FL - AWR	NWR
154	20490	MTJ	BME	SUF	110	130	05.05.24	AWR-FL	NWR
155	15633	BKN	GHY	MEX	110	130	08.05.24	FL - BKI	NFR
156	15634	GHY	BKN	MEX	110	130	11.05.24	BKI-FL	NFR

In reference to the above subject, the required information related to Coaching section are as under:-

Details of Extra coaches, Permanent augmentation, special trains and FTR trains/ coaches LHB Conversion of trains for the year 2022-23 & 2023-24		
	2022-23	2023-24
1. Extra Coaches (Day to Day basis & Temporary augmentation		
Number of coaches	42550 (Both Side)	31216 (Both Side)
2. Permanent Augmentation of trains		
Number of Coaches	81	27
Number of Trains	41	13
3. Special Trains (TOD/HSP/Mela, Exam Spl)		
Number of Trains	1499	1726
Number of Trips	38556	44038
4. FTR Special Trains		
Number of Trains	33	102
Number of Trips	60	156
5. FTR Coaches		
Number of Coaches	18	20
6. LHB Rake Conversion		
Number of Trains	05	12

Number of Rakes	10	18

Coaching Operations:

3.10 Punctuality performance of coaching trains of N. W. Railway for the year 2023-24

Category of trains	% of punctuality	
	BG	MG
Mail / Express	90.56	--
Passengers	95.22	99.73
All coaching	**92.58**	**99.73**

On A/C of alarm chain pulling total No. of cases and total time lost in minutes during the year 2023-24

Details	**2023-24**
Total No. of ACP cases	3147
Total No. of minutes lost	31060

No. of coaching trains services:

BG (Mail / Express) -	**2023-24**
1. Daily	160
2. Weekly	142
3. Bi-weekly	54
4. Tri – weekly	38
5. Four days a week	16
6. Five days a week	04
7. Six days a week	08
Total	**422**

BG (Passenger):	
Passenger trains	200

MG	
Passenger trains	02


Chapter-4

Commercial


4 Revenue

4.1.1 Originating Passenger Revenue – NWR has achieved the highest Originating Passenger Revenue of Rs. 3206.11 Cr. in 2023-24 which is 14.45% higherthan the revenue of Rs.2801.43 Cr achieved during the year 2022-23.


The total number of originating passengers in 2023-24 is16.45 Cr which is 17.33% higher than 14.02Cr.passengers booked during the year 2022-23.

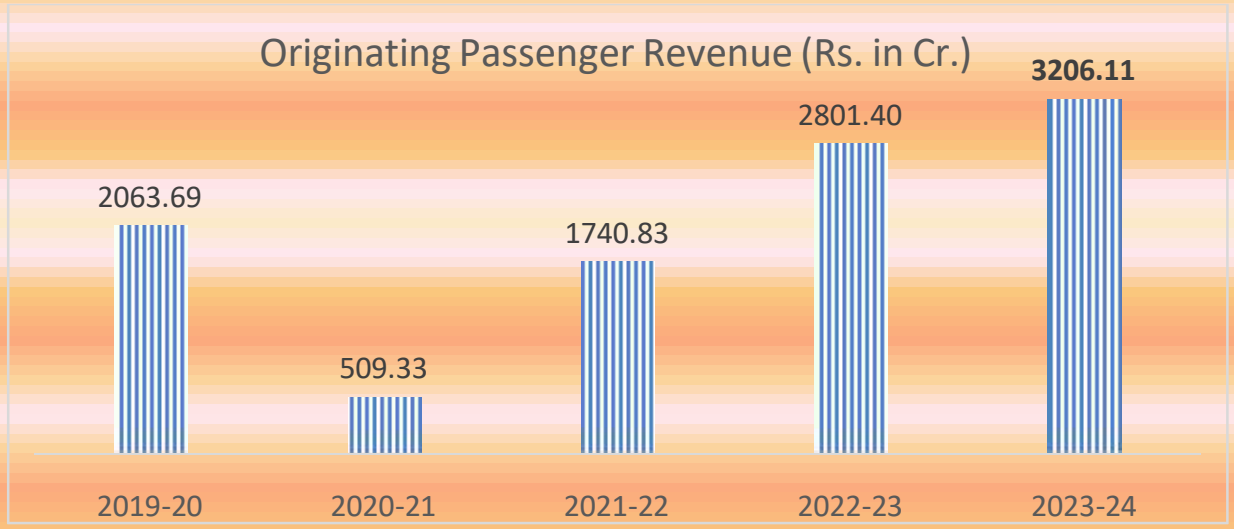


4.1.2 Other Coaching Revenue–NWR has achieved the highest originating OCH Revenue of Rs. 337.85Cr in 2023-24which is 20.79% higher than the revenue of Rs.279.70 Cr achieved during the year 2022-23.

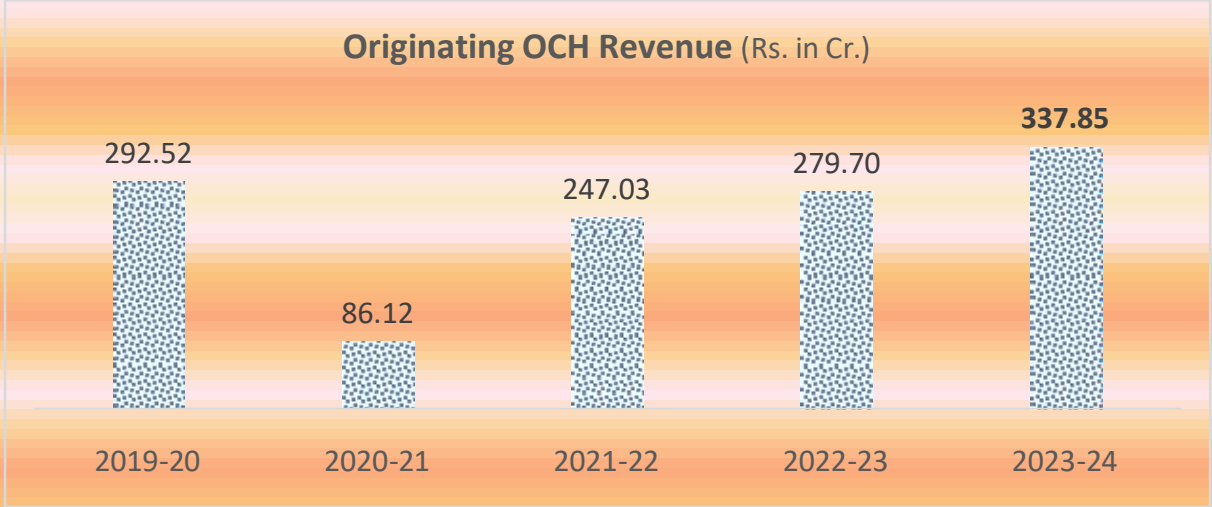


4.1.3 Originating Goods Revenue- The Originating Goods RevenueisRs. 3401.93 Cr.in 2023-24which is -8.28% lowerthan the revenue of Rs.3709.14Cr.achieved during the year 2022-23.

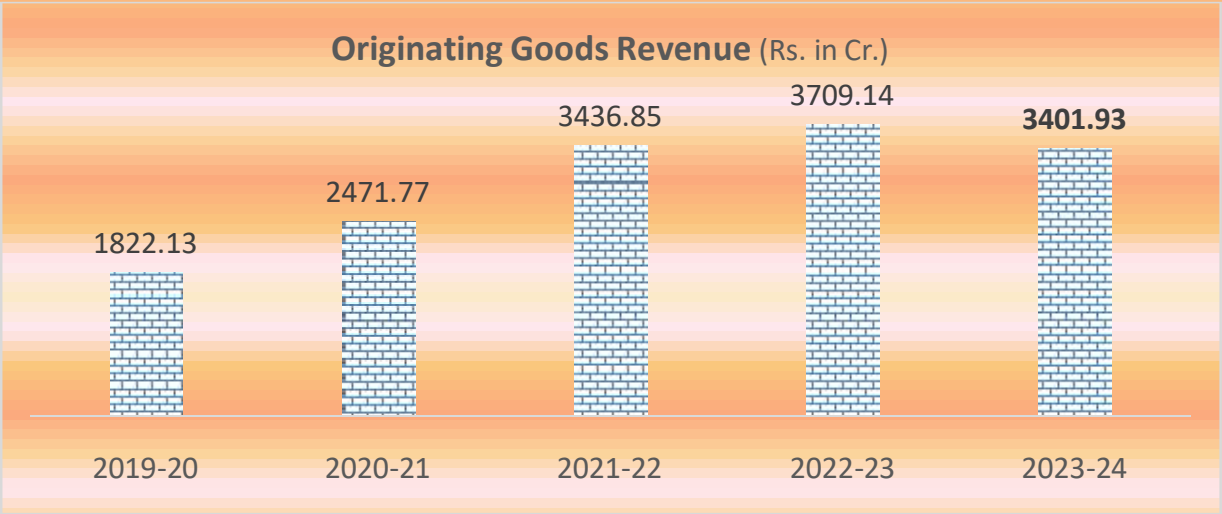


4.1.4 Sundry Revenue: The Sundry Revenue wasRs. 619.52 Cr. in 2023-24 which is 24.43% higher than the revenue of Rs. 497.90 Cr. achieved during the year 2022-23.

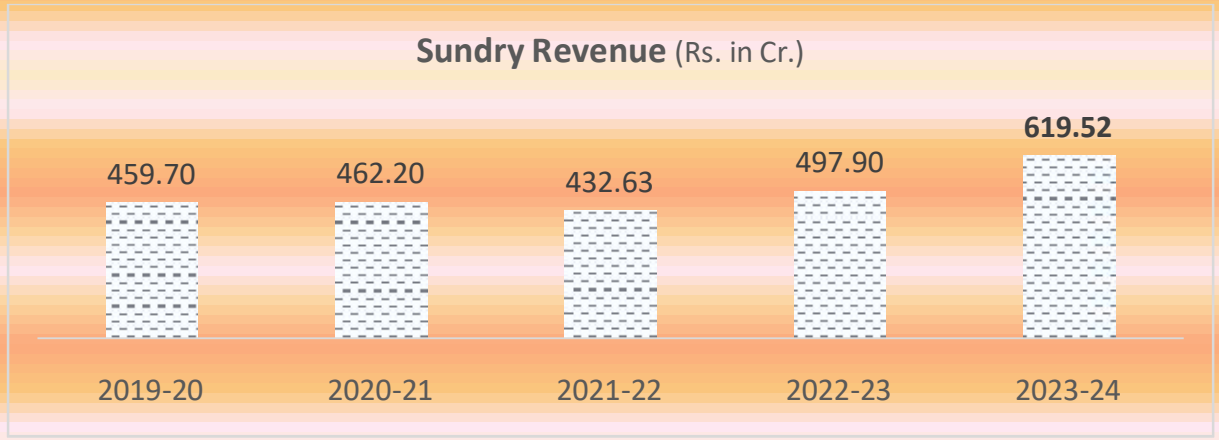

4.1.5 Originating Gross Revenue: NWR has achieved ever highest Originating Gross Revenue of Rs. 7565.48 Cr. in the year 2023-24 which is 3.80% higher than the revenue of Rs. 7288.18Cr. achieved during the previous year.

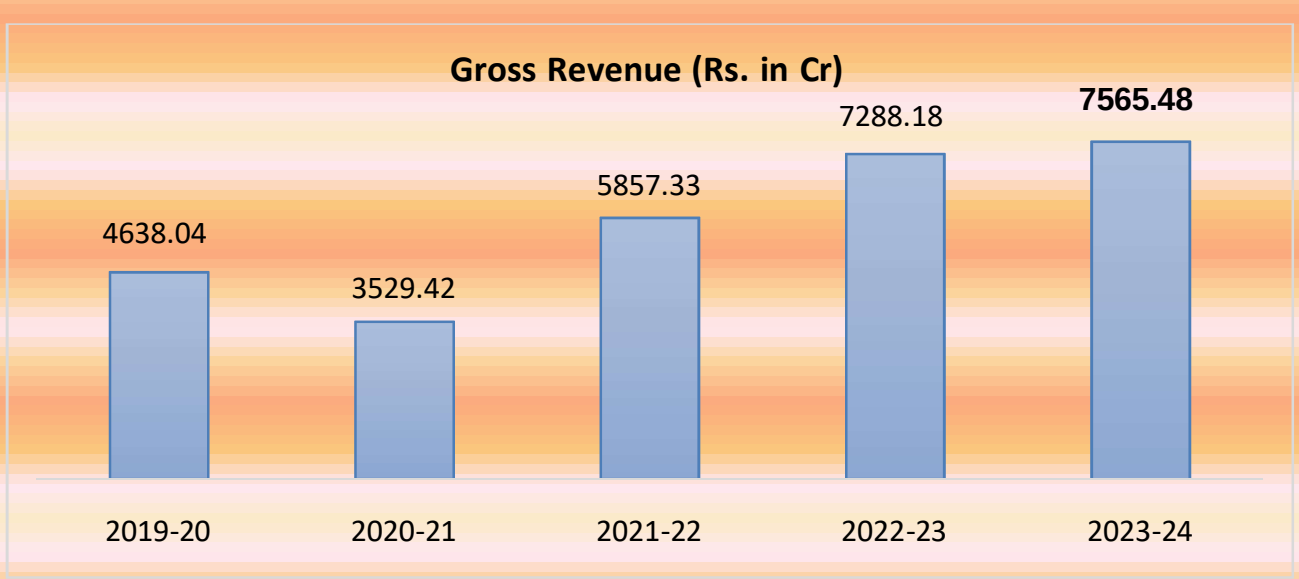


4.1.6 Commodity-wise Revenue (Rs. Cr.)

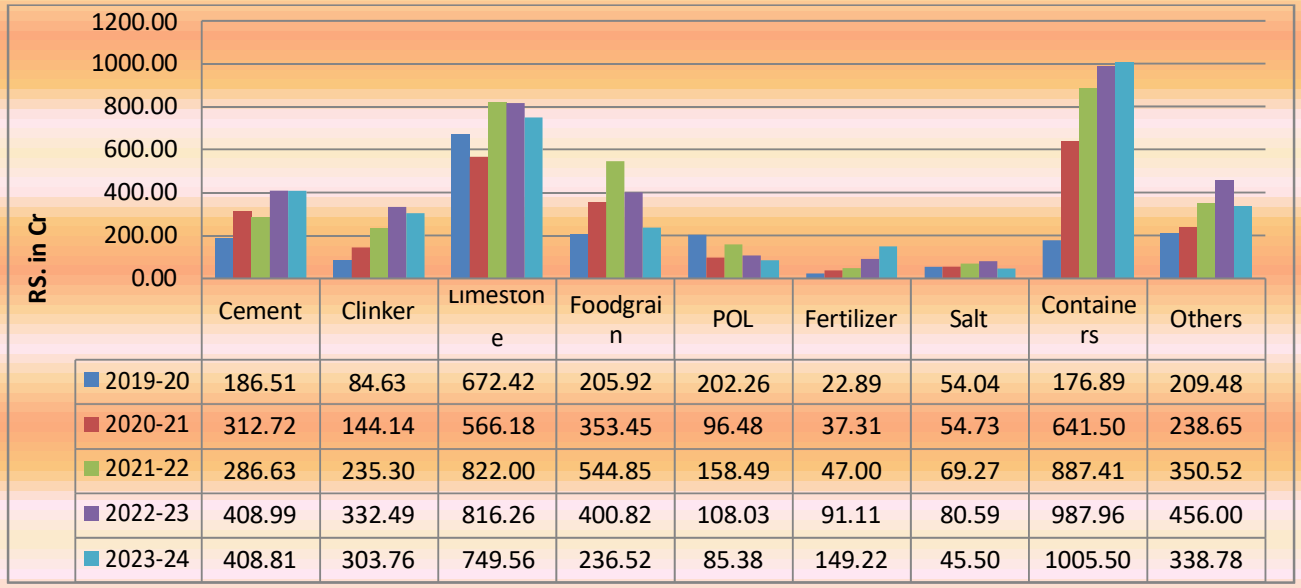


	Cement	Clinker	Limestone	Foodgrain	POL	Fertilizer	Salt	Containers	Others
2019-20	186.51	84.63	672.42	205.92	202.26	22.89	54.04	176.89	209.48
2020-21	312.72	144.14	566.18	353.45	96.48	37.31	54.73	641.50	238.65
2021-22	286.63	235.30	822.00	544.85	158.49	47.00	69.27	887.41	350.52
2022-23	408.99	332.49	816.26	400.82	108.03	91.11	80.59	987.96	456.00
2023-24	408.81	303.76	749.56	236.52	85.38	149.22	45.50	1005.50	338.78

4.1.7 Clearance of Station Outstanding – Due to concerted efforts, Station Outstanding was up to the level of Rs. 51.81 Cr at the end of the financial year 2023-24.

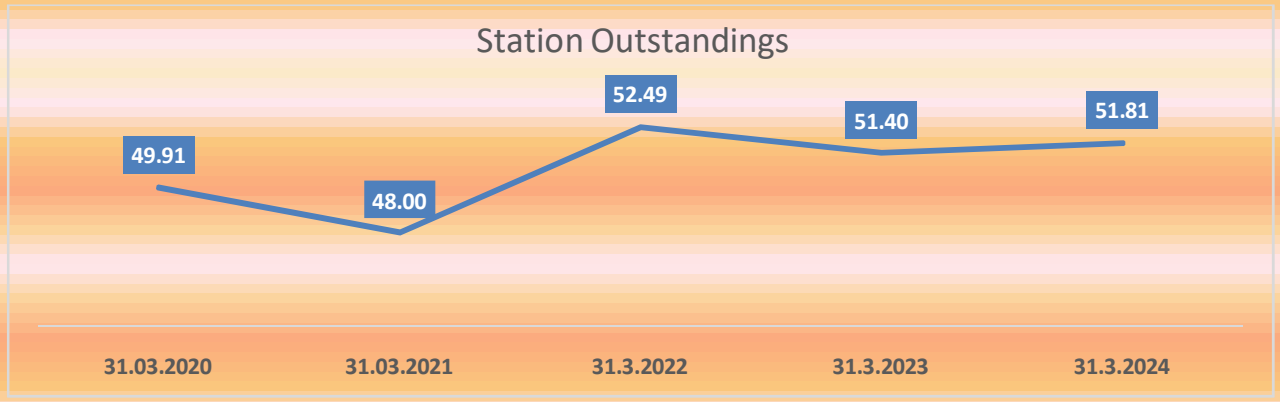

4.1.8 Parcel & Luggage Revenue/Leasing of SLR – The Parcel & Luggage Revenue in 2023-24 is 61.98Cr which is 16.86% higher than the revenue of Rs.53.04Cr achieved during the previous year.

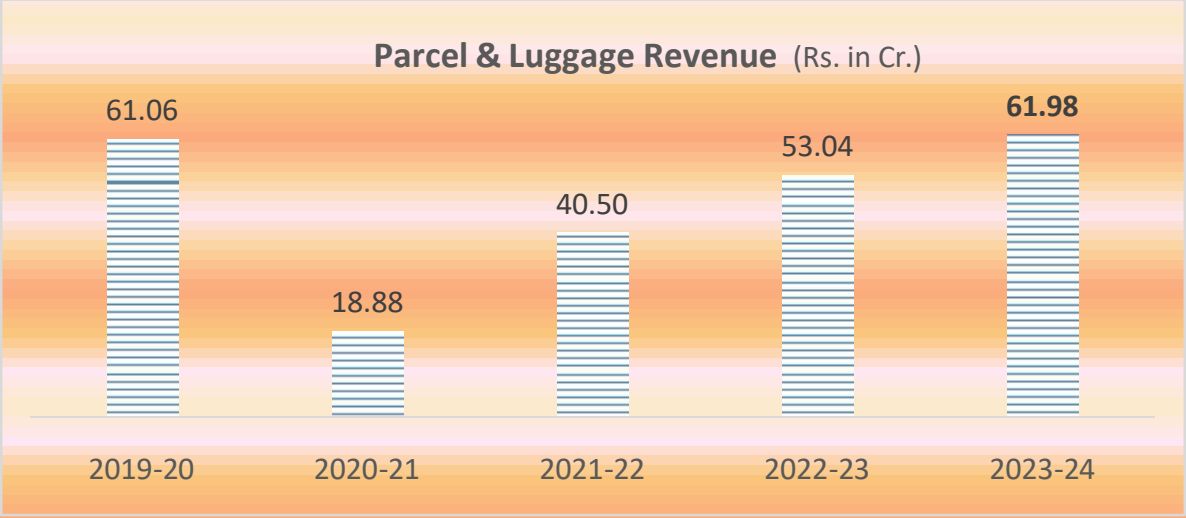



4.2 Ticket Checking

4.2.1 Ticket checking performance: Total Ticket Checking Revenue increasedby 13.91%. Ticket checking Revenueof Rs. 63.23 Cr.were ever highest in the year 2023-24 as compared to Rs. 55.51 Cr. in the previous year. The Nos. of cases were also gone up by 17.82%.

4.2.2 Cases and Revenue:


	Unit	2019-20	2020-21	2021-22	2022-23	2023-24
Total Cases	**Nos.**	999256	62992	858865	1117747	**1316898**
Total Revenue	**Cr.**	41.30	2.90	43.46	**55.51**	**63.23**



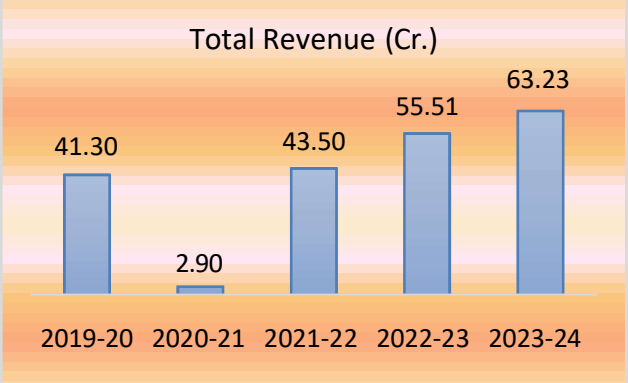

4.2.3 Commercial Publicity Revenue

The Commercial Publicity Revenueof Rs.11.89 Cr is ever highest in the year 2023-24 which is 6.07%higher than the revenue of Rs. 11.21 Cr. achieved during the previous year.

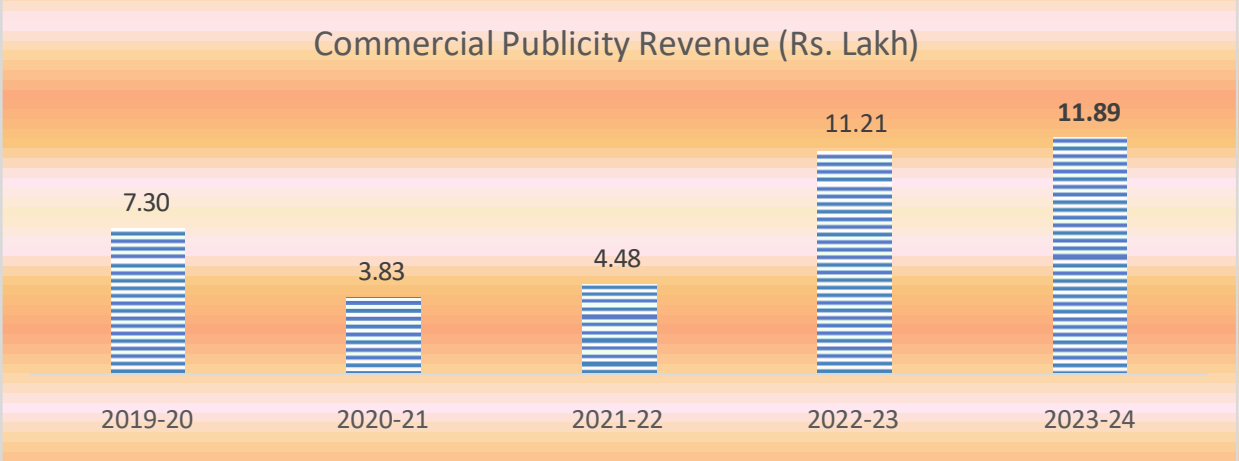

4.3 Passenger Amenities

4.3.1 Passenger Amenities – All endeavours have been made for perceptible improvements at railway stations over North Western Railway.

Amenities provided during 2023-24

AMENITIES	NAME OF STATIONS
Station Building (05 Stations)	Khuchamancity, NayaKhardiya,GovindiMarwar,Gudha&Sambhar Lake
Circulating Area	NIL
Foot Over Bridges (04 Stations)	Haripur, Pindwara, Banas&Rajaldesar
Improvement Platform Surface	NIL
Platform Shelter (17 Stations)	Sanganer,Kanauta,Bheslana, Khandel,Sanodiya,Mindha, Tiloniya, Sakhun,Shivdaspura, FatehpurShekhawati , Jhunjhunu, Khuchaman City, ThathanaMithri, Nawacity, Gudha, Govindimarwar&Sambhar lake
Lifts(02 Stations)	Abu Road & Ajmer
Escalators (01 Station)	Bhagat Ki Kothi (PF 1 & 2nd entry)
2nd Entry	Nil
Raising/Provision of High Level Platform (38 Stations)	Biraliya, Khimel, Iqbalgarh, FatehpurShekhawati, AsalpurJobner, Bhukerka halt, Hansiawas Halt, Sherekan, Dulrasar, DalpatSinghpur, Dokwa, Hadyal, NangalPathani halt, Surera halt, Udasar halt, Mayar Halt, Masaniwala halt,Mehuwala halt, Raman,Bhiwanicity,Jhupna, DabliRathan, Jatusana, KishangarhBalawas, KaninaKhas, Satnali,Diplana, Khinaniya, Suratpura, Ramsinghpur, Paylihalt,Patuwasmehrana halt,Khuchaman city, ThathanaMithri,NayaKhardiya, Nawacity, Govindimarwar&Sambhar lake
Extension of Platforms (08 Stations)	ThathanaMithri, NayaKharidiya, Nawacity, GovindiMarwar, Sambhar Lake, Gudha, SriDungargarh&Rajaldesar
Additional Platforms (01 Stations)	DabliRathan
Facilities for Divyangjan (05 Stations)	KhuchamanCity,NayaKhardiya, GovindiMarwar, Gudha& Sambhar lake
Toilets (09 Stations)	Badhal, Rani, Pindwara, Falna, Somesar, Jawaibandh, Marwar, Sojat Road &Nasirabad
Steel Benches (06 Stations)	Kuchamancity,Thathanamithri, NayaKhardiya, Govindimarwar, Gudha&Sambharlake

4.3.2Categorisation of Stations

Division	NSG-1	NSG-2	NSG-3	NSG-4	NSG-5	NSG-6	HG-1	HG-2	HG-3	TOTAL
Ajmer	0	1	3	3	11	74	0	2	33	**127**
Bikaner	0	0	3	5	23	98	0	0	64	**193**
Jaipur	0	1	6	3	11	68	0	4	24	**117**
Jodhpur	0	1	3	4	22	94	0	3	16	**143**
Total	**0**	**3**	**15**	**15**	**67**	**334**	**0**	**9**	**137**	**580**

4.3.3 Cleanliness –

- **Mechanised Cleanliness** - Mechanized Cleanliness contracts at 33 stations have been given to provide better and hygienic atmosphere at stations.
- **Pay and Use Toilets** – To provide clean and sanitized toilet facility, Pay & Use toilets have been provided at 29 stations.

4.3.4 Passenger Reservation System/Unreserved Ticketing System– 2023-24

Division	All	BKN	JP	JU	Total
No. of PRS	08	10	10	20	**48**
Non-Railhead PRS Locations	10	0	6	1	**17**
Total PRS	18	10	16	21	**65**
Unreserved Ticketing System (UTS)	81	84	73	93	**331**
UTS cum PRS system	15	44	20	31	**110**
YTSK	1	1	-	2	**4**
PoS Machine	48	109	66	32	**255**

4.4 CLAIMS FOR COMPENSATION FOR GOODS OR PARCELS LOST OR DAMAGED

(a) Registration of new claims

The total No. of new claims registered in the year 2023-24 were: 69

(b) Court Cases

(i) The No. of new suits registered in the year 2023-24were: 150

(c) Suit barred claims:

Suits barred claims paid in the year 2023-24 was: NIL

Claim for Compensation:

The table furnish below represents the figure of compensation for the previous year.

Statement - A 2023-24

	Particulars	Nos.
a)	No. of claims involving compensation for goods & parcels lost, damaged or carried over as unsettled at the end of the previous year.	34
b)	(i) Fresh Received.	69
	(ii) Re-opened for compensation on account of goods and parcels lost, damaged or delayed during the period	0
c)	Total (a) + (b)	103
d)	No. of claims referred to in item (a) & (b) settled: -	85
	(i) By payment	2
	(ii) Otherwise during the period	83
	(iii) Total	85
e)	Balance outstanding as unsettled at the close of the period	18
f)	(i) Paid amount (as per statement 'B' total) (Rs. In Lakhs)	1.95
	(ii) Amount realized from auction of unclaimed and damaged goods etc. (Rs. in Lakhs)	0.0
	(iii) Net amount paid as compensation i.e. f (i) - f (ii)	1.95
g)	Percentage of sum paid in compensation (item f (i) to Gross Revenue goods & other coaching)	0.00052%
h)	Average time taken in settlement of claims shown under item No. d (iii)	162 days
(i)	No. of claims cases pending more than for four months on 31st March	50

Note:

a) The figures shown under item (a) & (b) of the above statement are including of Coal Claims but exclusive of the Court cases.

b) Payment of Decreed Court cases not included in item f(i) was paid Nil during 2022-23.

4.5 CLAIM PREVENTION

The number of new claims received, paid and also number of claims repudiated and disposed of otherwise together with amount of compensation paid (excluding court cases) during the year 2023-24.

S. No.	Particulars	2023-24
1.	No. of claims received	**103**
2.	No. of claims paid	**2**
3.	No. of claims repudiated	**5**
4.	No. of claims disposed off otherwise	**78**
5.	**Total disposal**	85
6.	Closing Balance	**18**
7.	Claims cases Amount paid in lakhs of Rs.	**1.95**
8.	No. of claims settled by the Court	**0**
9.	**Amount paid in court cases (Rs. in lakhs)**	**0.0**

The number of wagon load connected together with the approximate value thereof, amount realized by sale of unconnected, undelivered articles and handing over unconnected goods for

S.No.	Particulars	2023-24
1.	No. of unconnected wagon load connected	NIL
2	Approximate value of wagon load connected (Rs. in lakh)	NIL
3.	Amount realized by sale of unconnected, undelivered articles	NIL
4.	Credit received for handing over connected goods for Departmental use	NIL

departmental use as compared to the previous year are as follows: -

Statement - B

S.No.	Cause wise statistics	No. of cases	Amount Paid (Rs. in lakh)	Percentage of Total	
				No (%)	Amount (%)
1.	Amount paid on account of loss ofCompletepackageconsignments	NIL	NIL	NIL	NIL
2.	Theft of complete package consignment	NIL	NIL	NIL	NIL
3.	Pilferage i.e. other than complete package consignment	NIL	NIL	NIL	NIL
4.	Damage by wet	NIL	NIL	NIL	NIL
5.	Delay in transit	NIL	NIL	NIL	NIL
6.	Leakage	NIL	NIL	NIL	NIL
7.	Fire	NIL	NIL	NIL	NIL
8.	Fraud	NIL	NIL	NIL	NIL
9.	All other causes	**71**	**0.00**	100%	**0.00**
10.	Settlement in Court (Claims)	NIL	NIL	NIL	NIL
	Total	71	0.00	**100%**	**0.00**

Statement - C

S. No.	Particulars	2023-24
1.	No. of suit carried forward from the previous year (Including Nil cases of U/s 124)	274
2.	No. of new suits registered (Including Nil cases of U/s 124)	150
3.	No. of suits settled out of court	424
4.	No. of suits dismissed	34
5.	No. of suits decreed	124
6.	No. of suits withdrawzn	0
7.	No. of suits otherwise	0
8.	No. of suits pending	266

4.6 RAILWAY ACCIDENT AND COMPENSATION CLAIMS:

No major train accident took place during the year; hence Nil cases have been registered under Sec 124.

Statement showing details of untoward incident cases registered under Sec 124'A'.

S. No.	Particulars	2023-24
1.	Opening balance (Including cases other than JP RCT)	274
2.	Fresh Registered (Including cases other than JP RCT)	150
3.	Total (1+2)	424
(a)	By Decreed - No. of cases Decreed Amount Death cases = 104Nos.659.80Lakhs Injury cases =20 Nos .244.89 Lakhs Total = 124Nos.904.69 Lakhs	124
(b)	Dismissed	34
	Total	158
4.	Closing balance 31st March -2024	266
5.	**Decreed amount (Rs. In Lakhs)**	**904.69**

*****

Chapter-5

Engineering Department

Progress of Works for GM Narrative Report 2023-24 (Engineering Department)

S. No.	PH No.	PB/ LB No.	Particulars of Work	Anticipated Cost (In Thousands)	Exp. uoto 31.03.23 (In Thousands)	Present Status of the Work (Phy.)/
1.	16	PB-60	North Western Railway-Traffic facilities and capacity augmentation works (PB#135/NR/2023-24)	0	0	
2.	16	PB-61	North Western Railway - Provision of safety fencing and subways on various routes with speed 130 kmph and above (PB#136/NR/2023-24)	0	0	
3.	16	-	ADEN/FA-Provision of Fencing/B wall at various location in C/w raising of Speed to 160KMPH. (Length 88.96 Kms)	397718	0	15%
4.	16	-	ADEN/Line-Provision of Fencing/B wall at various location in C/w raising of Speed to 160 KMPH (Length 53.41 KM)	352729	0	1%
5.	16	-	ADEN/ABR Sub Div:- Prov of Fencing/B Wall in C/w Raising of Spee to 160 KMPH Bet PDWA-ABR Section (Length 33.354 KM)	283852	0	15%
6.	16	-	ADEN/ABR:- Prov of fencing/B Wall at various locations in c/w raising of speed to 160 KMPH in ABR-PNU Section (Length 39.884 KM)	330924	0	
7.	16	-	ADEN/MJ-Provision of Fencing/B wall at	435531	0	5%

			various location in C/w raising of Speed to 160KMPH. (length 58.130 Kms)			
8.	16	-	Aburoad~~Train terminating facility at ABR and stabling line along with goods PF at BMN station	407035	0	
9.	16	-	Jawaibandh~~Provision on full length line along with goods PF at Jawaibandh (JWB) Station	25802	0	0
10.	16	-	Udaipurcity~~Convertin g stabling line no. 9 into running line and a passenger PF line at Udaipur station	51008	0	
11.	16	-	Ajmer~~Provision of 3 Loop lines at Ajmer station on Madar end	354100	0	
12.	16	-	Provision of Audio Visual Buzzer/Alarm system to alert station master to set point against occupied line at stations (89) over Ajmer division	7768	0	75%
13.	16	-	Prov of Temp Fencing to prevent CRO in section of ADEN/ ABR from KM 560.00 to 648.90 (Length 67.90 KMS)	19754	0	10%
14.	16	-	Prov of Temp Fencing to prevent CRO in the Section of ADEN/FA KM 454.00 to 560.00 (Length 45 KMS)	13092	0	10%
15.	16	-	Prov of Temp Fencing to prevent CRO in the Section of ADEN/MJ from KM 398.50 to 454.00, Bet CNL - BWA (Length 48.5 KMS)	14110	0	20%
16.	16	-	Prov Temp Fencing to prevent CRO in the Section of ADEN MJ from KM 342.5 to 398.50 , Bet BER to CNL(Length 49 KMS)	14255	0	20%
17.	16	-	Providing 61700 RM Temporary Fencing to prevent CRO in the	22021	0	

			jurisdiction of ADEN/RPZ in Chitaurgarh-Udaipur section.			
18.	16	-	Prov Temp Fenc to prevent CRO in the Section of ADEN /Line/Aii jurisidiction in MD-BER Section From KM 285.70 to 342.50 (Total 53.00 KMS)	16286	0	
19.	16	-	Providing 4700 RM boundary wall to prevent CRO in the jurisdiction of ADEN/RPZ in Chitaurgarh-Udaipur section.	26031	0	5%
20.	16	-	Dhuwala~~Det~~Prov of Temp Fencing to prevent CRO in section of ADEN/BHL from KM 114.67 to 175.46 (Length 40.65 KMS)	23120	0	
21.	16	-	Mokhampura~~Dhuwal a~~Prov of Temp Fencing to prevent CRO in section of ADEN /BHL from KM 59.00 to 114.67 (Length 40.47 KMS)	23017	0	
22.	16	-	Ajmer~~Mokhampura~ ~Prov of Temp Fencing to prevent CRO in section of ADEN/ BHL from KM 0 to 59.00 (Length 40.47 KMS)	23017	0	
23.	16	-	Mandi dabwali~~Conversion of non-running line no. 4 into running line at Mandi Dabwali (MBY)	26866		
24.	16	-	Jatusana~~Provision of development for traffic facilities at Jatusanan station (JTS).	276152	0	
25.	16	-	Ratangarh kanakwal~~Expansion of traffic facilities in RKK yard for smooth movement of HMEL traffic.	328594	0	
26.	16	-	Suratgarh~~Developme nt of Goods shed of Suratgarh Jn. Station.	26668	0	30%

27.	16	-	Provision of Buzzer/Alarm system to alert SM to set points against occupied line(122 station) over Bikaner division.	10640	8255	
28.	16	-	Hanumangarh jn~~Provision of Running room at Hanumangarh Jn. station located on BTI-SOG section.	23635	0	
29.	16	-	Jharli~~Provision of Running room at Jharli station located on RE-BNW section.	26144	0	12%
30.	16	-	NEW COACH CARE COMPLEX AT KHATIPURA.	2047837	23978	
31.	16	-	Development GOODS SHED SIDING AT KHORI	131447		
32.	16	-	Jaipur~~Phulera ADEN (Line)~Providing W beam Crash barrier fencing & pedestrian Sub Way by RCC Box size 2.5 m X 2.5m (06 Nos.) (Total 20K	191996	0	
33.	16	-	Jaipur~~Phulera~ADEN (Line)~Prov. PRCC Pillar & 03 PRCC panel B/Wall up to 1.50 height in c/w speed 130kmph on Main line B route.(Total Km 60.60)	333601	0	
34.	16	-	Jaipur~~Bassi~~Providing W beam Crash barrier fencing & Provision of pedestrian Sub Way by RCC Box size 2.5 m X 2.5m (02Nos.) Total 20KM.	134563	0	
35.	16	-	ADEN-BKI- Providing W beam Crash barrier fencing (20km)& Provision of pedestrian Sub Way by RCC Box size 2.5 mx2.5m (11Nos.) in C/with speed 130kmph.	288672	0	
36.	16	-	Jaipur~Bassi~Providing PRCC Pillar & Three PRCC panel Boundary wall up to 1.50 height	102616	0	

			on Main line B route Bet Km 216.2 to 241.00Km (total16.70Km.)			
37.	16	-	BKI to BAI section- Providing PRCC Pillar & Three Precast RCC panel Boundary wall up to 1.50 height in connection with speed 130kmph (90kms)	566416	0	
38.	16	-	AWR - BKI section.- Providing PRCC Pillar & Three Pre cast RCC panel Boundary wall up to 1.50 height in connection with speed 130kmph (90kms)	574229	0	
39.	16	-	ADEN-AWR - Providing W beam Crash barrier fencing(20 kms) & pedestrian Sub Way by RCC Box size 2.5 m X 2.5m (08Nos.) in c/with speed 130kmph.	230666	0	
40.	16	-	PSL to AWR section. - Providing PRCC Pillar & Three Pre cast RCC pannel Boundary wall up to 1.50 height in connection with speed 130kmph (6.70kms)	36883	0	
41.	16	-	RE to PSL section- Providing PRCC Pillar & Three Pre cast RCC pannel Boundary wall up to 1.50 height in connection with speed 130kmph (90kms)	495447	0	
42.	16	-	Phulera~Madar Jn.~Prov. W beam Crash barrier fencing & pedestrian Sub Way by RCC Box size 2.5 m X 2.5m (08Nos.) (Total 8.80Km)	188115	0	
43.	16	-	Phulera~Madar Jn.~Pro. PRCC Pillar & Three PRCC panel Boundary wall up to 1.50 height in c/w speed 130kmph on Main line (Total 51.30 Km.)	282405	0	

44.	16	-	Nizampur~~NIP goods she developed by extend of siding	79560		
45.	16	-	Additional loop line at BNWS	140791	0	0
46.	16	-	Kanakpura~~KKU line no 1 and 2 required Common loop with reception and dispatch facility and line no. 2 and 5 required siding about 100 meters	104921	0	0
47.	16	-	Provision of Safety Point reversal Audio-Visual alarm unit generated as networked through Datalogger on stations of Jaipur Division.	6014	4318	85%
48.	16	-	Provision for Development of Goods Shed at CHILLO station of MTD-BKN section.	42107	0	
49.	16	-	Provision for Extension of Line No. 01 by 250 meter of SANU station towards LANELA end.	41009		
50.	16	-	Ashapura gomat~~Ashapura gomat~~yard remodelling work.	137753	0	
51.	16	-	JU yard remodeling along with extension of platform no. 05 and construction of new platform on line no.7	324713	0	
52.	16	-	Luni~~Marwar jn.~~Marwar jn.~~Provision of double distant signals in Luni(excl)-Marwar(excl) section of Jodhpur division)	26095	0	80%
53.	29	PB-75	North Western Railway - Interlocking of level crossing gates as per codal provision (PB#109/NCR/2023-24)	280000	0	
54.	29	PB-76	North Western Railway - Signalling work for improving Reliability at Level crossing gates (PB#76/SWR/2023-24)	500000	0	

55.	29	PB-77	North Western Railway - Improvement of civil infrastructure at LC gates (PB#104/ER/2023-24)	250000	0	
56.	29	-	Repl of Mech Lifting Barriers by provision of Elec Lifting Barriers at 29 nos. of manned LC over AII Div of NWR	24913	0	30%
57.	29	-	Provision of Auxiliary transformer supplies for signalling system at various locations over Ajmer Division of NWR	3400	0	0
58.	29	-	AII Div.: Provision of Interlocking of 01 Nos. manned LCs over Ajmer Division NWR having TUV> 20000.	11744	0	40%
59.	29	-	Replacement of Over-aged cum outlived ELB gates over Bikaner Division.	27859	0	
60.	29	-	Replacement of (MLB) by provision of (ELB) at 15 Nos. of manned level crossing gates over BKN	38707	0	
61.	29	-	BKN Division - Provision of secured communication equipment voice logging between level crossing gates and station master as per RDSO specification	20985	0	90%
62.	29	-	Provision of RTU at 14 nos. mid-section Interlocked LC-gates and large format display of DLMC system with E-1 networking over Bikaner division.	24127	0	
63.	29	-	Provision of Double boom arrangement on LC 41(BNLW-CHNN) & LC-3 (RE) of Jaipur division.	26750	0	0
64.	29	-	Provision of Remote Terminal Data Logger unit at 18 Nos. Mid Section Interlocked LC Gates over Jaipur	25813	0	25%

			Division.			
65.	29	-	Provision of Auxiliary transformer supplies for signaling system at various Locations over Jaipur Division.	21884	0	50%
66.	29	-	JP Division - Improvement road surface at high road traffic LCs within city limits with Rubberized road surface at 10 LCs in JP-SWM & JP-RE.	24123	0	
67.	29	-	ADEN (SIKAR) Sub Division:- Improvement to road surfacing & gate lodges etc. (33 LCs)	24927	0	
68.	29	-	JP Div. – Up Gradation of LC's from A, B, B-1 & C to SPL Class =16 and C, B-2 to A=20 and C to B-I, B-2 class = 4 (Total 40 No.)	22016	0	
69.	29	-	Provision of Interlocking of 13 Nos manned LCs over Jodhpur Division having TUV >20000.	165076	3513	
70.	29	-	Provision of Auxiliary transformer supplies for signalling system at various locations over Jodhpur Division.	66025	0	
71.	29	-	Replacement of Over-aged cum outlived ELB gates over Jodhpur Division.	13664	3808	
72.	30	PB-99	Jodhpur Division - Road under bridges in lieu of level crossings (36 Nos)	393277	94227	6 LHS Work has been completed. 3 LHS found feasible & work in progress.
73.	30	PB-96	Udaipur-Himmatnagar - Road under bridges at different level crossing (52 Nos)	772995	714587	Work has been completed.(2 nos LHS not feasible). Financial liabilities are pending.
74.	30	PB-91	Bhatinda-Hissar-Rewari - 2-lane road over bridge in lieu of level crossing No.C-100	457607	170801	Work has been completed in Oct.21. Financial liabilities are pending.
75.	30	PB-90	Bhatinda-Hissar-Rewari - 2-lane road over bridge in lieu of level crossing No.C-80	385963	88319	Work has been completed. Financial liabilities are pending.
76.	30	PB-89	Bhiwani-Hissar - 2-lane road over bridge in lieu of level crossing No.C-	569516	170019	ROB with RUB completed. Financial liabilities are balance.

			54A			
77.	30	PB-88	Madar-Palanpur - 2-lane road over bridge in lieu of level crossing No.C-81	441554	64600	ROB completed in Dec.20. RUB Completed in June 21. Financial liabilities are pending.
78.	30	PB-87	Madar-Palanpaur - 4-lane road over bridge in lieu of level crossing No.104, 53 & 88	1694939	403561	ROB No. 53,104 Completed.(Work executing by Other agency) ROB no 88- Crash barrier work in progress. Approaches almost completed.
79.	30	PB-85	Madar-Palanpur - 2-lane road over bridge in lieu of level crossing No.132	287987	40000	Rly Portion:- ROB has been completed in Nov 23 and RUB NIT discharged.
80.	30	PB-85	Rewari-Jaipur - Road over bridge in lieu of level crossings142,156,175,206(4 Nos) (2-lane) & (1 No) 211 (4-lane)	2396584	1245471	ROBs at LC-206,211,156 & 175 Completed LC-142-ROB completed on 31.03.2024. LC physically closed in March 2024.
81.	30	PB-84	Ajmer Division - Road over bridges with subways in lieu of level crossings 44,108,18,72,43 & 74 (6 Nos)	2398400	420180	ROB at LC-72,43X Completed LC-74 not Feasible Work Dropped by State Govt. ROB 18 -"Rly portion- Pier and Pier cap completed. Bow String Girder (54.0m) fabrication & Painting work completed. Launching scheme approved on 07.06.2024.Foundation for temporary works for Launching of BSG is under Progress. On Approach RE panel, Earth work in progress, LC Shifting & diversion road work completed." I) ROB-44 -"Rly portion- Work not started, stopped since Oct 2021. Approaches -90
82.	30	PB-83	Rai ka Bagh Palace-Jaisalmer - Road over bridge in lieu of level crossings (3 Nos) 8,18,23 & Samdari-Bhildi - level crossings (3 Nos) 48,56,109	2329123	324304	ROBs at RKB-JSM - (3 Nos) 8, 18, 23 & SMR-BLDI (3 Nos) 48,56,109 (i) ROB at LC no. - 8, 18, 23 work have been dropped by State Govt. or not feasible. (ii) ROB 56:- ROB complete in Aug.21. RUB Completed in 2022. LC closed. (iii) ROB 109:- ROB complete IN April-22. (iv) ROB at LC No 48-The work of 2 lane ROB has been deferred by State Govt. However, now LC on NH as road upgraded to NH. ROB work to be taken up by MORTH/NHAI.4 ROB deferred by STATE Govt.
83.	30	PB-	Sikar-Loharu - Road	1004077	687245	29 LHS completed, 13 LHS not

		82	under bridge at level crossings (42 Nos)			feasible,3 nos. LHS not feasible earlier, are converted into feasible after joint survey.
84.	30	PB-81	Ajmer Division - Road under bridges at level crossings (65 Nos)	977283	637289	8 RUB earlier Completed,14 in progress (Box casting in progress) 13 no RUB box has been launched. In joint feasibility report 9 nos. RUB not feasible.
85.	30	PB-81	Phulera-Madar - 2-lane road over bridge & 2 lane road under bridge in lieu of level crossing No.32	480771	114553	ROB Completed. Financial liabilities are pending.
86.	30	PB-80	Bandikui-Jaipur - 4-lane road over bridge in lieu of level crossing No.200	391057	126610	ROB completed in Nov.21. RUB-GAD/TAD Approved. Box casted, Launching to be done . LC not closed. No work at site. TWO under Review after observations from JP Division. Land required for work. Letter written by DYCE/C-IV to JDA on 06.10.2023 for working space for cranes. RUB Boxes ready at site for launching.
87.	30	PB-80	Phulera-Merta Road - Road under bridges in lieu of level crossings (74 Nos)	2143708	1348179	43 LHS Work has been completed. 19 Not feasible. 9 Nos. LHS found feasible. 8 No LHS work in progress
88.	30	PB-79	Bikaner Division - Limited height subways in lieu of level crossings (66 Nos)	1133087	633596	LC-8-I, LC closed 19.02.2024. LHS completed in March 2024.52 no's LHS completed earlier,13 no's LHS are not feasible
89.	30	PB-78	Sikar-Loharu - Limited use subways in lieu of level crossings (51 Nos)	752588	581668	Three new LHS LC-218-Box casted. Launched on 11.02.2024. LC closed in feb 24. LC-259-Land acquisition involved.20E notification published in Gazette for land acquisition . GAD approved, for TAD , CBE office observation sent to DyCE/C-IV/JP. Boxes have been casted on 15.04.2024. Shifted location.LC-262-GAD-Approved. "Box has been launched on 04.02.2024. LC Closed in Feb 2024. In Approaches R/wall work is in progress."
90.	30	PB-77	Luni-Munabao & Samdari-Bhildi - Road under bridges (71 Nos)	672578	554736	13 nos LHS completed, 11 LHS not feasible. Work is in progress on 5 LHS. at 02 LHS box has been erected. work in progress,
91.	30	PB-76	Rai ka Bagh-Jaisalmer & Jodhpur-Marwar - Limited height subways	1511924	778699	At 33 LHS work has been completed. 30 LHS not feasible. Work is in progress. work in

			at level crossings (78 Nos)			progress on 7 LHS.
92.	30	PB-75	Merta Road-Bikaner - Road under bridges in lieu of level crossings (66 Nos)	1609104	1E+06	47 completed 15 not feasible. Work is in progress at 3 LHS. in 2 LHS box erected. Approach work in progress
93.	30	PB-74	Rani-Keshavganj & Swarupganj-Palanpur - Road under bridges in lieu of level crossings (43 Nos)	1009153	832744	PB-93 Work completed partially (2 LHS not feasible. Financial liabilities are pending.
94.	30	PB-73	Jaipur-Ringas-Sikar-Churu - Limited use subways in lieu of level crossings (71 Nos)	1217028	1060247	Work has been completed. One LHS found feasible at LC-36 in SIKR-CUR Section.GAD under Approval. CBE observation Sent to Dy.CE/C/IV/JP on 19.06.2023. NOC ISSUE.
95.	30	PB-72	Madar-Palanpur - 2-lane road over bridge in lieu of level crossings (7 Nos) LC No. 1,2,70,74,75,105 & 153	2246408	353251	DFCCIL ROBs at LC No. 70,74,75,105,153 have been completed, which are executed by DFCCIL & ROB at 1,2 are being executed by RSRDC (Rajasthan Govt.) (i) ROB 1 :- "Both side in approaches road work & PSC Girder Launching in progress, RE Wall work in both side is in progress (ii)ROB-2-"Steel girder at site. Pier caps cast wrongly removed revised design Approved on 10.11.2023. Launching scheme not submitted. . ROB Work stopped. Approx.. work completed except
96.	30	PB-71	Luni-Munabao & Samdari-Bhildi - Road under bridges in lieu of level crossings (79 Nos)	1415733	575709	(PB-84) 20 LHS feasible out of 79 LHS. at 16 LHS Work have been completed, 3 LHS not feasible. at 1 LHS on LC no.288 Launching done on 07.11.2023. Approach work in progress. LC Closed on 0.11.2023. One approach completed. Other side /wall in progress.
97.	30	PB-70	Rewari-Ringus-Phulera-Madar - Road over bridges (5 Nos) in lieu of LC No. 72,85,102,249 & 5	1596934	478270	DFCCIL & PWD/Raj 4 ROB Completed out of 5 LC 249-"Rly Portion:- Sub str work to be started. Design of R2 pier approved. On Approaches:- One side (Balaji) approach work complete, other side in progress. LA award issued, payment &

						possession work of land in progress, RE wall work started this side. Cable shifting agency has been terminated. Work has been stopped. Retender done by state Govt. Revised GAD Approved in March 2023.
98.	30	PB-69	Rewari-Ringus-Phulera-Madar - 2-lane road over bridges (5 Nos) in lieu of LC No. 18,30,39,42 & 53	1586937	85310	Work has been completed. Financial liabilities are pending.
99.	30	PB-127	Bhatinda-Suratgarh - 4-lane road over bridge in lieu of level crossing No.70(T) (PB#147/2018-19/NWR)	1326390	0	ROB- GAD approved. State Govt. has deferred the work due to non availability of fund. RUB- State Govt. has deferred the work due to non availability of fund.
100.	30	PB-126	Rewari-Jaipur- Road over bridge in lieu of level crossing No.140 at Rajgarh (PB#147/2018-19/NWR)	425998	62	ROB- Work delayed due to court case , Court stay vacated. LC closed on 19.02.2024.RUB- RUB GAD Not submitted By PWD/Raj.
101.	30	PB-125	Rewari-Hisar - Road over bridge in lieu of level crossing No.52 at km 81/9-82/0 (PB#147/2018-19/NWR)	432205	97707	"Rly portion:- . Launching done on 11.03.2023. Deck slab casting completed, Road &Crash barrier remaining. In approaches one pile cap is balance due to infringement of sewer line. RE wall work not started yet by PWD/Haryana. Work delayed due to court case , Court stay vacated." LC closed on 19.02.2024.
102.	30	PB-124	Rohtak-Bhiwani - Road over bridge in lieu of level crossing No.45 at km 40/8-9 (PB#147/2018-19/NWR)	286244	118711	ROB-"Rly Portion :- Girder launching done, and deck slab completed, crash barrier completed and Road work balance. In Approaches:- 10 span Girder has been launched out of 10 span. Deck slab in progress (10/10). RE work 85% completed.
103.	30	PB-123	Rewari-Bhatinda - Road over bridge in lieu of level crossing No.27 at km 41/4-5 (PB#147/2018-19/NWR)	425183	170992	ROB completed in Jun-24 RUB-GAD Approved. Box inserted on 12&13.12.2023. LC will be closed after commissioning of ROB.
104.	30	PB-122	Rewari-Bhatinda - Road over bridge in lieu of level crossing No.114 at km 172/1-2	272068	119131	LC closed in Oct 2023. ROB completed in Jun-24.financial liabilities are pending

			(PB#147/2018-19/NWR)			
105.	30	PB-121	Rewari-Bhatinda - Road over bridge in lieu of level crossing No.96 at km 140/0-1 (PB#147/2018-19/NWR)	283711	0	Draft GAD-HQ observations yet not submitted by PWD/Haryana since 16.11.22 Reminder sent on 04.05.2023. RUB not feasible due to High water table. GAD-HQ observations yet not submitted by PWD/Haryana since 16.11.22 Reminder sent on 04.05.2023.GAD submitted to HQ on 22.05.24 after compliance of the observations. sent to CBE office on 21.06.24.
106.	30	PB-120	Rewari-Jaipur- Road over bridge in lieu of level crossing No. 61 (Anajmandi Rewari) (PB#147/2018-19/NWR)	715736	277749	ROB-Rly Portion:- Pile cap, piers ,Pier cap completed. Trial assembly inspection has been done by RDSO. Girder fabrication completed and material received at site. On Approach:- .Rewari side Girder launched deck slab completed in all span. Sahjhapur side Girder launched deck slab completed in all span. ROB Launching scheme under approval in HQ. ROB work in Rly portion will be completed by 31.12.2024. Once the RUB work is completed in Rly portion , BSG launching work will be started.
107.	30	PB-118	Rewari-Bhatinda - Road over bridge in lieu of level crossing No.144 (PB#147/2018-19/NWR)	365089	0	PWD, Haryana has revised the Proposal from ROB to RUB. A ROB already existed nearby this LC, hence Haryana PWD proposed RUB instead of ROB. GAD of RUB approved .Detailed estimate and NIT under technical sanction. Tender to be floated by PWD after approval of detailed estimate and NIT.
108.	30	PB-117	Jaipur-Sawai Madhopur - Road over bridge in lieu of level crossing No.14	364800	0	Work is being Executed by PWD Rajasthan ROB & RUB, GAD approved Dec.20. State Govt. yet to sanction the work in State budget. Detail estimate vetted and sent to State Govt. for further necessary action.
109.	30	PB-116	Bandikui-Alwar & Agra Fort-Bandikui - Subways in lieu of level crossings (20 Nos.)	415811	259889	Work completed. Financial liabilities are balance. 10 LHS are not feasible out of 20 Nos.

110.	30	PB-115	Jaipur-Sawaimadhopur-Road over bridge in lieu of level crossing No.70 with subway at Sitapura	1466855	265287	ROB Work has been completed. Financial liabilities are balance.
111.	30	PB-114	Hisar-Jakhal- Road over bridge in lieu of level crossing No.C-89 & LC No. 60 (1 No.)	975468	244181	Rly portion :Rly portion: Pile cap completed, Pier completed (6/6), pier cap completed (6/6). Girder launching completed at ROB 89. Approaches Road work completed. adjacent span pending due to common pier. Girder Launching of LC 89 done on 23/04/24. and Launching scheme of LC 60 approved but launching delayed due to infringement of TRD feeder wire RUB @ 89 and RUB @ 60 Box Launched on 13.08.23 & 21.07.23 respectively. Both RUBs commissioned. U type wall in progress in Approaches:- 8
112.	30	PB-113	Sikar-Loharu- Road over bridge in lieu of level crossing No. 265	361226	39055	ROB- "Sub structure completed. Fabrication not started. In Approach. piers & pier caps, work has been stopped. Now no work at site. Launching scheme not submitted. Compliance of observations raised by RB on 01.05.2023 for revision of estimate not submitted by RSRDC/JJN." RUB-GAD & TAD not submitted by RSRDC.
113.	30	PB-112	Hisar-Bathinda- Road over bridge in lieu of level crossing No. C-112-A	500251	104903	Work has been completed. Financial liabilities are pending.
114.	30	PB-111	Phulera-Sambhar Lake-Road over bridge in lieu of level crossing No.1	712878	398993	Work completed. Financial liabilities are balance.
115.	30	PB-110	Rewari-Jaipur- Road over bridge in lieu of level crossing No. 69	361226	86391	Work completed. Financial liabilities are balance.
116.	30	PB-109	Rewari-Hisar- Road over bridge in lieu of level crossing No. C-76	594000	273083	ROB -Completed in Feb-23.LC closed in Mar 23 RUB-RCC box Casted & launched. On approaches work not started. GAD approved as part of GAD of ROB. .GAD submitted to Division on 07.12.22
117.	30	PB-106	Lalgarh Yard - 4-lane road over bridge in lieu of level crossing No.136	844860	240599	"Rly portion - 07 no's pier completed out of 12 Nos. On approaches - Girder launched (99/105), Deck slab completed except adjoining span and 2 span

						on which court stay. No work at site since April 22. Launching scheme of girder Approved. Tender re invited, open on 18.01.24 and under finalization."
118.	30	PB-100	Jodhpur Division - Limited height subways at level crossings (33 Nos)	550390	388348	29 LHS completed.2 NO LHS are feasible, . 2 LHS are not feasible. Work is in progress at 1 LHS
119.	30	LB-99	ADEN/ MJ Sub div - Aug works at RUBs i.e. Ht gauge, imp of drainage arrang, ext of ret walls and road approaches for exist RUB No. 76,78,79,80,82,83	22325	449	Items identified such as plugging of weep holes, tie rod holes, joint sealing, backfilling, retainin wall extension, road work etc were completed. Based on experience during monsoon some works are to be taken up. Final variation sanctioned and Final Bill with accounts for payment
120.	30	LB-97	ADEN/ ABR Sub div- Aug works at RUBsi.e. Ht gauge, imp of drain. arrang, ext of ret walls and road appr for exist RUB No.90,93,101,102,104, 107,109	17571	889	Items identified such as plugging of weep holes, tie rod holes, joint sealing, backfilling, retaining wall extension, road work etc were completed. Based on experience during monsoon some works are to be taken up. Work completed. Final Bill and variation awaited
121.	30	LB-96	Ext & raising of existing retaining wall & other ancillary works in various RUB's LC C-17,25,57/A,21,10,7,38, 39,43 ,52 ,48,49,1,2,27&28ADEN /Line,BKN	28884	15333	"Work completed. Final bill paid in March 22. Further, work is to be executed & accordingly revise estimate sanctioned. Contract for RUB no.11 awarded on 29.04.24. Work is in progress (10%).
122.	30	LB-95	ADEN/ MJ Sub div-Aug works at RUBs i.e. Ht gauge, imp of drainage arrang, ext of ret walls and road approaches for exist RUB 65,66,68,69,71,72,73	24355	714	Items identified such as plugging of weep holes, tie rod holes, joint sealing, backfilling, retaining wall extension, road work etc were completed. Based on experience during monsoon some works are to be taken up. Work Completed. Final Bill and variation awaited
123.	30	LB-94	ADEN/ MJ Sub div - Aug works at RUBs i.e. Ht gauge, imp of drainage arrang ext of ret walls and road app for exist RUB No. 52,56,57/A,58,61,62	22586	8111	Items identified such as plugging of weep holes, tie rod holes, joint sealing, backfilling, retaining wall extension, road work etc were completed. Based on experience during monsoon some works are to be taken up. Sump work completed at RUB no 57A, Pond work completed at RUB no 62.Final variation and Bill Passed. GST Reimbursement under process.

124.	30	LB-93	ADEN/ MJ Sub div- Aug. works at RUBs i.e. Ht gauge, imp of drainage arrang, ext of ret walls and road appr for exist RUB No. 40,41,44,45,46,47,51.	21942	5420	Items identified such as plugging of weep holes, tie rod holes, joint sealing, backfilling, retaining wall extension, road work etc were completed. Based on experience during monsoon some works are to be taken up. Sump work completed at RUB no 46. Work of Sump completed at RUB 45. Work Completed, Final variation sanctioned. Final bill Awaited
125.	30	LB-92	ADEN/MJ Sub div- Augworks at RUBs i.e. Ht. gauge, imp. of drainage arrang. ,ext. of ret. walls and road approaches for exist RUB No.39,42,43,49,50,54	13446	8575	Items identified such as plugging of weep holes, tie rod holes, joint sealing, backfilling, retaining wall extension, road work etc were completed. Based on experience during monsoon some works like sump were taken up and completed at identified RUBS. Work completed. Final bill passed, GST reimbursement Bill passed, Proposed for Deletion, CR Awaited
126.	30	LB-91	Additional work on RUBs at L.C. NO 17,33,35,36,46,47A on RKB-JSM section for etc under ADEN- JSM	59141	59141	Work completed. Final bill & Final PVC Bill passed.PG Release.SD/EMD to be release
127.	30	LB-86	Extension & raising of retaining wall RUB covering & other works to prevent entrance of rain water in RUB No.- 39A & 41A on BTI-SOG	14659	0	Earlier contract short closed. Work is to be executed & accordingly estimate revised. Tender opened on 25.08.22 & awarded on 27.12.22 but terminated due to non submission of PG. Re-tender opened on 27.06.23 & awarded on 31.08.23.Work is in progress.
128.	30	LB-85	Ext. & raising of retaining wall with RUB covering & other works in RUB No.- 166A,167A & 174A on RMN-BTI and A-1 & 5A on BTI Bye-pass section.	24857	0	Earlier contract short closed. Work is to be executed & accordingly estimate revised. Tender opened on 25.08.22 & awarded on 27.12.22 but terminated due to non submission of PG. Re-tender opened on 27.06.23 & awarded on 31.08.23. Work is in progress.
129.	30	LB-84	Bathinda~~Suratgarh~ ~Ext. & raising of retaining wall with RUB covering & other works in RUB No.- 15A, 15AB, 16A & 16AB on BTI-SOG section.	24900	1347	Earlier contract short closed. Work is to be executed & accordingly estimate revised. Tender opened on 25.08.22 & awarded on 27.12.22 but terminated due to non submission of PG. Re-tender opened on 27.06.23 & awarded on 31.08.23. Work is in progress.

130.	30	LB-83	ADEN/HQ/II/JP Sub divn. -Covering of approaches of RUB at LC no. 68, 74, 75, 76, 77& 66. Const. RCC retaining wall on RHS approach of LC no.66.	25270	24674	Work completed and final bill passed. May be deleted.
131.	30	LB-79	Ajmer division-Providing RUB (LHS) at LC no. 80, 82 & 93 in connection with	24966	16395	Work Completed. Party not signs Final Bill and Final variation due to measurement dispute. The matter sorted out with the agency. Final Variation vetted and sanctioned by CA. Final Bill Received from ADEN ABR and under process
132.	30	LB-77	Rewari~~Alwar~~Construction of ROB(2 lane) in lieu of L-xing no. 76 on Rewari-Alwar section.	364506	0	Required State Govt consent for execution of work by Rly on single entity basis.
133.	30	LB-76	Raising /Rebuilding of ROB No. 32B (02 Lane) at Km 81/0-1 between Rewari-Hisar section to facilitate running of Double Stack Container .	539594	69600	Pile work 44/196 is in progress.3 no's Pier completed, 03 no pier cap completed.
134.	30	LB-75	Proposed RUB of size 4.5x4.5m in lieu of LC-46 (T) at KM 55/6-7 on BTI-SOG section	59142	38614	RUB completed and opened for road traffic on 27.2.2024. LC closed on 02.03.2024.
135.	30	LB-74	Raising /Rebuilding of ROB No.76A (02 lane) at Km 137/2-3 between Rewari-Hisar section to facilitate running of Double Stack Container .	510594	0	GAD approved. Tender awarded. Structural Drg under approval in HQ. Launching scheme sent to DyCE/C/BKN with observation on 25.07.2023.CBE observation for alteration in GAD sent to Dy.CE/C-I/BKN on 12.10.23. For temporary LC ESP is in process.
136.	30	LB-73	Construction Of ROB in lieu of LC NO 168 (RTO Pathak) at Km 620/0-55 on JODHPUR-Merta Road Section. under cost Sharing basis	824526	30000	ROB completed. RUB not feasible due to water logging area. Financial liabilities are pending.
137.	30	LB-145	Provision of RUB size 4.5x4.5m in lieu of manned LC C-146 on SDLP-RTGH section	46238	27556	Work completed and opened for road traffic on 27.02.24 & LC closed on 04.03.24.
138.	30	LB-144	Makrana~~Degana~~Construction of ROB (2 Lane) in lieu of level crossing no.72 at Km	366146	37772	ROB- Work sanctioned under Umbrella work 2020-21 in Oct.2021, GAD - Approved on 06.07.23. Working pile in

			107/7-8 Bet. Ganchipur-Degana on MKN-DNA section			progress 80/118, Pile cap work started. Facia panel casting is in progress 550/1400. RUB: GAD CBE observation sent to DyCE/C on 27.03.2024. GAD sent to CBE on 13.06.24.
139.	30	LB-143	Merta road~~Bikaner~~Construction of ROB (2 Lane) in lieu of level crossing no.27 at Km 525/5-6 on MTD-BKN section	366146	0	ROB- GAD Approved on 14.02.2024. Tender awarded on 05.12.2023.Test pile work completed,, structural drg submitted by agency and under approval in Field unit. RUB:GAD under preparation.
140.	30	LB-142	Construction of ROB (2 lane) in lieu of LC-189 at km 234/7-8 bet. Ringus - Sikar section.	364506	17117	Work transferred from GSU/JP to Construction NWR on dated 23.07.24 Work sanctioned under Umbrella work 2020-21 in Oct.2021. Detailed estimate sanctioned. ENGG:- Work awarded on 05.10.2023. Test pile done. Structural drawings duly proof checked by MNIT, Jaipur submitted by CEG, Jaipur has been submitted to HQ on 12.03.2024 observations given by HQ on 12.04.2024. Another proof checking consultant engaged as per HQ instructions. 15 Nos box casted. Composite girder work is in progress. Service
141.	30	LB-141	Construction of ROB (4 Lane) in lieu of LC.No:-3 on RE-NNL line and LC. No: 59A (2 lane) on RE- SDLP sec	1354169	0	Rly Portion:- Tender Awarded. Test pile design approved, test piling start shortly.On approaches:- Tender Awarded by HSRDC. Test pile in progress."
142.	30	LB-140	Construction of ROB (02 lane) in lieu of LC No.146 spl at km 226/3-4 on Rewari-Bathinda section .	288060	0	GAD under approval. GAD return by HQ with observations on 06.10.2023 to Dy.CE/C/BKN.
143.	30	LB-139	Construction of ROB (02 lane) in lieu of LC No.11 at km 17/0-1 on Rewari-Hisar section ..	356532	0	GAD not finalized by PWD.GAD return by HQ with observations on 14.09.2023 to DyCE/C/BKN.
144.	30	LB-138	Construction of ROB (02 lane) in lieu of LC No.C-122 at km 188/0-1 on Rewari-Bathinda section .	274518	0	GAD not finalized by PWD.(ROB not feasible).(ROB not feasible as per Joint feasibility report). Re-feasibility to be check.

145.	30	LB-137	Construction of ROB (02 lane) in lieu of LC No.35 at km 56/2-3 on Rewari-Hisar section	297842	0	GAD Approved, estimate sanctioned for Railway portion.
146.	30	LB-136	Construction of ROB (02 lane) in lieu of LC No.19A at km 17/0-1 on Rohtak-Bhiwani section .	245068	0	GAD Approved, estimate sanctioned for Railway portion.
147.	30	LB-133	Additional work on RUBs at L.C. NOB1, B2 & 222 on LUNI- SMR section under ADEN-LINE	20805	13650	Work completed. Final bill passed. Final PVC Bill is under process. Work to be recommended for deletion on IRPSM.
148.	30	LB-130	Additional work on RUBs at L.C. NO 15, 16, 17 & 18 on PPR-BARA under ADEN-LINE	24001	20500	Work has been completed. Work recommended for deletion on IRPSM.
149.	30	LB-129	Additional work on RUBs at L.C. NO 11, 13 & 14on PPR-BARA section under ADEN-LINE	24900	19500	Work has been completed. Work recommended for deletion on IRPSM.
150.	30	LB-124	Additional work on RUBs at L.C. NO 4,5, 11 on LN -MJ section etc under ADEN- LINE	29559	29559	Work has been completed. Final liabilities are to be cleared.
151.	30	LB-123	Additional work on RUBs at L.C. NO 19,21,26,55 on RKB-JSM section etc under ADEN- JSM	18000	18000	Work completed. Final bill & Final PVC Bill passed.PG Release.SD/EMD to be release
152.	30	LB-119	Additional work on RUBs at L.C. NO16,32 & 34 on RKB-JSM section etc	29184	29184	Work completed. Final bill Passed.PG released.SD/EMD & Final PVC Bill to be paid.
153.	30	LB-117	JP Division: SIKR-LHU section:- Remedial actions required for miscellaneous deficiencies at existing 10 LHS no. 238, 246, 254, 256, 271.....	34822	23819	Work completed. Final bill Pass. Completion report certified by finance. Work may be deleted
154.	30	LB-110	ADEN/RPZ Sub division - Augmentation works RUB No.7,24,33 & 41 in BEC-UDZ Section	19800	10868	Physically work has been complete. Final variation vetted. Final bill passed work proposed for deletion.
155.	30	LB-109	ADEN/RPZ Sub division - Augmentation	23974	16439	Work completed. Final variation vetted. Under approval of TAA

			works RUB No.39,57,60,61,62,65 & 66 in BEC-UDZ Section			and ADRM.
156.	30	LB-108	ADEN/RPZ Sub division - Augmentation works at RUB No.3,4,5,6,8,10,16,22,23,26,27,28,29,30,42,44, 47,49,55 & 56 in BEC-UDZ Section	23716	21536	Physically work has been complete. Final variation vetted. Final bill passed work proposed for deletion.
157.	30	LB-106	ADEN/ L/Ajmer and ADEN/BHL Sub division - Augmentation works at RUBs No. 5, 11 & 18 in MD-MJ JN 27, 28 & 57 in AII-COR	24980	10267	Final Bill under passing status.
158.	30	LB-102	ADEN/ MJ & ABR Sub div - Aug works at RUBs i.e. Ht gauge, imp of drain arran, ext of ret walls and road appr for exist RUB No. 55,60,67,77,160	16098	5519	Items identified such as plugging of weep holes, tie rod holes, joint sealing, backfilling, wall extension etc were completed. Based on experience during monsoon some works are to be taken up. Sump work completed at RUB no 55. Final Bill and variation awaited
159.	30	LB-100	ADEN/ MJ Sub div - Aug works at RUBs i.e. Ht gauge, imp of drain arrangement, ext of ret walls and road appr for exist RUB No. 84,85,86,87,89	15679	6917	Items identified such as plugging of weep holes, tie rod holes, joint sealing, backfilling etc were completed. Based on experience during monsoon some works are to be taken up. Final variation sanctioned and Final Bill with accounts for payment
160.	30	-	Sub Work for ROB in lieu of LC No.1, KM 2/3-4, in AII-COR & LC No. 50, Km 296/8-9 in MD-PNU section	653941	0	Work Transferred to construction (Dy.CE/C/I/AII) new work
161.	30	-	Sub Work for ROB in lieu of LC No.3 at KM 4/8-9 (TVU = 232016) in AII - AHO Section.	593400	0	Work has been transfer to Ajmer division.
162.	30	-	ADEN/Ranapratnagar : - Provision of Covering Shed at RUB on old LC-33 in BSJ Yard	6034	1936	Detail Estimate sanctioned. LOA has been issued on 27.12.22. Work completed and final variation approved. Final bill in process.
163.	30	-	ADEN-L-Aii Sub Div. Ajmer-Providing covering shed at RUB at LC 25, I.R. Side.	8998	1442	Final bill sent to Division
164.	30	-	ADEN-L-Aii Sub Div. Ajmer-Providing covering shed at RUB no.3, I.R. Side.	12609	9858	Work physically completed and Final bill sent to division

			between Ajmer-DOZ stations.			
165.	30	-	ADEN-L-Aii Sub Div. Ajmer-Providing covering shed at RUB at LC 42, on I.R. Side.between Madar-Ajmer stations.	11483	11483	work physically completed and final bill sent to Division
166.	30	-	ADEN/Ranapratnagar : - Provision of Covering Shed at RUB on old LC-41 between BSJ-FAN	19844	19844	Detail Estimate sanctioned. LOA has been issued on 27.12.22. Final bill in process.
167.	30	-	Ajmer-Chittourgarh-Provision of RUBs at LCs No. 4, 24, 29, 50 , 76 & 79	387566	0	NOC received for 24, 50 & 79 and NOC awaited for remaining LCs. GADs have been prepared for the LCs where NOCs are received.
168.	30	-	Ajmer- Chittaurgarh - Provision of RUB with Covering shed (4m x2.5m)- Twin box at LC no 41, km 65/2-3 in AII-COR section.	66608	0	NOC awaited from State authorities.
169.	30	-	Construction of RUB at LC No.70/C Bet. BHL-MDPA	44703	0	LOA issued on 03.01.2024 and work is under progress.
170.	30	-	Provision of RUB at Closed LC No.-53 at Km. 414/3-4 and Closed LC 104 at KM 555/4-5 with covering shed in HP-PNU Section	113640	0	Work transfer to GSU on 04/03/2024. Work again transferred to Div. GAD under preparation
171.	30	-	BAR-HP Sec-Provision of RUB (1X4.5mx4.0m)along with covering shed drainage system in lieu of LC no.36 km 372/9-373/0	59173	0	Work transfer from GSU to division in June-24. Detailed Estimate vetted by accounts on date 01.08.2024, Estimate Sanctioned on 05.08.24, NIT in process
172.	30	-	Provision of RUB (5.0 x 2.50m) at Km. 108/9 to 109/0 in BEC-UDZ Section	35000	0	New work sanctioned. GAD and Detail estimate under preparation.
173.	30	-	Provision of RUB (5.0 x 2.50m) at Km. 103/9-10 in BEC-UDZ Section	40000	0	New work sanctioned. GAD and Detail estimate under preparation.
174.	30	-	Provision of RUB (5.0 x 4.0m) at Km. 197/5-6 in UDZ-HMT Section	49999	0	New work sanctioned. GAD and Detail estimate under preparation.
175.	30	-	Providing covering shed at RUB no. 105,138,139 on IR side	20794	0	Detail Estimate Sanctioned. NIT issued, under TC

			in MD - PNU Section			
176.	30	-	Providing covering shed at RUB no. 50,90,103 on IR side in MD - PNU Section	23102	0	DE Sanctioned on date 21.05.2024, NIT issued, Under TC
177.	30	-	Providing covering shed at RUB No. 649 A in UDZ-HMT Section	8720	0	Detail estimate sanctioned. Revised estimate under vetiing with self supporting roofs. LOA issued on 03.07.24.
178.	30	-	Providing covering shed at RUB no. 146 on IR side in MD - PNU Section	9047	0	Detail Estimate sanctioned, Tender Opened, LOA issued on 28.11.2023, Drawing of covering shed approved
179.	30	-	Providing covering shed at RUB no. 118 on IR side in MD - PNU Section	6448	0	Detail Estimate Sanctioned, Tender Opened, Under TC, Discharged, Reinvaded, opened and LOA issued, work commenced
180.	30	-	Providing covering shed at RUB no. 67 on IR side twin Box in MD - PNU Section	6488	0	Detail Estimate Sanctioned on 21.08.2023, Tender Opened, Under TC, Discharged, Reinvited , opened and LOA issued, Work in Progress
181.	30	-	Providing covering shed at RUB no.31 on IR side in MD-PNU section.	8297	0	Detailed estimate sanctioned, Tender Opened, LOA issued on 28.11.2023, Work in progress
182.	30	-	Madar Jn.~~Palanpur~~Providing covering shed at RUB no.4 on IR side in MD-PNU section.	7220	0	Work awarded on 29.11.2023. Work is in progress.
183.	30	-	Prov. covering shed at RUB no. 7 on IR Side in MD-PNU sec.	9450	0	Detailed Estimate sanctioned and work awarded on 29.11.2023. Work is in progress.
184.	30	-	Providing covering shed at RUB No. 810 A in UDZ-HMT Section	9168	0	Detail estimate sanctioned. Revised estimate under vetting with self supporting roofs.LOA issued on 03.07.24.
185.	30	-	Sadulpur~~Ratangarh jn~~Construction of ROB (04 lane) in lieu of LC No.167-A at km 282/3-4 in between Churu-Depalsar block section	979482	0	Tender under finalization.
186.	30	-	Construction of ROB(2 Lane) in lieu of L. Xing No:- 78 at Km:- 105/4 - 5 on RE-SDLP section.	477826	0	GAD under preparation. Now ROB is being considered instead of LHS as TVU is more than 1 Lakh at this LC.LHS not feasible.

187.	30	-	Rebuilding of ROB 04 lane at Km 143/0-1 at Hisar yard for removing vertical infringement .	866282	0	New work ROB sanctioned in Umbrella work 2022-23. vide CE/RSW letter dated 11.07.2023
188.	30	-	Construction of RUB of size 5.00m x 4.00m in lieu of LC no. 83-II at Km 118/3-4 on Bathinda-Suratgarh section over Bikaner division.	66064	0	Work sanctioned on 21.12.23. Detail estimate sanctioned on 10.06.24. Tender opened on 05.07.24 & under TC.
189.	30	-	Construction of RUB of size 4.50m x 4.50m in lieu of LC no. 113 at Km 174/0-1 on Suratgarh-Lalgarh section over Bikaner division.	83664	0	Work sanctioned on 18.01.2024. Detail estimate sanctioned on 01.04.24. Estimate Revised. Tender opened on 02.07.24 & under TC.
190.	30	-	Construction of RUB of size 4.50m x 4.50m on trespassing location at Km 230/3-4 in Suratgarh - Lalgarh section over Bikaner division.	71952	0	Work sanctioned on 07.02.24. Detail estimate sanctioned on 06.05.24. Tender opened on 24.06.24 & under TC.
191.	30	-	Construction of RUB of size 5.00m x 4.00m on trespassing location at Km 61/6-7 in Bathinda - Suratgarh section over Bikaner division.	65343	0	Work sanctioned on 07.02.24. Land aquisition required and estimate for the same is awaited. Detail estimate under preparation.
192.	30	-	Construction of RUB of size 2 x 4.0 x 4.5 M in lieu of LC No.36 at km 54/8-9 on Sarupsar - Sriganganagar-Hanumangarh (CLL) section over BKN div.	106967	0	Work sanctioned on 16.03.2024. Estimate sanctioned on 22.07.24. Tender to be opened on 06.09.24.
193.	30	-	Extension & raising of existing retaining wall & other works to prevent entrance of rain water in various RUB's in the jurisdiction of ADEN/HMH-II	8588	0	Work sanctioned on 12.10.23. Contract awarded on 29.04.24. Work is in progress.
194.	30	-	Jaipur~~Phulera~~JP Division- Providing ROB in lieu of LC at LC no. 245 bet. Jaipur-Phulera at km 284.06 Four lane.	727445	0	New work , ROB sanctioned in Umbrella work 2022-23. vide CE/RSW letter dated 11.07.2023. A & F sanction to be taken by state govt.
195.		-	JP Division- Providing ROB in lieu of LC at LC no. 222 bet. Gandhi	613096	0	LC closed on 31.01.2024 " Railway portion:- Revised GAD

			nagar - Jaipur at km 239/5-6 Four lane.			approved. Substructure Design approved. Pilling work in progress 13/20. Approach:- Piling work, RE wall, Pier, Girder Launching work is in progress.
196.	30	-	Rewari~~Ringas~~Sr. DEN (N) JP Div.: Construction of RUB at LC No.-13 (Box Size -2 x 3.50 x 2.75) at Km. 16/5-6 between RE-PALI Sections.	81666	49960	ENGG- Work completed. Final bill passed. S&T:- Work completed and Final bill sent to Accounts.
197.	30	-	JP Division- Providing ROB in lieu of LC at LC no. 243 bet. Jaipur-Phulera at km 277/9-278/0 (Four lane)	821674	0	Work is being executed by PWD Rajasthan. GAD approved. State Govt. yet to sanction the work in State budget.
198.	30	-	ADEN (RGS) JP Sub. Division – Improvements of drainage system at for existing LHSs at old LC 70,75,116 in RPC section	9500	0	Work In Progress.
199.	30	-	ADEN (RGS) JP Sub. Division – Improvements of drainage system at for existing LHSs at old LC 104, 80, 81 & 88 in RPC section	9000	0	Work In Progress.
200.	30	-	ADEN (RGS) JP Sub. Division – Improvements of drainage system at for existing LHSs at old LC 26, 57&60 in RPC section	9000	5486	Work In Progress.
201.	30	-	Chaksu~~Sawaimadhopur~~Sawaimadhopur~~ADEN/Line/JP Sub division:- Protection of Leakage and Seepage treatment in segmental at LHS	9933	0	LOA issued on 06.12.23. WIP
202.	30	-	Phulera~~Renwal~~ADEN/FL Sub division:- Protection of Leakage and Seepage treatment in segmental joints and RCC joints at LHS	9963	7147	Work awarded. Work is in progress.

203.	30	-	Phulera~~Ladpura~~ADEN/FL Sub division:- Protection of Leakage and Seepage treatment in segmental joints and RCC joints at LHS(No.2,4,7,8,9	9989	3030	Work is in progress.
204.	30	-	Phulera~~Ladpura~~Ladpura~~Ladpura~~Ladpura~~ADEN/FL Sub division:- Protection of Leakage and Seepage treatment in segmental joints	9028	0	Work awarded. Work is in progress.
205.	30	-	Construction of 2 lanes ROB in lieu of existing LC no.-269 at km 304/5-6 bet. SIKR - LHU section.	430295	0	new work, ROB sanctioned in Umbrella work 2023-24. vide CE/RSW letter dated 05.12.2023.Tender floated for FLS.
206.	30	-	Rewari~~Alwar~Cons of 2 lane ROB with LHS (Internal Size 4m X 4.50m) along with proper drainage in lieu of Existing LCs no. 93 in RE-AWR.	479850	0	New work, ROB sanctioned in Umbrella work 2023-24. vide CE/RSW letter dated 05.12.2023.Tender floated for FLS.
207.	30	-	Jaipur~~Sawaimadhopur~~JP Div.: Construction of 2 lane ROB in lieu of Existing LCs no. 78 in SWM-JP section.	417458	0	New work, ROB sanctioned in Umbrella work 2023-24. vide CE/RSW letter dated 05.12.2023. Tender floated for FLS.
208.	30	-	Construction of 2 lane ROB with LHS (Internal Size 4m X 4.5m) along with proper drainage arrangement in lieu of Existing LCs no. 73 in SWM-JP.	472022	0	New work, ROB sanctioned in Umbrella work 2023-24. vide CE/RSW letter dated 05.12.2023.FLS tender floated.
209.	30	-	Sr. DEN/HQ/JP section- Construction of RUB/LHS of size 2X7.50mX5.00m for augmentation of Br. No.74 (Existing LHS at SH-12 Diggi-Malpura Road).	98694	0	LOA Issued, GAD & TAD approved. Work being started. Design of thrust bed and RRC box approved. Utility shifting is being done & Work is being started
210.	30		Bandikui~~Madar Jn.~~Construction of 06 Nos. LHS in lieu of existing LCs no.205, 208, 209, 210, 1 & 235	299308	0	Tender for LC 1 & 235 under Sr. DEN(S)/JP has been opened and work awarded and other LC under Sr. DEN(HQ)/JP Tender opened on 19-6-24 and under

			with covering shed over JP Division.			finalization
211.	30	-	Construction of 09 Nos. LHS in lieu of existing LCs no. 165, 167, 176, 184, 185, 187, 191, 192 & 199 with covering shed over JP Division.	512841	0	LOA issued on 15.07.2024
212.	30	-	Construction of 09 Nos. LHS in lieu of existing LCs No. 98, 99, 102, 105, 106, 107, 109, 130 & 163 with covering shed over JP Division.	512911	0	LOA issued on 15.07.2024
213.	30	-	Construction of 09 Nos. LHS in lieu of existing LC no. 95, 190, 114, 66, 78, 80, 81, 88 & 97 with covering shed over JP Division.	512817	0	LOA issued on 15.07.2024
214.	30	-	Construction of Pedestrian Subway (Size- 4.00 m x 2.50m) with proper drainage arrangement and covering shed near of dabla station in rewari end.	54309	0	Estimate under preparation.
215.	30	-	Rewari~~Madar Jn.~~JP- Preparation & Submission GAD of minor bridges .Preparing Building lay outs plans & drawing of level crossing & land plans etc.	3596	0	Detailed estimate under process.
216.	30	-	ADEN (HQ)II Sub Division:- Remedial actions and ancillary works required for miscellaneous deficiencies at existing LHS no. 75,59,76,209-A,66	10677	0	LOA issued on 29/01/2024. Work is in progress,
217.	30	-	Various type of improvement works at RUBs/LHSs in Rewari-Bassi section.	10000	0	LOA issued on 16.07.2024.
218.	30	-	Construction of 4 lane ROB in lieu of LC No.159 at Km. 212/9-213/0 on Samdari - Bhildi section of Jodhpur Division	855501	0	ROB sanctioned in Umbrella work 2023-24. Estimate technically checked and approval for construction of ROB obtained under R&B deptt. Gujarat. NIT under finalization and same will

						be published online in a week, as per XEN/Gujarat. GAD for LHS approved on 28.06.2023.. Tender is under process by Gujarat State Govt.
219.	30	-	Balanced ancillary work of RUB at LC No C-121 & C-141 for effective Drainage, Retaining wall, CC Road for safety point of under ADEN/SMR	9880	0	-
220.	30	-	Balanced ancillary work of RUB at LC No C-164 & C-166 for effective Drainage, Retaining wall, CC Road for safety point of under ADEN/SMR on SMR-BLDI	4954	7098	-
221.	30	-	Ancillary works on RUBs on SMR-BLDI section LHS against LC no 129 for effective drainage, retaining wall, C.C. road etc. under ADEN/SMR	9936	11143	-
222.	30	-	Ratangarh jn~~Degana~~ Providing 02 lane ROB in lieu of LC no. 21 between Talchhaper-Sujangarh at Km 369/3-4 on RTGH-DNA section.	400000	0	Tender awarded on 15.07.24. soil testing in progress.
223.	30	-	Construction of Road under Bridge at KM 493/5-6 in lieu of LC no.C-06 in & at KM 380/4-5 in lieu of LC no.C-33 at Ladnun yard in	85537	0	Tender open on 25-6-2024 work under TC
224.	30	-	Merta road~~Bikaner~~Construction of Road under Bridge (5x2.50 mt.) at KM 495/9 - 496/0 in ---- Merta Road- Bikaner section,	23241	0	new work
225.	30	-	Merta road~ ~Bikaner~ ~Construction of Road under Bridge (5x2.50 mt.) at KM 490/5-6 in --- MTD-BKN SECTION	24890	0	new work

226.	30	-	Degana~~Merta road~~ Construction of Road under Bridge (4x4.5 mt.) at KM 502/3-4 in between REN-JAC Block section on DNA- MTD section	24836	0	new work
227.	30	-	Phulera~~Degana~~Degana~~ Construction of Road under Bridge (5x4.0 mt.) at KM 51/4-5 in between KMNC-MKN Block section on FL-DNA section	24874	0	new work
228.	30	-	Provision of LHS at KM 31/5-6 on PPR-BARA Section of Jodhpur Division	24960	0	new work
229.	30	-	Provision of LHS at KM 118/8-9 in RKB-JSM Section of Jodhpur Division	24945	0	
230.	30	-	Balance ancillary work of RUB between SMR-BLDI sections LC No C-97 for effective Drainage, Retaining wall, CC Road for safety point of view.	9999	0	Work awarded on 14.08.23 &Work is in progress.
231.	30	-	Balance ancillary work of RUB SMR-BLDI Sec.LC No C-106 at RH side for effective Drainage, extension of Retaining wall, CC Road, water stopper Etc.	9960	8947	Work awarded on 14.08.23 &Work is in progress.
232.	30	-	Merta road~ ~Bikaner~ ~Improvement of Drainage system by raising/extension etc at. 7L (C-21), 7C --- in MTD-BKN sec	8321	0	Estimate sanctioned, Contract work awarded on 06-12-2023. Work in progress.
233.	30	-	Balance ancillary work of RUB between SMR-BLDI section LC No C-158 for effective Drainage, Retaining wall, CC Road for safety point of view.	10335	10335	Work awarded on 14.08.23 &Work is in progress.
234.	30	---	Balance ancillary work of RUB between SMR-BLDI section LC No C-168 for effective	14275	0	Work awarded on 14.08.23 &Work is in progress.

			Drainage, Retaining wall, CC Road for safety point of view.			
235.	30	-	Merta road~~Bikaner~~Improvement of Drainage system by raising/extension of retaining wall cross drainag etc at RUB No. 7U (C-4)---	8377	0	Estimate sanctioned, Contract work awarded on 06-12-2023. Work in progress.
236.	30	-	Balance ancillary work of RUB between LN-SMR-BLDI section LC No C-3 & C-242 for effective Drainage, Retaining wall, CC Road for safety point of view.	14873	0	Work awarded on 14.08.23 &Work is in progress.
237.	30	-	Balance ancillary work of RUB on SMR-BLDI Sec. LC No C-106 at LH side for effective Drainage, extension of Retaining wall, CC Road, Water stopper etc	9978	0	Work awarded on 14.08.23 &Work is in progress.
238.	30	-	Degana~~Ratangarh jn~~Improvement of Drainage system by raising/extension of etc at RUB No. 4A & 4B between DNA-KRC & 32A	9994	0	Work awarded on 06.12.2023 and is in progress.
239.	30	-	Balance ancillary work of RUB between SMR-BLDI section LC No C-20 for effective Drainage, Retaining wall, CC Road for safety point of view.	9623	0	Work awarded on 14.08.23 &Work is in progress.
240.	31	PB-100	Madar - Palanpur - CTR(P) 34.25 Km	964540	381567	Work completed. Final Bill and Final variation awaited. Material Booking to be done
241.	31	PB-101	Bikaner - Merta Road CTR (P) 25.80 Km	877376	58416	work is physically completed, contract final bill is paid. Material against some indents to be received from HQ. will be deleted after clearing all liabilities.
242.	31	PB-102	Marwar Jn. - Abu Road CTR(P) 57.69 Km	501961	66568	CTR completed. final variation and bill awaited. Ballast Tender invited vide Tender no 104-2022 and will opened on 12.08.22, LOA issued on 03.10.22, Completed and final bill and variation awaited

243.	31	PB-104	Madar - Palanpur - CTR (P) - 34.30 Kms	619740	72152	CTR completed. Final bill passed. Proposed for Deletion
244.	31	PB-105	Madar - Palanpur - CTR (P) 38.28 Kms.	641797	23975	CTR completed. Final variation & Final Bill awaited. Material Booking to be done, Ballast tender awarded on 16.01.24
245.	31	PB-106	Madar - Palanpur- CTR (P) - 37.71 km	689876	132348	CTR completed. TTR Work in progress. 2 nd Variation vetted by accounts. Work Completed, Final bill and variation awaited
246.	31	PB-107	Phulera - Madar (Up) - CTR (P) - 29.12 km (from km 225.12 to km 254.24) (PB#225/2019-20/NWR)	779000	771126	Work Completed, final bill passed. Completion report under process
247.	31	PB-108	Jaipur Division - Phulera - Madar (UP) - CTR (P) - 31.53 km (from km 254.24 to km 285.77) (PB#225/2019-20/NWR)	775700	752732	Work completed; Final bill passed. Completion report under process
248.	31	PB-110	Rewari - Alwar(UP & DN) - CTR(P) - 37.820 km (PB#244/2021-22/NWR)	889600	837463	Work completed. FVS sanctioned and f/Bill passed. Completion report under process
249.	31	PB-111	Bandikui - Jaipur (DN) - CTR(P) - 36.524 km, Ghariharsaru - Rewari (UP) - CTR(P) - 0.166 km & Alwar - Bandikui (DN) - CTR(P) - 0.376 km (PB#244/2021-22/NWR)	941778	835778	Work completed. FVS vetted and F/Bill passed. Completion report under process
250.	31	PB-112	Alwar - Bandikui (DN) - CTR(P) - 3.890 Tkm and Rewari - Alwar - CTR(P) - 31.690 Tkm (PB#271/2022-23/NWR)	758000	132240	Work awarded on 03.08.2022. Work completed. F/Bill passed. Materia to be booked.
251.	31	PB-113	Phulera - Degana (UP) - CTR(P) - 31.145 Tkm (PB#278/2023-24/NWR)	697500	225556	Work in progress.
252.	31	PB-114	Rewari - Ringus - Phulera (SL) - TBR - 215 Km & Phulera - Madar (UP) - TBR - 35.22 Km	1065995	824747	Work Completed. But Ballast provision is to be utilized.

253.	31	PB-115	Samdari - Bhildi (SL) - TBR - 222.20 km (PB#227/2019-20/NWR)	583640	348295	Work completed.
254.	31	PB-116	Rewari - Bathinda - TBR - 196.030 km (PB#241/2020-21/NWR)	632078	426110	"SSA (Km.100.52 to 188.68) - Ancillary work completed. Final bill paid in June24. SSA (Km.188.68 to 270) - Deep screening work completed. HMH-I (Km.270 to 296.55) - Ancillary work completed. Final bill paid in March 22 HMH Depot (80000/ 26200 cum) - supply quantity against this work completed. Final bill paid in May23. HMH Depot (39000/10620 cum) work is in progress. HSR depot completed. BWK Depot (65000/41000)- work completed. New HSR depot 50000 cum opened on 15.02.24 but discharged. T
255.	31	PB-117	Jodhpur Division - Through Fitting Renewal - 2473.419 km (Metal Liners - 1205.804 km, GFN Liners - 186.358 km & GRSP - 1081.257 km) (PB#246/2021-22/NWR)	733900	142397	Work in progress.
256.	31	PB-118	Suratgarh - Lalgarh - CTR(P) - 26.500 Tkm (PB#282/2023-24/NWR)	636181	0	"Work sanctioned on 01.09.23. Tender opened on 16.01.24 & awarded on 02.05.24. PQRS material received. RMSR depot 39045/34100 cum-tender opened on 07.05.24 & awarded on 29.07.24. TRD- tender to be opened on 27.08.24. Material booking being done."

257.	31	PB-136	Madar - Palanpur - Removing of PSR (Kms 589/1 to 590/1)	181477	56400	Work transferred to RVNL. Work completed by RVNL. Cost Adjustment between RB and RVNL Pending. Will be deleted after cost adjustment
258.	31	PB-137	Jaipur - Sawaimadhopur - TRR (P) 41.17 km	612480	-188482	Work Completed, Final bill passed. Completion report is in process.
259.	31	PB-138	Rai ka Bagh-Jaisalmer (SL) - TBR - 41 km	109121	143198	Work completed Final bill passed. SD PG released. Work to be deleted from IRPSM
260.	31	PB-140	Jaipur - Madar & Jaipur - Swaimadhopur - TTR (CS CMSC) - 90 sets (PB#228/2019-20/NWR)	87824	59364	Work is in progress as per availability of material
261.	31	PB-143	Jaipur - Sawaimadhopur - TRR(P) - 14.620 km & Delhi - Rewari - TRR(P) - 1.700 km (PB#238/2020-21/NWR)	240492	179392	Work completed. F/bill passed. Completion report under process
262.	31	PB-145	Hanumangarh - Suratgarh - TRR(P) - 31.484 km (PB#239/2020-21/NWR)	326443	315232	Work completed. Final bill to be paid. Material booking done.
263.	31	PB-147	Alwar - Bandikui (UP) - CTR(P) - 16.776 Tkm (18/Suppl./Dec'2023/NWR)	375700	0	Tender opened on 19-6-24 and Discharged and reinvite
264.	31	PB-148	Madar - Palanpur - TRR(P) - 36.390 Tkm (18/Suppl./Dec'2023/NWR)	457800	0	Work in progress
265.	31	PB-149	Madar - Palanpur - TTR(TWS) - 121 sets (1:12)(18/Suppl./Dec'2023/NWR)	149039	0	Detail Estimate sanctioned .tender opened on 28.06.2024, Discharged, again invited and opened on 12.08.2024, no bid received, again invited and will open on 09.09.24
266.	31	PB-150	Phulera - Madar (UP) - CTR(P) - 9.640 Tkm (18/Suppl./Dec'2023/NWR)	254886	0	Work awarded on 1-8-24
267.	31	PB-151	Alwar - Bandikui (DN) - CTR(P) - 21.900 Tkm(18/Suppl./Dec'2023/NWR)	490500	0	Tender opened on 19-6-24 and Discharged and reinvite

268.	31	PB-162	Madar - Palanpur - CTR (P) - 10.92 Kms	203202	19132	CTR completed. Final bill and variation awaited. ballast tender awarded on 16.01.2024
269.	31	PB-165	Suratgarh - Lalgarh - TRR (P) -14.82 Km & CTR (P) - 6.22 km	266844	252098	Work completed. Final bill of Rs.67.45 Lac hold due to theft of material & case under vigilance enquiry. After final decision same shall be paid.
270.	31	PB-171	Madar - Durai Bypass Line - CTR(P) - 8.10 km (PB#225/2019-20/NWR)	148000	11850	HR and Final Bill send to Division.
271.	31	PB-173	Rewari - Jaipur - CTR(P) - 14.600 km (PB#240/2020-21/NWR)	294200	264740	Work completed. FVS & Final bill awaited from ADEN/AWR.
272.	31	PB-175	Madar - Marwar Jn. - CTR (P) - 12.280 km (PB#240/2020-21/NWR)	247600	-81603	Completion report has been submitted.
273.	31	PB-176	Degana - Merta Road - CTR(P) - 21.390 km (PB#240/2020-21/NWR)	431400	157662	work is in progress, 21.39 km work has been completed, balance is in progress.
274.	31	PB-177	Madar - Marwar Jn. (UP) - CTR (P) - 3.630 km (Madar Yard) (PB#240/2020-21/NWR)	73200	4596	Completion report has been submitted.
275.	31	PB-179	Jodhpur - Merta Road (SL) - CTR(P) - 5.200 km (PB#244/2021-22/NWR)	105100	74500	Work Completed. final liabilities to be cleared.
276.	31	PB-182	Jodhpur Division - Phulera - Degana (UP) - CTR(P) -13.932 Tkm and Bikaner Division - Kolayat - Phalodi (SL) - TRR(P) - 1.000 Tkm (PB#271/2022-23/NWR)	310200	149320	Work in Progress.
277.	31	PB-183	Madar - Palanpur - TRR(S) - 2.072 Tkm (Loop Lines), Madar - Palanpur - TRR(S) - 1.642 Tkm (Loop Lines) and Marwar - Mavli Jn. (MG/S1) - CTR(S) - 19.000 Tkm (PB#272/2022-23/NWR)	241100	3290	TRR work for 1.642 is completed.

278.	31	PB-184	Ajmer Division - Renewal of SEJs - 21 Nos. and TTR(TWS+WCMSC) - 9 sets (1:12) and Jodhpur Division - TTR(FS TWS CMSC) - 7 sets (1:12) (PB#273/2022-23/NWR)	43691	17132	For 21 Set SEJ : - Detail Estimate sanctioned for SEJ 21 sets, tender opened on 04.07.22 and LOA issued on 08.07.22. Contractor expired.
279.	31	PB-185	Ajmer - Chittaurgarh (SL) - TBR - 52.800 Tkm (PB#273/2022-23/NWR)	213900	72476	TBR work is completed and ancillary works are in progress and ballast supply against this work is under progress in depot.
280.	31	PB-186	Ajmer - Chittourgarh (SL) - TRR(P) - 22.515 Tkm (PB#278/2023-24/NWR)	423407	270211	Work under progress.
281.	31	PB-187	Jodhpur - Luni (DN&SL) - CTR(P) - 3.661 Tkm (PB#278/2023-24/NWR)	82000	11323	Tender awarded on 08.08.23. Work in progress.
282.	31	PB-189	Samdari-Munabao - TBR - 197.32 km	483730	135195	work is completed, recommended for deletion on IRPSM.
283.	31	PB-189	Phulera - Degana (UP) - CTR(P) - 16.814 Tkm (PB#278/2023-24/NWR)	376500	160105	Work in progress.
284.	31	PB-190	Phulera - Degana (UP) - CTR(P) - 8.860 Tkm (PB#278/2023-24/NWR)	198400	62272	Work in progress.
285.	31	PB-191	Chitaurgarh - Udaipur city - TRR(S) - 10.695 km & ISD - 10.695 km	68652	34813	ISD completed. TRR(S) work has been completed. Final variation vetted. Final bill passed.
286.	31	PB-192	Rewari - Jaipur (SL) - TRR(P) - 3.10 Km & Rewari-Ringus-Phulera (SL) - TRR(P) - 0.600 Km	43590	36330	Work completed. F/Bill passed. Completion report under process
287.	31	PB-193	Haripur - Karjoda - TRR(S) - 6.446 km (loop lines) (PB#226/2019-20/NWR)	57400	10384	LOA issued on 10.11.21,TRR (S) and TWR of looplines as per available scope is completed. Some ancillary works are left
288.	31	PB-195	Rohtak - Bhiwani (SL) - TRR(P) - 19.000 km (PB#245/2021-22/NWR)	234520	228520	"TRR work completed. Final bill paid in Sept 22. Material booking done." TRD- TRD- contract awarded on 20.12.22. Work completed. Final bill to be paid.

289.	31	PB-196	Suratgarh - Lalgarh (SL) - TRR(P) - 2.624 km (PB#245/2021-22/NWR)	42218	34467	"Work completed. Final bill paid in July 23. Material booking done." CR sent to a/c on 01.08.24 for vetting.
290.	31	PB-197	Jaipur Division - TRR(P) - 5.728 km (Bandikui - Jaipur (DN) - 0.311 km, Garhiharsaru - Rewari - 2.106 km & Jaipur - Phulera - 3.311 km) & Jodhpur Div. - Rai-Ka-Bagh - Jaisalmer (SL) - TRR(P) - 1.259 km (PB#245/2021-22/NWR)	85240	53632	Work completed. FVS sanctioned and Final Bill passed. Material to be booked
291.	31	PB-198	Rewari - Alwar (UP & DN) - TRR(P) - 3.200 km (PB#245/2021-22/NWR)	50000	10343	Work completed. FVS sanctioned and Final bill passed. Material to be booked
292.	31	PB-199	Madar - Palanpur - TRR(S) - 4.478 Tkm (PB#279/2023-24/NWR)	49313	37964	Detail Estimate Sanctioned on 23.06.2023, Opened on 21.08.2023, No bid Received, Estimate revised with AT Welding with Rly Portion, Tender Re invited, no response, Again Invited Tender opened on 30.11.23, LOA issued on 07.12.23, Work in progress
293.	31	PB-200	Rewari - Bhiwani - TRR(S) of Loop Lines - 5.267 Tkm (PB#279/2023-24/NWR)	42229	10387	"Work sanctioned on 18.05.23. TRR(S)-Loop line-contract awarded on 03.08.23. Work completed. Flush butt welding- Tender opened on 18.07.23, 31.10.23 & 04.01.24 but discharged. TRD- tender to be opened on 27.08.24.
294.	31	PB-201	Suratgarh - Anupgarh (Loop Lines) - TRR(S) - 10.964 Tkm (PB#279/2023-24/NWR)	93654	4944	"Loop Line- Contract awarded on 23.08.23. 8.5 Km completed. Work is in progress. Flush butt welding-Tender opened on 14.08.23 & awarded on 03.10.23. Welder approval under process. TRD- tender to be opened on 27.08.24.

295.	31	PB-202	Merta Road - Bikaner - TBR - 50.65 Kms	241877	17543	Work Completed, final bill & all contractual Liabilities cleared.
296.	31	PB-204	Phulera - Madar (Down) - TBR - 22.50 km (PB#227/2019-20/NWR)	73743	45305	Work Completed. F/Bill & FVS awaited from ADEN/FL.
297.	31	PB-205	Degana - Ratangrah (SL) - TBR - 142.89 km (PB#227/2019-20/NWR)	447556	126402	Work is in Progress.
298.	31	PB-206	Ajmer - Chittaurgarh - TBR - 33 km (loop lines) (PB#227/2019-20/NWR)	83125	17577	work is in progress and delay due to monsoon period.
299.	31	PB-208	Jaipur - Phulera (DN) - TBR - 54.08 km (PB#227/2019-20/NWR)	194237	94158	Work completed. FVS & F/bill is awaited from ADEN/Line/JP
300.	31	PB-209	Rohtak - Bhiwani - TBR - 41.400 km (PB#241/2020-21/NWR)	145097	118340	"On availability of BCM work will be carried out. Flush butt welding from 6 to 32 opened on 04.01.23 but discharged on 15.02.23. Ancillary work is in progress (45%) . Material booking being done."
301.	31	PB-211	Rai ka Bagh - Jaiselmer - TBR on Plain Track - 25 km & TBR on Turnout - 6 sets (PB#241/2020-21/NWR)	78700	70265	Work in progress
302.	31	PB-212	Jaipur Division - TBR - 160.360 km (PB#241/2020-21/NWR)	419614	139875	Sr.DEN/HQ/JP sec. Work awarded on 04.02.2022. Sr.DEN/E/JP sec. work awarded on 27.02.2022.Sr.DEN/S/JP sec. work awarded on 17.02.2022. Work is in progress.
303.	31	PB-214	Jaipur Division - TBR on Turnout - 206 sets (PB#241/2020-21/NWR)	36700	3319	Sr.DEN/S/JP sec. - Work awarded on 17.02.2022. Sr.DEN/HQ/JP sec. work awarded on 04.02.2022. Sr.DEN/E/JP sec. work awarded on 27.02.2022. Work is in progress.

304.	31	PB-215	Phulera - Degana - TBR on Plain Track - 67.950 km & TBR on Turnout - 26 sets (PB#241/2020-21/NWR)	215000	77264	Work in Progress.
305.	31	PB-216	Merta Road - Bikaner - TBR on Plain Track - 49.890 km & TBR on Turnout - 15 sets (Turnout) (PB#241/2020-21/NWR)	157400	83912	Work completed. final bill paid.PG & SD to be paid
306.	31	PB-218	Jaipur Division - Renewal of GRSP - 161.068 km and Metal/GFN Liner - 573.798 km (PB#246/2021-22/NWR)	205430	51335	Sr. DEN/E/JP section work awarded on 29.10.21. Sr. DEN/S/JP Work awarded on 02.03.2022 Sr. DEN/HQ/JP sec. Work awarded on 04.02.2022. Work is in progress.
307.	31	PB-219	Jaipur Division - TBR - 27.170 km (Alwar - Bandikui (DN) - 25.600 km & Jaipur - Phulera (UP) - 1.570 km) (PB#246/2021-22/NWR)	95445	11020	Sr. DEN/E/JP section work awarded on 29.10.21. Sr. DEN/S/JP Work awarded on 02.03.2022 Work is in progress.
308.	31	PB-220	Luni - Marwar Junction - TBR - 8.675 km (PB#246/2021-22/NWR)	28700	15131	Detailed Estimate sanctioned. Tender will be invited as per availability of BCM machines.
309.	31	PB-221	Jodhpur - Luni Junction - TBR - 11.640 km (PB#246/2021-22/NWR)	48600	632	Detailed Estimate sanctioned. Tender will be invited as per BCM planning.
310.	31	PB-222	Luni - Samdari (SL) - Increasing Sleeper Density(M 7 to M 8) - 47.940 km (PB#246/2021-22/NWR)	65800	25016	Work Completed . Final variation and Final Bill under process.
311.	31	PB-223	Jodhpur Division - TBR - 11.553 km (Kolayat - Phalodi - 5.253 km, Phalodi By Pass - 1.300 km & Pokran - Triangle - 5.000 km) (PB#246/2021-22/NWR)	48300	0	Detailed Estimate sanctioned. contract will be invited as per availability of BCM machines.
312.	31	PB-224	Bikaner Division - TBR - 77.268 km (Hisar - Sadulpur - 67.815 km & Ratangarh - Degana - 9.453 km)	302405	102196	"Deep screening work in RTGH-DNA section of BKN division is completed. Ancillary work- work completed.

			(PB#246/2021-22/NWR)			Final bill paid in Jan. 24. Hiring of truck -WIP. SURP Depot (60000 cum)- Work is in progress.(43%). Misc. Work completed. Final bill paid in Dec.23 PIH Depot (108000/148000) cum-contract awarded on 12.10.23. Work is in progress. TRD- Work is in progress."
313.	31	PB-225	Bikaner Division - Renewal of GRSP - 808.333 km, GFN Liner - 148.855 km & Metal Liner - 556.434 km (PB#246/2021-22/NWR)	398323	70810	"RTGH- work is in progress (80%) DEN/W- contract terminated on 03.05.23. Contract again awarded on 11.09.23. Work is in progress. (60%). DEN/N Work is in progress. SDLP - contract terminated. Contract again awarded on 11.02.24. Work is in progress.30% Sr.DEN/E- work is in progress (65%) TRD- contract awarded on 20.12.22. work is in progress."
314.	31	PB-226	Bikaner Division - TBR - 6.925 km (Bridwal - Lalgarh - 3.925 km, Haumangarh - Suratgarh - 1.330 km & Suratgarh - Bridwal - 1.670 km) & Suratgarh - Anupgarh (SL) - TBR - 21.380 km (PB#246/2021-22/NWR)	131665	68041	"Contract for TBR 28.305 Km. awarded on 26.04.22. Work completed. Hiring of truck-work is in progress. Bap Depot (39627/97258) cum-tender opened on 10.05.23 & awarded on 19.10.23. Work is in progress."
315.	31	PB-227	Rewari - Sadulpur - TBR - 141.200 km (PB#246/2021-22/NWR)	542057	138882	68.03 Km. (Sr.DEN/East) - Misc. civil - contract short closed due to non availability of BCM. Final bill paid in Feb.24(15%) 68.03 Km. (Sr.DEN/East) -TBR- Work is held up due to non availability of BCM (37%) 71.78Km. (DEN/South) 26 T/out & 61 Km. deep screening

						completed. Cess repair in progress.(55%) Misc. work (71.78 South) - contract awarded on 04.06.24. Work is in progress (5%). PIH depot Ballast supply is in progress.
316.	31	PB-228	Rewari Jn. - Alwar Jn. (DN) - TBR - 51.240 Tkm & Mathura Jn. - Alwar Jn. (SL) - TBR - 1.926 Tkm (PB#280/2023-24/NWR)	221897	566	LOA issued on 22.02.24. Work in progress
317.	31	PB-229	Rewari Jn. - Bhiwani Jn. (SL&UP) - TBR - 75.875 Tkm (PB#280/2023-24/NWR)	305854	763	Work sanctioned on 18.05.23. TBR 88.375 Km Tender opened on 25.08.23 & 04.12.23 but discharged. Re-tender opened on 15.02.24 & awarded on 03.05.24. Work is in progress. TRD- tender to be opened on 27.08.24.
318.	31	PB-230	Bikaner Division- TFR (GRSP) - 100.153 Tkm (PB#280/2023-24/NWR)	27461	2655	"Work sanctioned on 18.05.23. East- TFR 26.105 Km contract awarded on 20.09.23. Work is in progress (95%) South (70.048Km TFR)- Tender 30.05.24 & awarded on 04.07.24 TRD- tender to be opened on 27.08.24.
319.	31	PB-231	Suratgarh - Lalgarh - TFR (ERC- 115.811 km , GRSP-127.74 km, Liner-118.733 Km) (PB#280/2023-24/NWR)	118944	4163	Civil -Work is in progress. TRD- tender to be opened on 27.08.24.
320.	31	PB-232	Ratangarh - Bikaner Jn. (SL) - TBR - 11.500 Tkm (PB#280/2023-24/NWR)	51663	11185	TBR work completed. Ancillary work is in progress. Cess supply 7050 cum -contract awarded on 13.09.23. work completed"
321.	31	PB-233	Luni Jn. - Barmer (Loop Lines) - TBR - 16.910 Tkm (PB#280/2023-24/NWR)	46300	15454	Work completed in LN-BME section.
322.	31	PB-234	Samdari - Bhildi - TBR of Loop Lines - 36.870 Tkm (PB#280/2023-	101100	3801	Work completed in SMR-JOR section and in progress in

			24/NWR)			balance section.
323.	31	PB-235	Suratgarh Jn. - Lalgarh Jn. (SL) - TBR - 8.677 Tkm (PB#280/2023-24/NWR)	43330	9364	TBR -contract awarded on 23.08.23. Work completed. Ancillary work is in progress . Cess supply 5000 cum -contract awarded on 13.09.23. work completed."
324.	31	PB-236	Ajmer Jn. - Chittaurgarh (SL) - TBR - 11.900 Tkm (PB#280/2023-24/NWR)	60281	22792	TBR Work is completed and supply of ballast is pending.
325.	31	PB-237	Bikaner - Merta - Phulera and Jodhpur - Marwar Jn Section - TTR(CS CMSC) - 237 Nos.	226978	127850	Work is in progress.
326.	31	PB-238	Rewari - Jaipur-Madar - TTR - 165 set & TTR - 73 set	282305	181965	Work in progress as per availability of TWS & WCMSC.
327.	31	PB-240	Ajmer - Chittaurgarh - TTR (TWS+CMSC) - 57 Sets	83185	46052	A new proposal for TTR (CS-52 kg)-87 set in PB 2023-24 is not approved by Railway Board. As per HQ and Railway board instruction the parent work of TTR (TWS) -57 is to be done with new proposal of TRR (P) - 60 kg in main line of yards in AII-COR section, which is sanctioned by railway board. Accordingly the work is awarded and under progress.
328.	31	PB-241	Rai ka Bagh - Jaisalmer & Samdari - Bhildi - TTR(TWS CMSC) - 22 sets & TTR(CS CMSC) - 6 sets, Renewal of SEJs - 142 nos. & Glued Joints - 659 Nos. (PB#242/2020-21/NWR)	142500	98665	Estimate sanctioned. Contract awarded, work is in progress.
329.	31	PB-245	Jaipur Division - Renewal of Glued Joints - 1058 Nos. & SEJs - 80 Nos. & Provision of Track Machine Siding at Phulera & Gehlota (PB#247/2021-22/NWR)	147504	59532	Sr. DEN/S/JP work awarded on 31.01.2022. Siding at Gehlota work awarded on 19-12-22 and completed. . DEN/E/JP section tender opened on 28.11.23 and work awarded on 22-2-24 & is in progress

330.	31	PB-246	Ajmer Division - Renewal of Liner and GRSP - 479.799 km (Metal Liner - 265.408 km, GFN Liner - 62.275 km & GRSP - 152.116 km) (PB#247/2021-22/NWR)	128424	20542	LOA issued on 05.06.22. Work is in progress.
331.	31	PB-247	Madar - Palanpur - TTR(TWS) - 32 sets & TTR(TWS CMSC) - 49 sets (PB#247/2021-22/NWR)	124142	104048	LOA issued on 06.09.2021.Work Completed
332.	31	PB-248	Ajmer Division - Renewal of Glued Joints - (Ajmer - Chittorgarh(SL) - 549 Nos., Phulera - Ajmer(DN) - 39 Nos. & Marwar - Palanpur(DN) - 48 Nos.) (PB#247/2021-22/NWR)	56500	11372	Work is stopped by agency from 30.03.2023 and not turned up till date.
333.	31	PB-249	Rewari - Bathinda - TTR(FS TWS WCMSC) - 103 sets (1 in 12 - 75 sets & 1 in 8.5 - 28 sets) (PB#247/2021-22/NWR)	347759	36242	"Estimate under revision. Sleeper not required, all the turnouts are fan shaped and already laid on 60 Kg PSC sleepers and all sleepers are in good condition and codal life is also not completed. Decision received from HQ. North-77 set TTR contract awarded on 21.09.23. Work is in progress (30%). As per PCE instruction, work not to be executed. East- 26 set TTR contract awarded on 06.11.23. Work is in progress (85%) TRD- Work is in progress.
334.	31	PB-250	Rewari - Ringus - Phulera - TTR(CS CMSC) - 91 sets (1 in 12) (PB#247/2021-22/NWR)	90640	49852	Sr. DEN/S/JP Tender opened on 27.12.2021 and work awarded on 31.01.2022. Sr. DEN/N/JP Tender opened on 13.01.2022 and work awarded on 25.02.2022. Work is in progress. Material to be booked
335.	31	PB-251	Bikaner Division - TTR(CS) - 35 sets, Glued Joints - 93 sets & SEJs - 82 sets (PB#247/2021-22/NWR)	66093	28162	"DEN/South section- work completed. Sr.DEN/E section- work completed. Contract terminated on 16.06.23.

						West- 29 Set TTR tender opened on 04.09.23 & awarded on 30.10.23. Work is in progress. TRD- work is in progress . Material booking being done.
336.	31	PB-252	Jaipur Division - Minor modification of curves - 104 Nos. (PB#247/2021-22/NWR)	259375	0	Sr. DEN/E/JP -work awarded on 27.02.2022. Sr. DEN/S/JP -work awarded on 17.02.2022. Sr. DEN/HQ/JP work awarded on 12-12-22. Work is in progress
337.	31	PB-253	Jaipur Division (Rewari - Ajmer & Jaipur - Sawaimadhopur) - TBCSR (H-Beam) - 900 Nos. (PB#247/2021-22/NWR)	40956	24339	Sr. DEN/S/JP work awarded on 16.03.2022. Sr. DEN(HQ)/JP work completed and F/bill under process.
338.	31	PB-254	Jaipur Division - TTR(TWS CMSC) - 182 sets (1 in 12 - 163 sets & 1 in 8.5 - 19 sets) (PB#247/2021-22/NWR)	275750	185107	Sr. DEN/E/JP section work awarded on 29.10.21. Sr. DEN/N/JP section work awarded on 25.02.2022. Sr. DEN/S/JP work awarded on 5/12/2022. Sr. DEN/HQ/JP section work awarded 04.02.2022. Work is in progress (104 set replaced out of 182 set)
339.	31	PB-255	Jaipur Division - TTR(CMSC) - 85 sets & TTR(CS) - 206 sets (PB#247/2021-22/NWR)	190345	59095	Sr. DEN/E/JP section track work awarded on 29.10.21 & associate civil work tender opened on 28.11.23 and under finalization. Sr. DEN/N/JP section work awarded 25.02.2022. Sr. DEN/S/JP section work awarded on 31.01.2022. Work is in progress. Material to be booked
340.	31	PB-256	Provision of Track Machine Siding along with resting facility at Ding & Klanaurkalan and only resting facility at Dahinajanabad & Mahendragarh (PB#247/2021-22/NWR)	49075	25645	"Contract for Siding awarded and work completed. Final bill paid in Jan.24. Resting facility & Track Machine siding - Work completed. Final bill to be paid. TRD- Work is in progress. Work carried out after NI. (90%) Elect. Contract awarded on 04.02.23. 90% work completed."
341.	31	PB-257	Jodhpur Division(Luni-Samdari, Merta Road-Bikaner, Rai-Ka-Bagh-Jodhpur & Samdari-Bhildi)-TTR(CS CMSC) - 257 sets(1 in 12-254	226500	57	Work awarded on 03.02.24

			sets & 1 in 8.5 - 3 sets) (PB#247/2021-22/NWR)			
342.	31	PB-258	Lalgarh - Surtgarh - TTR(CS CMSC) - 29 sets (1 in 12 - 25 sets & 1 in 8.5 - 4 sets) & Lalgarh - Phalodi - TTR(CS CMSC) - 25 sets (1 in 12 - 24 sets & 1 in 8.5 - 1 set) & Rohtak - Bhiwani - TTR(CS CMSC) - 3 sets (1 in 12) (PB#247/2021-22/NWR)	62341	668	"East- work completed. Contract terminated. West- tender opened on 04.09.23 & awarded on 30.10.23. Work is in progress. Material booking to be done."
343.	31	PB-259	Rewari - Hisar - Bathinda - Suratgarh - Biradhwal - TTR(TWS WCMSC) - 32 sets (1 in 12 - 28 sets & 1 in 8.5 - 4 sets) (PB#247/2021-22/NWR)	69615	26192	"Civil- Work completed. TRD- Tender opened on 28.11.22 & awarded on 20.12.22. Work completed. Material booking being done.
344.	31	PB-260	Chittaurgarh - Udaipur - Providing track machine facilities at Ghosunda, Kapasan, Khemli and Udaipur stations. (PB#281/2023-24/NWR)	48937	4666	Detail estimate sanctioned. LOA of work other than track portion issued on 25.01.24. LOA of track issued on 11.04.24. Work of Pathway and approach road at GSD station is in progress
345.	31	PB-261	Bikaner Division - Provision of facilities at existing Track Machine Sidings (PB#281/2023-24/NWR)	95497	12837	"Work sanctioned on 18.05.23. East- tender opened on 28.07.23 & 19.09.23 but discharged. Re-tender opened on 04.01.24 & LOA issued on 11.03.24 and work in progress. West -Contract awarded on 14.12.23. Work is in progress (30%). South contract awarded on 16.10.23. At SDLP, SWNI & NPS work is in progress (65%) North contract awarded on 23.10.23. Work is in progress (60%)"
346.	31	PB-262	Merta Road - Bikaner - Removal of PSR - 5 nos. (PB#281/2023-24/NWR)	68800	3909	Work in progress.
347.	31	PB-263	Jodhpur - Luni - TTR(FS TWS WCMSC)	37100	10352	Estimate sanctioned. Tender under process.

			- 16 sets (1:12) (PB#281/2023-24/NWR)			
348.	31	PB-266	Jaipur Division - Conversion of SWR into LWR of loop lines - 86.40 km & ISD - 11 km	382785	330511	DEN/E, DEN/N/JP & Sr. DEN(HQ)/JP - Work Completed & final bill passed. Sr DEN/S - Work is in progress
349.	31	PB-267	Jaipur Division - Glued Joints (52 Kg) - 1000 No	73000	60443	Sr. DEN(N)/JP & DEN(E)/JP section Work is in progress. Sr. DEN/s - Work completed and Final bill passed.
350.	31	PB-268	Jaipur Division - SEJ - 211 Nos	95400	55080	Sr DEN/S - Work completed and Final bill passed. In othern Sr.DENs section When ever material is received booked accordingly.
351.	31	PB-269	Rewari - Bhatinda - Conversion of SWR into LWR of loop lines - 51 km	113614	60965	"Ballast 40800 cum supplied & Final bill paid in Jan.19. Welding work completed. Final bill paid in May 22.PVC paid in Aug23 Misc. track work held up 40%). Contract terminated on 22.08.22. Estimate revised. Tender opened on 04.01.24 & awarded on 23.01.24 and work terminated due to non submission of P.G. and tender is being invited.
352.	31	PB-270	Chittorgarh - Udaipur - TBR - 112.01 km	215547	124129	Deep screening work has been completed. The work of Ballast supply has been terminated on 26.10.2021 due to poor performance.Final bill pending on account of contractor due to non sumbission of royalty and GST invoice.
353.	31	PB-273	Jodhpur Division - Strengthening of Loop Lines - 49.62 km	117408	8354	Work completed.
354.	31	PB-274	Suratgarh, Ramsinghpur and Anupgarh Yard - TRR(S) - 5.858 km (PB#248/2021-22/NWR)	64683	54583	"TRR work completed. Final bill paid in July 23. Flush Butt Welding work completed. Final bill paid in July 23. Material booking done. Proposed

						for deletion. CR sent to a/c on 01.08.24 for vetting.
355.	31	PB-276	Rohtak - Bhiwani - TRR(P) - 12.000 Tkm (PB#282/2023-24/NWR)	178730	123105	Contract awarded on 29.12.23. Work is in progress. Material booking being done .
356.	31	PB-904	Ajmer Division - Installation of track mounted automatic Gauge Face Lubricators on curves - 445 Nos.	188600	0	Detail estimate vetted by accounts. Revised estimate vetted by accounts. Tender will be opened on 17.09.24.
357.	31	PB-904	Bikaner Division - Installation of track mounted automatic Gauge Face Lubricators on curves - 310 Nos.	147800	0	Work sanctioned on 20.03.24. Detail estimate sanctioned on 26.06.24. Tender to be floated.
358.	31	PB-904	Jaipur Division - Installation of track mounted automatic Gauge Face Lubricators on curves - 182 Nos.	697000	0	Detailed estimate sanctioned and Tender to be opened on 21-8-24
359.	31	PB-904	Jodhpur Division - Installation of track mounted automatic Gauge Face Lubricators on curves - 334 Nos.	141600	0	Detail estimate under prepration
360.	31	PB-95	Phulera - Madar (DN) - TRR(P) - 70.460 Tkm (18/Suppl./Dec'2023/NWR)	955110	0	Work awarded on 1-8-24
361.	31	PB-96	Luni Jn. - Marwar Jn. (SL) - CTR(P) - 28.143 Tkm (PB#903/2023-24/NR)	630300	88696	Tender awarded on 08.08.23
362.	31	PB-97	Luni Jn. - Marwar Jn - CTR(P) - 28.500 Tkm (PB#903/2023-24/NR)	638300	170593	Tender awarded on 08.08.23
363.	31	PB-98	Jodhpur Jn. - Luni Jn. - CTR(P) - 22.398 Tkm & Merta Road Jn. - Jodhpur Jn. - CTR(P) - 2.988 Tkm (PB#903/2023-24/NR)	568500	389517	Tender awarded on 08.08.23
364.	31	PB-99	Jodhpur Jn. - Luni Jn. (UP) - CTR(P) - 23.168 Tkm (PB#903/2023-24/NR)	518800	256892	Tender awarded on 08.08.23
365.	31	LB-150	Jaipur~~Kanauta~~Improvement to sanded dead end and sidings. in KUT-JP-SAS	9724	5427	Work near completion

			Section.			
366.	31	LB-151	Jaipur~~TRR, Deep screening and replacement of sleepers between Km. 241/8 to 242/4 point No. 190 and curve No. 62 Up line in JP Yard	7957	7289	Work completed and F/bill passed. Completion report certified by finance. work may be deleted
367.	31	LB-152	AII Div. - Strengthening of Bridge approaches of Br. No. 845 (Important Bridge) on MD - PNU sec.	11065	0	Contract awarded. However RVNL has done formation pitching and toe wall work during doubling. DFC has done pitching and toe wall work on their side. Therefore Contract scope is being reviewed.
368.	31	LB-158	Bandikui~~Jaipur~~BKI -JP - CTR(P)- 1 km (between km 204.5 to 205.5) & DO-Didwana main line -TRR(P) 0.946 km	21963	20445	Work completed. FVS & F/bill awaited from ADEN/BKI
369.	31	LB-163	Jaipur~~TRR of line NO. 5 and line exist on platform No. 2A in JP Yard.	8454	7813	Work Completed. F/Bill passed. GST difference bill paid. completion report certified b y finance & attached . Work may be deleted.
370.	31	LB-169	Phulera - Merta Road - TBR - 6.94 km	15245	0	Earlier tender was invited for manual deep screening , which was terminated due to failure of contractor. Now tender will be planned as per planning of BCM.
371.	31	LB-179	Replacement of 1 in 8.5 turnouts with 1 in 12 turnouts and shifting of turnout in RE yard.	24771	15722	Work awarded & Work is near completion
372.	31	LB-181	AJMER Div. Removal of DFWR(Welds) 0f 52 Kg -90 UTS in Ladpura-Marwar Jn Section and Ajmer- Chittaurgarh-Udaipur Section	6295	0	LOA issued. The progress of work was slow, hence contract terminated for Sr.DEN/East section. Agency has demanded for arbitration
373.	31	LB-188	ADEN- Aburoad & MarwarJn Renewal of Glued Joints in HP - PNU section.	7280	955	Work will be done departmentally. Material Awaited
374.	31	LB-193	Rewari~~Madar Jn.~~JP Division-Casual Renewal of Switches & CMS crossings 1 in 12 60 kg	9143	8216	Work completed. Final bill passed. Completion Report under process
375.	31	LB-194	Jaipur~~Bandikui~~TB R of loop line of GTJT ,KUT & KWP(DN), SNGN (1&3),SAS (1&3)	10398	8109	Work completed, F/Bill passed. GST difference bill passed. Completion report vetted by finance and attached. work may

						be deleted
376.	31	LB-195	Jaipur~~Bandikui~~Welding of free rail/ SWR to convert into LWR of GTJT Line no. 3,GADJ line no.1&4 DPA line no.2/3 , line no.1&3 of SNGN&SAS.	10567	7258	Work completed and Final bill passed. Completion report Certified by finance and attached. work may be deleted
377.	31	LB-201	MD-HP & AII-COR sec-Renewal of existing SEJs (52Kg./ 90 UTS) by Improved SEJs (52Kg./ 90 UTS) (60sets)	17507	0	Work completed and will be proposed for deletion after material booking.
378.	31	LB-202	ADEN-MJ Sub Div-Renewal of Worn out CMS crossings & Worn out Switches.	19278	1507	Work will be done departmentally. 17 set Thick web Switch Allotted to ADEN/MJ = 06 Sets, ADEN/ABR = 06 Sets & ADEN/FA = 05 sets on 29.08.22
379.	31	LB-203	MD-PNU section-Construction of pucca trolley refuges. (165 Nos)	9938	0	Masonry trolley refugees were proposed to be constructedin this work. Some work has been done. However as per Item No 3.12 of GM/NWR LV inspection note dated 06.07.20 of ABR-MD-JP section it was instructed to make trolley refugees using released sleepers instead of masonry work as they are more economical and durable. At present no further scope. Final variation sanctioned. Final bill awaited
380.	31	LB-204	COR-UDZ section-Renewal of Glued joints in COR-UDZ section	7251	1116	Glued joint material recieved. NIT has been floated tender to be opened LOA issued on 21.02.23. Final bill passed.
381.	31	LB-207	Rewari~~Jaipur~~Sr. DEN/East jurisdiction-Through fitting renewal of yards including Points & crossings 52 Kg/ 60 Kg	9664	9631	Work completed. F/Bill passed. Completion report certified by finance and attached. work may be deleted
382.	31	LB-219	Deep screening of DN main line bet. BAI-JP and T/O on DN-Line bet.BAI-JP and Main running line in yards including T/O deep screening bet.CKS-JP.	9887	6541	Work Completed. F/bill passed. GST difference bill passed. Completion report certified by finance & attached. work may be deleted
383.	31	MLB	Rousing of corroded ERCs and greasing of free rail screws on Point and crossing in AII-COR-UDZ sec	2934	167	Work completed and final bill under process. Work terminated on 23.02.2024.

384.	31	MLB	Providing Track machine siding at Sareri (SSR).	12307	1924	Track laid only connection is to be done with dead end for which 1:8.5 RHS Right hand turnout is available but agency is not turned up.
385.	31	MLB	Providing Track machine siding at Gangrara (GGR).	12307	5215	Doubling of Ajmer-chittaurgrh section is sanctioned and TMC siding is taken in Gangrar yard to be done with yard remodeling work as if the work is carried out now then five numbers of junction boxes needs to be shifted. Hence work will be proposed for deletion.
386.	31	MLB	Deep screening of point and crossing between HP-PNU section.	24714	6437	Discharged due to very high rates. NIT issued tender opened on 01.03.2022, discharged. Re tender opened on 13.05.2022, LOA issued on 27.06.22. As per HQ manual deepscreening work to be reviewed, Approval of New items sanctioned, variation sanctioned, Contract terminated.RE sanctioned .Tender invited and opened on 25.06.2024, LOA issued on 27.06.2024, Work in progress
387.	31	MLB	Daurai-Rewiring of old CSM machines 925 & 944 and schedule maintenance of track machines of N. W. R.	9011	1402	Work completed, final variation is under accounts vetting.
388.	31	MLB	Development of Satellite Track Machine Depot at Daurai.	24910	14340	Location has been changed to Marwar jn. in place of Daurai in compliance of HQ Letter No. W/722/19-20/LAW/PH-31/Tr. dated 30.01.2020.Estimate is under Accounts Vetting. ESP alteration under process. Detail Estimate for Civil Portion sanctioned on 30.05.2022, Tender invited vide tender no. 80-2022. No Bid Received, Re tender vide tender no 96-2022, Tender opened on 27.07.2022, Discharged, Re tender opened on 03.10.22, LOA issued on 21.10.22, Work Completed
389.	31	MLB	Casual renewal of Rails in the Jurisdiction of SSE/P.Way / Rani (2.20 Km)	24913	0	Detail Estimate sanctioned on 02.09.2022. Tender invited and opened on 03.10.22, 01.11.22 and 02.12.22 no bid received. Again, reinvited and opened on 26.12.22, Discharged, Reinvited , Date of opening : - 14.02.23,no

						bid received, again invited and opened on 10.03.23,Discharged, Again invited and opened on 02.06.2023, NO Response, Revised Estimate sanctioned, Retender opened on 04.08.2023, No bid received. tender Re-Invited, no response, Again Invited Tender opened on 30.11.23, LOA issued, WIP
390.	31	MLB	SSE/P.Way/ABR Section - TRR(S) in the loop lines	24925	936	Detail Estimate sanctioned. Tender invited clubbing with other TRR(S) works, Date of opening 14.11.2022, no bid received, Tender Re-Invited and opened on 07.12.22, Discharged, Reinvited , Date of opening : - 01.02.23, no bid received, Re- tender opened on 28.02.2023, discharged, Retender opened on 12.05.2023, LOA issued on 27.06.2023, Work in progress
391.	31	MLB	Ajmer-Chittourgarh section-Proposal for providing of Joggled plate on all AT Welds.	7979	1473	Work is physically completed, and final bill and final variation is under preparation.
392.	31	MLB	Ajmer-Chittorgarh-TRR(P) - 2.59 Tkm.	26251	8415	Work completed and final variation submitted for acceptance.
393.	31	MLB	SSE/P.WayABR Section - TSR(S) in Loop lines	21369	1957	LOA issued on 15.03.2023 and work in progress.
394.	31	MLB	ADEN/ MJ Sub Division -Deep screening of Track in Main line. (3.209 Km)	9043	3446	Detail Estimate sanctioned. Tender Invited and opened on 07.12.22,LOA issued on 03.01.23, terminated, work done departmently
395.	31	MLB	Ajmer - Chittorgarh - TRR & Casual renewal of Rails	13035	349	Work completed and final variation is submitted for acceptance.
396.	31	MLB	TRR(S) in the loop lines in the Jurisdiction of SSE/P.Way/Sojat Road - 3.562 Km	24759	1064	Detail Estimate sanctioned on 02.09.22, Tender invited opened on 03.10.22, Discharged due to higher rates, again invited clubbing with other TRR(S) works, T. no 154-2022, Tender opening date: - 14.11.2022 ,no bid received, Tender Re-Invited and opened on 07.12.22, Discharged, Reinvited , Date of opening : - 01.02.23, no bid received, Re- tender opened on

						28.02.2023, Discharged, Retender opened on 12.05.2023, LOA issued on 27.06.2023, Work in progress
397.	31	MLB	TRR(S) in the loop lines in the Jurisdiction of SSE/P.Way/Rani - 1.932 Km	13663	1226	Detail Estimate sanctioned on 02.09.22. Tender invited opened on 03.10.22, Discharged due to higher rates, again invited clubbing with other TRR(S) works, T. no 154-2022, Tender opening date: - 14.11.2022, no bid received, Tender Re-Invited and opened on 07.12.22, Discharged, Reinvited , Date of opening : - 01.02.23, no bid received, Re- tender opened on 28.02.2023, Discharged, Retender opened on 12.05.2023, LOA issued on 27.06.2023, Work in progress
398.	31	MLB	ADEN/MJ Jurisdiction : - TSR(S) in Loop lines.	10643	0	Detail Estimate sanctioned. Tender Invited and opened on 07.12.22, LOA issued on 03.01.2023, again opened and LOA issued and work in progress
399.	31	MLB	Casual renewal of Rails in the jurisdiction of SSE/P.Way/Sojat Road (2.20 Km)	24913	0	Detail Estimate sanctioned on 02.09.22. .Tender invited opened on 03.10.22, 01.11.22 and 02.12.22 no bid received. Again, reinvited and opened on 26.12.22, Discharged, Reinvited , Date of opening : - 14.02.23,no bid received, again invited and opened on 10.03.23, Discharged. Again invited and opened on 02.06.2023, NO Response, Revised Estimate sanctioned, Retender opened on 04.08.2023, No bid received, tender Re-Invited,no response, Again Invited Tender opened on 30.11.23, LOA issued on 07.12.23
400.	31	MLB	Madar - Ajmer DN line - TBR -- 4.60 Km	14651	11177	TBR Work completed.this work was clubbed with other work.hence it will be deleted after completion of other works.
401.	31	MLB	Ajmer- Chittourgarh - TRR(P) - 2.03 Tkm.	20588	1728	work physically completed and final variation is submitted for acceptance.

402.	31	MLB	Madar,Ajmer & Daurai Yard - TRR(S) - 3.53 Tkm (Loop Lines)	24924	1420	Work has been physically completed
403.	31	MLB	Ajmer-Chittorgarh - TRR(P) - 2.13 Tkm.	21596	5449	Work completed and final variation is submitted for acceptance.
404.	31	MLB	CPWI/PDWA Section - TSR(S) in Loop lines - 1550 TRM	12886	866	LOA Issued on 15.03.2023 and work in progress.
405.	31	MLB	TRR(S) in the loop lines in the Jurisdiction of SSE/P.Way/PDWA - 1.515 Km	12829	0	Detail Estimate sanctioned. Tender invited clubbing with other TRR(S) works, Date of opening 14.11.2022, no bid received, Tender Re-Invited and opened on 07.12.22, Discharged, Reinvited , Date of opening : - 01.02.23, no bid received, Re- tender opened on 28.02.2023, Discharged, Retender opened on 12.05.2023, LOA issued on 27.06.2023, Work in progress
406.	31	MLB	Ajmer-Chittourgarh section - TTR (TWS+CMSC)- 15 sets (Part -II)	23678	0	Work is completed and final variation is awaited.
407.	31	MLB	Ajmer yard:- Provision of Ballasted Track in lieu of CC Apron Track with new sleepers and fittings at Line no. 1&2	24999	0	Work in progress
408.	31	MLB	Chittaurgarh - Udaipur- Casual renewal of switches and crossings.	14986	0	Detail estimate sanctioned. NIT opened on 25.07.24. Tender discharged and reinvited to be opened on 13.09.24
409.	31	MLB	Sr.DEN/West Jurisdiction - Reconditioning of Wornout SEJ, CMS crossing & Switches.	4128	0	Detail Estimate sanctioned on 19.03.2024,NIT under preparation
410.	31	MLB	Chittaurgarh - Udaipur - TRR (S), ISD and Deepscreening of Loop line no 5,6 of Udaipur City Station.	14286	0	Tender opened on 25.07.24. Tender discharged and reinvited to be opened on 13.09.24

411.	31	MLB	Provision of WCMS crossing between Madar-Palanpur section in connection with raising of speed	23868	0	Detail estimate sanctioned & Tender invited opened on 28.06.2024, Discharged, again invited and opened on 12.08.2024, no bid received, again invited and will open on 09.09.24
412.	31	MLB	ADEN/Abu Road Jurisdiction - TTR(TWS) - 12 nos. in Madar - Palanpur Section	24478	11955	Detail Estimate Sanctioned , Tender invited, Opened on 30.11.23, LOA issued on 07.12.23
413.	31	MLB	ADEN/Falna jurisdiction - TTR(TWS) - 12 nos. in Madar - Palanpur Section	24478	2753	Detail Estimate sanctioned, Tender invited, Opened on 30.11.23, LOA issued on 07.12.23, Work in Progress
414.	31	MLB	ADEN/Marwar Junction - TTR(TWS) - 12 nos. in Madar - Palanpur Section	24478	2753	Detail Estimate sanctioned on 22.08.2023, Tender invited, Opened on 30.11.23, LOA issued on 07.12.23, Work in progress
415.	31	MLB	Ajmer-Chittaurgarh section - TTR (TWS+CMSC)- 14 sets (Part -I)	21835	3211	Work completed and final variation is awaited.
416.	31	MLB	Improvement to Fastening and Fittings of Channel Sleepers on Girder Bridges on Madar - Palanpur Section	2991	0	Detail Estimate under Preparation
417.	31	MLB	Provision of TWS in AII division.	24527	2753	Detailed estimate is Sanctioned, and work is required for material procurement only.
418.	31	MLB	AII yard:Repl of sleepers due to slacking gauge and providing check rail & ADEN/L-Repl of Sleeper of P&C =06Set	22785	6355	work in progress
419.	31	MLB	Chittaurgarh - Udaipur - Renewal of SEJs	9976	0	Detail estimate sanctioned. LOA issued on 09.11.2023. Work in progress.
420.	31	MLB	Ajmer Division - Various P Way material for Casual Renewal in Ajmer Division.	24498	0	Detailed estimate is sanctioned and procurement of material is under process.
421.	31	MLB	Ajmer Division : - Requirement of Welding Portions and Equipment	14993	0	DE sanctioned and work is only for material procurement.

422.	31	MLB	Chittaurgarh - Udaipur- Casual renewal of switches and crossings.	11993	0	LOA issued on 09.11.2023. Work in progress.
423.	31	MLB	Chittaurgarh - Udaipur - Conversion of fish plated loop lines into LWR - 9.92 km	23972	111	Tender of welding portion invited on 28.07.23. No bidding was received and new tender was floated on 12.08.23 and opened on 04.09.23. LOA issued on 06.11.2023. LOA of remaining portion issued on 09.11.23. Work is in progress.
424.	31	MLB	Ajmer Division : - Renewal of ordinary SEJs with improved SEJs	19956	4225	Detail Estimate sanctioned on 18.08.2023, Tender invited, Opened on 30.11.23, LOA issued on 07.12.23, Work in progress
425.	31	MLB	Bathinda~~Replacement of worn out Rubber Pad in the RE-BTI section in the jurisdiction of DEN/East.	29027	21070	Contract awarded for 91 Km. Contract proposed for short closure due to non availability of material since long. Final bill paid in May 23. Tender opened on 06.11.23 & awarded on 30.11.23
426.	31	MLB	Bhiwani - Hisar - TBR - 17.50 Kms.	27002	22826	Contract short closed due to non availability of BCM since long. Final variation approved. Final bill paid in Nov.22. Balance work tender (TBR 88.375 Km) opened on 25.08.23 & 04.12.23 but discharged . Re-tender opened on 15.02.24 & finalised on 02.05.24. Work is in progress.
427.	31	MLB	Rewari-Bhiwani - TBR - 13.22 Kms.	36189	34769	Contract short closed due to non availability of BCM since long. Final variation approved. Final bill paid in Nov.22. Balance work tender (TBR 88.375 Km) opened on 25.08.23 & 04.12.23 but discharged . Re-tender opened on 15.02.24 & finalised on 02.05.24. Work is in progress.
428.	31	MLB	Lalgarh~~Development of sattelite track machine depot at Lalgarh.	29663	17234	"RCC OH Tank- work completed. Final bill paid in March 22. Water Softening Plant commissioned. Final bill to be paid. Provision of shed work comp. Final bill paid in June 22. Indents of various track machine items submitted. Material partly received.

						Elect. Work completed.
429.	31	MLB	Deep screening of T-outs 1 in 12 by manually in the jurisdiction of Sr.DEN/East (55 Nos.)	9480	6199	"36 no. T/out completed. Work stopped & short closed as per instruction of HQ office. Final bill paid in Jan.23. Ballast supply (55000/6875 cum)-supply completed ."
430.	31	MLB	Ratangarh - Churu - TFR - 42.77 km (42.77 km GRSP, 7.20 km GFN Liner& 35.57 km Metal Liner)	24533	6965	Work completed. Final bill paid in May.24. Material booking to be done.
431.	31	MLB	Churu - Sadulpur - TFR - 45.32 Km (45.32 km GRSP, 8.88 km GFN Liner& 36.44 km Metal Liner)	25865	3196	Work completed. Final bill paid in May.24. Material booking to be done.
432.	31	MLB	Suratgarh - Lalgarh - TBR - 6.05 Km	23601	0	"Work completed. Bap Depot (8470/97258) cum-tender opened on 10.05.23 & awarded on 19.10.23. Supply is in progress"
433.	31	MLB	Suratgarh - Lalgarh - TSEJ (60Kg) - 15 Sets & TSEJ (52 Kg) - 11 sets	13032	0	"Work completed. Material booking being done.
434.	31	MLB	Flash But Welding at BKN, LGH and KLYT Yard for conversion of Passenger Loop lines to LWR under jurisdiction of Sr.DEN/West	6234	0	Work sanctioned on 12.10.23. Detail estimate sanctioned on 31.10.23. Tender opened on 29.11.23 but discharged. Re-tender opened on 16.01.24 but no response.
435.	31	MLB	Installation of Intelligent field devices in existing installed CRTs over BKN division.	3557	0	Work sanctioned on 12.10.23. Detail estimate sanctioned on 27.10.23. Tender opened on 02.02.24 & awarded on 28.04.24. Installation work is in progress.
436.	31	MLB	Provision of extension of goods line /oc siding including TR (S) work in c/w Ballast depot at Ramsinghpur.	13070	0	Contract awarded on 19.01.24. Work is in progress.
437.	31	MLB	Improvement to cess in Hanumangarh-Gogameri & Sarupsar-Hanumangarh (CLL) section over Bikaner division.	24179	0	Work sanctioned on 27.10.23. Detail estimate sanctioned. Tender opened on 24.06.24 & under TC.

438.	31	MLB	Provision of tool cum rest room in the jurisdiction of ADEN-Ratangarh.	21964	0	Work sanctioned on 27.10.23. Detail estimate sanctioned. Tender 05.04.24 & awarded on 07.05.24. Work is in progress.
439.	31	MLB	Provision of tool cum rest room in the jurisdiction of ADEN-I/Hanumangarh.	21964	0	Work sanctioned on 27.10.23. Tender opened on 01.03.24 & awarded on 09.04.24. Work is in progress.
440.	31	MLB	Improvement to cess in Hanumangarh-Suratgarh section over Bikaner division.	27272	0	Work sanctioned on 27.10.23. Detail estimate sanctioned. Tender floated & to be opened on 24.06.24 but cancelled.
441.	31	MLB	Replacement of H-Beam sleeper and chequered plate at Bridge no. 02, 25 & 72 in Suratgarh-Anupgarh section	11992	0	Work sanctioned on 27.10.23. Tender opened on 15.12.23 & awarded on 19.01.24. Work completed.
442.	31	MLB	Churu - Ratangarh - TTR (TWS) - 14 Nos	17431	0	Work sanctioned on 29.11.23. Detail estimate sanctioned on 08.05.24. Tender opened on 25.07.24 & under TC.
443.	31	MLB	Sadulpur-Bikaner-Deep Screening of Turnouts 70 sets.	28608	0	Work sanctioned on 29.11.23. Detail estimate sanctioned on 24.05.24. Tender opened on 25.07.24 & under TC.
444.	31	MLB	Sadulpur - Churu - TTR (TWS) - 15 Nos	19902	0	Work sanctioned on 29.11.23. Detail estimate sanctioned on 08.05.24. Tender opened on 25.07.24 & under TC.
445.	31	MLB	Replacement to existing failed glued joints by making G-3 (L) type glued joints as per RDSO drawing for 52 kg/60 kg rails with all fittings etc.	5101	0	Work sanctioned on 29.11.23. Tender opened on 23.01.24 &awarded on 01.02.24. Work is in progress.
446.	31	MLB	Suratgarh-Bikaner - deep screening of turnouts 43 sets.	23264	0	"Tender opened on 23.01.24 & awarded on 09.02.24. 20 T/out completed. Work is in progress. RMSR depot 39045/4945 cum-tender opened on 07.05.24 & awarded on 29.07.24."
447.	31	MLB	TSEJ (60Kg) - 14 Sets & TSEJ (52 Kg) - 25 sets of main line section under the jurisdiction of Sr. DEN/West, Bikaner.	24301	0	Work sanctioned on 27.12.23. Detail estimate sanctioned on 21.02.24. Tender opened on 21.03.24 but no offer received. Re-tender opened on 25.04.24 & awarded on 10.05.24. Work is in

						progress.
448.	31	MLB	Hisar - Bathinda - TGJ renewal - 80 Nos.	6723	0	Work sanctioned on 29.01.24. Detail estimate sanctioned on . Tender opened on 11.06.24 & awarded on 28.06.24.
449.	31	MLB	Improvement to cess by providing catch water drain, retaining wall, etc. at various locations in SDLP-BKN, RTGH-SRDR & RTGH-DNA sections	23618	0	Work sanctioned on 29.01.24. Detail estimate sanctioned. Tender to be opened on 14.08.24.
450.	31	MLB	Jaipur~~Sawaimadhopur~~ADEN (Line) JP Sub Div:- CTR work at bridge no 23 (549 RM.)	33986	32949	Work near completion.
451.	31	MLB	Bandikui~~Development of satellite track machine depot at BKI.	23995	11040	Engg. Work awarded on 07.10.2022 and Engg. work completed & FVS under sanctioned
452.	31	MLB	Jaipur~~Bandikui~~ADEN/BKI Sub Div:- CTR work at BKI Yard DN M/Line = 1.5 km.	32735	32643	Work completed. FVS & final bill awaited from ADEN/BKI
453.	31	MLB	Rewari~~Ringas~~RP C-Section TRR(P) – 3 km on major bridges (Br. no. 112A, 135, 163, 164, 184, 191, 193, 201, 203, 220 & 221B).	25000	11066	Work Completed. Final bill passed. Material to be booked
454.	31	MLB	Bandikui~~ADEN/BKI Sub Div:- CTR work at approach of BKI yard at AWR end = 1.5 km.	25092	13746	Work completed. FVS & final Bill awaited from ADEN/BKI.
455.	31	MLB	Jaipur~~Bandikui~~Baswa~~ADEN/BKI Sub Div:- CTR work in SSE/PW/II BKI Juridiction between BKI-BU = 1.5 km.	24975	23790	Work completed. FVS & final bill awaited from ADEN/BKI

456.	31	MLB	Jaipur – Sawaimadhopur – TRR (P) from Km 26.00 to 27.76 = 1.76Km	19308	18383	Work Completed. Completion report under process
457.	31	MLB	Sr.DEN (E) Section - TSR(P) 1.50 Km (Bandikui-Jaipur - UP line)	17315	0	Tender opened on 28-11-23 and work awarded on 22-2-2024
458.	31	MLB	NNL& Dabla station yard (RPC Section - Main line) TRR(P) - 0.750KM	17659	170	Work awarded on 27-1-23. Work is in progress. Material to be booked
459.	31	MLB	Jaipur - Sawai Madhopur - CTR - Bridge No. 40 and Renewal of fitting of steel girder bridge no. 223 Dn Line.	5478	106	Work awarded on 23-11-22 and work is in progress
460.	31	MLB	JP Division: TRR, TFR of loop line-6 in JP yard and deep screening of loop line-4 in GADJ yard and loop line-6 in JP yard.	9877	1802	Work awarded on 7-4-23 & Work is in progress
461.	31	MLB	KUND & PALI station yard (RPC Section - Main line) TRR(P) - 0.750KM	20987	8998	Work awarded on 27-1-23. Work is in progress
462.	31	MLB	RGS & SMPR station yard (RPC Section - Main line) TRR(P) - 0.750KM	17659	9828	Work awarded on 27-1-23. Work is in progress
463.	31	MLB	Rewari - Bhiwani (DN) - TRR(P) - 0.961 Km	17315	0	Work awarded on 22-2-2024.
464.	31	MLB	FL Yard - Replacement of Turnout 1 in 8.5 to 1 in 12	16929	1817	Work awarded on 20-2-2023 & Work will be done after NI
465.	31	MLB	Provision of P.Way Materials for Casual Renewals by CMSC 1:12 & 1:8.5 of 60Kg & 52 Kg over JP division	27721	0	Detail estimate sanctioned. Material schedule under process
466.	31	MLB	ADEN-BKI & ADENHQ-II sub division-Through renewal ofexisting channel sleepersby providing H-Beamsleepers at bridges.	24982	0	Detail estimate sanctioned and Tender opened on 6-5-24 and under finalization
467.	31	MLB	JP-VHF based approaching train warning system	24844	0	Detailed estimate sanction. Tender opened on 22-5-24 and work awarded on 14-8-24

			(RAKSHAK) for trackmen in RE-JP.(Total- 30 Nos)			
468.	31	MLB	Rewari~~Jaipur: - Pre & Post tamping Track measurements using Gedo Vorsys trolley system in Up line & Dn line(452 Tkm.)	23170	0	Detailed estimate sanctioned. NIT is under process
469.	31	MLB	Sr.DEN/S/JP section standardization of cess width & trolley refuses & Removal of false cutting and standardization of cess and in	23969	0	Tender opened on 12-1-24 and work awarded and work is progress
470.	31	MLB	Through ERC renewal work for 20 TKM between BKI -BAI stations.	24158	0	Detailed estimate sanctioned and NIT under process
471.	31	MLB	DEN(East) JP DIV: TSR(P) works for Bridges no.195 UP, 138 UP&DN, 178 UP and remaining from plain track at km. 169/0-171/0 UP line in BKI-JP Section.	24501	0	Detailed estimate sanctioned and NIT under process
472.	31	MLB	Phulera~~Madar Jn.~~ADEN/FL Sub Division :- Drainage improvement work in FL yard and Km 294/6 to 295/9, 214/7 to 215/3 etc. FL-RNW and FL-MD Section.	24539	0	Detailed estimate sanctioned and Tender opened on 12-1-24 and work awarded
473.	31	MLB	Casual renewal work of Glued Joint in between RE-BAI stations. (Total 120 New & 700 Nos. Refurbishment).	24998	0	Work awarded and in progress.
474.	31	MLB	Jaipur~~Bandikui~~JP-Div. - TRR (P) with 60 KG in UP Main line 1.035Km bet JP BKI section.	13094	0	Detailed estimate sanctioned and NIT is in process

475.	31	MLB	Jaipur~~Bandikui~~JP Div. – TTR & TTSR (Through Turn Out Sleeper Renewal) with 60 KG PRC Sleepers of P&C of 1 in 12(8 nos.)	18538	0	Detailed estimate sanctioned and Tender opened on 19-6-24 & under finalization
476.	31	MLB	Rewari - Alwar Section - TRR (P) from Km 47/150 to 48/320 (UP Line) and Km 40/700 to 41/400 (DN Line) (Total-1.870km).	23659	0	Detailed estimate sanctioned and NIT is under process
477.	31	MLB	Sr.DEN/S section-Various Pway Material for casual renewal such as SEJ, Glued Joints, Fittings, Switch, Crossings etc.	24887	0	Detailed estimate sanctioned . M S under process
478.	31	MLB	Jaipur~~Bandikui~~JP Div. – TTR & TTSR (Through Turn Out Sleeper Renewal) with 60 KG PRC Sleepers of P&C of 1 in 8.5(9 Nos)	17962	0	Detailed estimate sanctioned and Tender opened on 19-6-24 & under finalization
479.	31	MLB	Jaipur~~Bandikui~~JP-Div. - TRR (P) with 60 KG in DN Main line 0.345 Km bet JP BKI section.	4365	0	Detailed estimate sanctioned and Tender opened on 19-6-24 and under finalization
480.	31	MLB	Jaipur~~Bandikui~~JP-Div. CTR (P) of UP Main line 1.116 Km Bet. JP-BKI Section(Km 0.947 Km. at GADJ by 60 KG & 0.169 Km in JP yard by 60 KG)	24933	0	Detailed estimate sanctioned. Tender opened on 19-6-24 & under finalization
481.	31	MLB	Provision of P.Way Materials for Casual Renewals by ISEJ 80mm & 65 mm of 60Kg & Glued Joint 60 Kg over JP Division	22936	0	Detailed estimate sanctioned and Material schedules prepared and under process

482.	31	MLB	Pre & Post tamping Track measurements using Gedo Vorsys trolley system in Up line & Dn line in in JP-MD & JP-SWM & RE-FL(RPC) section (470Tkm)	23730	0	Detailed estimate sanctioned and NIT under process
483.	31	MLB	JP-VHF based approaching train warning system (RAKSHAK) for trackman in in JP-SWM & JP-MD & JP-RGS-NMK.(As per RDSO Specification)	24942	0	Tender opened on 22-5-24 and under finalization
484.	31	MLB	Provision of P.Way Materials for Casual Renewals by 1:12 & 1:8.5 of 60Kg & 52 Kg Fittings over JP Division	28238	0	Detailed estimate sanctioned. Material schedules prepared and under process
485.	31	MLB	Merta road~~Bikaner~~Strengthening of loop lines in the MTD - BKN section	9318	0	work is in progress.
486.	31	MLB	Luni~~Samdari~~Bhildi jn.~~Renewal of Switches of Main line on age cum condition basis in Luni - Samdari - Bhildi section.	24669	0	Work is completed.
487.	31	MLB	Merta road~~Bikaner~~Proposal for machine siding along with resting facilities at Nokha station of MTD-BKN Section of ADEN/MTD	12307	2593	Work physically completed, final bill paid, PG & SD relesed.
488.	31	MLB	Samdari~~Bhildi jn.~~Proposal for machine siding along with resting facilities at Raniwara station of SMR-BLDI Section of ADEN/SMR	12307	4295	Work Completed. Final Bill Passed. PG released and SD/EMD to be released.
489.	31	MLB	Proposal for machine siding along with resting facilities at Osian and Ramdevra station of Raikabagh-Jaisalmer section of ADEN/JSM.	24614	6052	Work in progress

490.	31	MLB	Casual renewal of rails and renewal of fittings on Steel girder bridges in RKB-JSM Section	24895	14399	Work in progress
491.	31	MLB	ADEN/Line, Jodhpur Renewal of special bridge sleepers on bridges, ROB's & FOB's	21000	8014	due to CTR it is drop
492.	31	MLB	Ratangarh - Degana - Replacement of 24 switches & 26 crossing	24474	7347	Work in progress.
493.	31	MLB	Increasing sleeper density in HWT, SZ, BANE, RT arid BGKT loop lines	19428	0	Work awarded on 04.01.2024
494.	31	MLB	Samdari~~Munabao~~ Removal of PSR of curve No 75,79 and 92	24500	0	Work completed at Curve 75,79 and 92.
495.	31	MLB	Improvement of of Salawas yard by shifting of existing crossover .	17999	0	estimate under preparation.
496.	31	MLB	Jodhpur - Marwar Section - Provision of standard type sleepers on level crossings and deep screening	15000	0	Tender under process.
497.	31	MLB	Samdari - Bhildi - Casual Renewal of Turn out sleepers (45 sets) on main line	24238	0	Tender awarded, material required
498.	31	MLB	Samdari~Bhildi jn.~ADEN/Samdari Section Rail Renewal (2350 Track meter) on Steel Girder bridges	24789	0	Tender awarded, Rail required.Work in progress.
499.	31	MLB	ADEN/Samdari Section- Rail renewal (2325Track meter) on bridges	117713	117713	Tender awarded, Rail required.Work in progress.
500.	31	MLB	Raikabagh -Jaisalmer Casual renewal of rails in SSE/P.Way/PLC section	24800	1098	Work in progress
501.	31	MLB	Samdari~~Munabao~~ Removal of PSR of curve No 17 and 72	22004	14885	Work completed at curve 72 and in progress at curve 17.
502.	31	MLB	LN-SMR-BLDI-Replacement of Rail, weld & Fitting in Turn-out X-ing portion	24381	0	Tender awarded, material required
503.	31	MLB	Luni - Samdari - Conversion of loop	24303	2735	Work completed at 8 loop lines

			lines into LWR			and in progress at 2 loop lines.
504.	31	MLB	Raikabagh -Jaisalmer - Casual renewal of rails in SSE/P.way/JSM section	24895	0	Work in progress
505.	31	MLB	Bhgat Ki Kothi Goods siding & Defence yard TRR(S) - 3.68 KM	24498	0	Tender under process.
506.	31	MLB	Development of Satellite Track Machine Depot at Basani.	24903	0	Work in progress
507.	31	MLB	Replacement of Curved Switch & CMS Crossing in LN-SMR-BLDI section under ADEN/SMR	24273	0	Estimate under preparation.
508.	31	MLB	Strengthening of loop line by conversion of SWR into LWR 52kg under ADEN/DNA	27231	0	Detailed estimate sanctioned &tender to be opened on 23.08.2024
509.	31	MLB	Replacement of SEJ in LN-SMR-BLDI section under ADEN/SMR	24753	0	Detail estimate under prepration
510.	31	MLB	Strengthening of loop line by conversion of SWR into LWR 52kg under ADEN/MTD	27221	0	Detailed estimate sanctioned. Tender opened on 23.08.2024
511.	31	MLB	Replacement / Renewal of SEJs, in RKB-JSM Section under ADEN/JSM..	24268	0	Detail estimate under prepration
512.	31	MLB	Replacement / Renewal of Glued Joints in RKB-JSM Section under ADEN/JSM.	24854	0	Estimate under process
513.	31	MLB	Utarlai~~Barmer~~Proposal for pitching of bank of Railway track at breach prone location from km 831/6 to 833/5 in BME-UTL section of ADEN/BME .	19365	2449	work in progress
514.	31	MLB	Through Weld Renewal	23854	2546	Estimate under preparation.
515.	31	MLB	Raikabagh~~Pokran~~ Through Weld Renewal	23854	0	Estimate under preparation.

516.	31	MLB	Phulera~~Merta road~~Replacement of Low insulation Glued joint 60 kg under ADEN/DNA	6633	0	Work in progress.
517.	31	MLB	Degana~~Through renewal of switch & crossing of 1;8.5 52 kg to TWS 1;12 60 Kg under ADEN/DNA	3295	0	Estimate under preparation.
518.	31	MLB	Makrana~~Merta road~~Through renewal of switch & crossing of 1;12 52 kg to TWS 1;12 60 Kg under ADEN/DNA	14826	0	Estimate under preparation.
519.	31	MLB	Replacement of Low insulation Glued joint 52 kg under ADEN/DNA	22040	0	Work in progress.
520.	31	MLB	Merta road~~Bikaner~~ Replacement of Switche & Crossing of SSE/P.way/NGO in MTD-BKN section under ADEN/MTD	17194	0	Tender under proses.
521.	31	MLB	Merta road~~Bikaner~~ Replacement of Switche & Crossing of SSE/P.way/NOK in MTD-BKN section under ADEN/MTD	16182	0	Tender under proses.
522.	31	MLB	Casual Rail renewal on curves (2.35 Km.) on condition basis (wear) at isolated locations on SMR-BLDI section in the jurisdiction of ADEN/Samdari	24835	0	Estimate sanctioned and material indents placed.
523.	31	MLB	Samdari:-Renewal of chequred plates on girder bridged in the jurisdiction of ADEN/Samdari	13480	0	Estimate sanctioned and tender is to be invited.
524.	31	MLB	Improvement to Facilities in track machine siding over jodhpur division	23800	0	Estimate sanctioned &under tender invitation.
525.	31	MLB	Provision of Improved SEJ over Jodhpur division	24753	0	Estimate sanctioned, tender to be invited.
526.	31	MLB	Replacement of low insulation glued joints 52 kg in the jurisdiction	24192	0	Estimate under preparation.

			of DEN/West			
527.	31	MLB	Strengthening of loop line by conversion of SWR to LWR 52 Kg in the section of SSE/PW/MKN& SUJH Under ADEN/DNA	24962	0	Estimate under preparation.
528.	31	MLB	Repair to washable aprons at Jodhpur station	20000	0	Estimate under preparation.
529.	31	MLB	Deep screening and associated works in RKB,JU yard.	19997	0	Estimate under preparation.
530.	32	PB-282	Delhi-Rewari - Repl of bridge No.100 & Rewari-Hisar - repl of bridge No.1	27400	4619	The work of bridge no.100 has been dropped with approval of competent authority and Work for rehabilitation of bridge no.01 has been awarded on 22.10.2021. The Work is in progress. The work is terminated on 14.03.2022 due to no executing the work & non executing the contract agreement. Now fresh NIT is proposed for tender. Tender opened on 31.05.2022 but no bid received. Now retender will be done for proposed work. Tender opened on 30.06.2022 Again, The tender discharged and retender not done.
531.	32	PB-281	Samdari-Bhildi - Provision of bridges & protection works at various breaches sites	111623	120265	Work is physically completed and final bill is passed, Work proposed for deletion on IRPSM.
532.	32	PB-280	Madar - Palanpur - Rehabilitation / rebuilding (60 bridges)	258883	224156	Out of 60 bridges, 57 Bridges work Completed. Work in Progress on balance 03 Bridges, Br No 602,690, 841. Br 690 & 841 BOX casted. Launching to be done. 602 Drawing to be approved. Br 602 GAD under preparation with Interning
533.	32	PB-279	Jethi-Chitrasani - Regirdering & strengthening of sub structure (bridge No 845)	270013	201661	Physically work has been completed. Final variation under accounts vetting.
534.	32	PB-124	Madar-Palanpur - Rebuilding / strengthening of bridges (up line) in connection with running of higher loads and	325916	0	Total 41 bridges in scope. 01 Bridge does not exist at site. Work to be done at 40 bridges. Plans are under sign at division/HQ approval. All bridge plans are not finalized/ approved.

			higher speed (41 bridges)			Detail Estimate sanctioned. Tender invited for 15 Bridges and cancelled, Again invited on 01.03.2024 for phase I (15 Bridges, list in attachment), Discharged again invited and opened on 24.05.2024, No bid received, Again invited and opened on 20.06.2024, no bid received. Again invited and opened on 19.07.2024
535.	32	LB-266	AII Div-Reb/Streng. of GC standard Bridges on MD-PNU (Up ln.) in c/w running of higher loads and speed (Br. No.336,351,407,437 & oth.)	16925	516	Contractor is unable to complete the work and not agree to execute the work Hence work contract is terminated. Revised estimate is sanctioned and Tender uploaded and opened on 27.08.2024
536.	32	LB-265	AII Div- Reb/Streng. of GC Stnd. Br. on MD-PNu(UP ln.) in C/w runn higher load/speed (Br. No. 545)	13650	4032	GAD approved. Detail Estimate Sanctioned. LOA issued on 04.09.2023. Jacketing of Piers and abutments completed. Retainers, bed blocks and PSC slab launching done in June-24. Re-strengthening work is omplete. Contractual liabilities to be cleared.
537.	32	LB-264	AII Div- Reb/Stren. of GC Stnd Br. on MD-PNU (UP Ln.) in C/w Runn. of higher load & Speed (Br. No.552,561,677 & oth)	24062	2590	Contract awarded. Total Scope of 3 Bridges. 1. GAD approved of Br No 552,561,677 2. Box casting completed of Br 552,561 & 667 3. Launching to be done of all bridges.
538.	32	LB-263	AII Div-Reb/Streng. of GC Stnd. Br. on MD-PNU (UP Ln.) in c/w with Runn. of higher load & Speed (Br. No.558,667,717,718 & oth)	23903	17	Contract awarded. Total Scope of 4 bridges. 1. GAD approved for 667,717,718. 2. Br 558 GAD under approval (Skew bridge in BQN Yard) 3. Box casting done at Br 717,718,667 4. Launching to be done at all bridges
539.	32	LB-262	AII Div. -Reb. /Stren. of GC Stnd. Bridges in MD- PNU (UP Line) in C/W running Higher load and Speed. (Br. No.725, 735, 742, 744, 756, 771, 782 & oth)	19017	5907	LOA issued on 28.05.2021. Total 7 bridges in this work. Work completed at all 7 bridges (Br. No.725, 735, 742, 744, 756, 771, 782) Contractual liabilities to be cleared.

540.	32	LB-261	Rebuilding / Strengthening of GC standard Bridges in MD-PNU (Up line) in connection with running of higher loads and higher speed.	19512	9555	Work completed final Bill & Variation send to Division.
541.	32	LB-260	Reb./Streng, of GC Standard br. in MD-PNU (UP Ln.) in c/w running higher loads/speed (br. No. 808,824,826,835, 847,857 & oth)	24830	13968	LOA issued on 29.01.2021. Total Scope of 06 Bridges. Work completed at 4 Bridges(Br 808,847,857,835) .Box casting done at remaining Br No 824 & 826. Launching is to be done.
542.	32	LB-259	Rep./Streng. of GC Stand. Br. in MD-PNU (Up ln.) in c/w runn. higher loads & speed (Br. No. 729,783,784, 797 & Oth)	21809	7172	LOA issued on 29.01.2021. Total Scope of 4 Bridges. Work completed at 2 Bridges (Br 783 & 784)Box casting done at remaining Br No 729 & 797. Launching is to be done
543.	32	LB-258	Repairs of Arch Bridges by epoxy grouting , cement pressure grouting, guniting etc.of Bridge	24479	4317	LOA issued on 29.01.2021. Work has been completed. Contractual liabilities to be cleared.
544.	32	LB-254	Replacement of stone slabs with RCC slabs 11 no bridges in RKB-JSM & LN-MJ section and raising of height of ballast retainer of various bridges	15789	12480	All bridges were completed earlier except 01 Br. in RKB-JSM Section, due to unavailability of approach road for road cranes. Now the bridge has been launched with Railway crane in April-22 and work has been physically completed. Final bill passed and SD to be released.
545.	32	LB-251	Provision of new bridge (7 x 6.1 m PSC slab) at km 672.04 between Rohat-Kairla stations on LN-MJ section under ADEN/Line.	12961	7872	Work proposed for deletion on IRPSM.
546.	32	LB-250	Strengthening of sub structure ad replacement of existing RCC slab with	5379	4948	Work has been completed and tender of this work has been clubbed with bridge no 348 & 349.
547.	32	LB-249	Strengthening of sub structure ad replacement of existing steel girders (1x12.20m PSC +1x24.40m) of bridge No. 347/1at km 293/10-11 by PSC slab (1x12.20m)/ (1x24.40m steel girder) on MD - DOZ by pass line of	15500	11060	Jacketing work has been completed and side pathway work under progress.

			Ajmer division to make fit for.			
548.	32	LB-248	Strengthening of sub structure and replacement of steel girders (1x12.20m + 1x9015m) of Br. No. 349/1 at km 293/12-294/0 by PSC slabs on MD - DOZ by pass line of Ajmer division to make fit for MBG /25T loading.	5625	1620	Work has been completed and tender of this work has been clubbed with bridge no 347 & 348.
549.	32	LB-247	MD-PNU section-Rebuilding / strengthening of existing arch bridges by providing RCC / PSC slab / box or intermy including strengthening of sub structure (Br. Nos. 533, 535, 550,571, 575,636,764 & 864=9 Nos.)	11232	8622	Total 10 bridges in this work. Rebuilding work completed at 9 bridges. 1 Bridge (Br No 864) is balance. Box casting completed at Br 864, Launching of Br 864 is to be done (TDC Dec-24)
550.	32	LB-239	Samdari~~Bhildi jn.~~Provision of side pathway for steel girders and inspection platforms at each pier & abutment	24999	17743	Side pathway work has been completed at br. No. 3 and Inspection platform work at bridge no 3,54 is under progress.
551.	32	LB-238	Bikaner~~Providing inspection arrangement/facilities at piers and abutments on major/important various ROBs on Bikaner division.	17499	74	Scope of inspection arrangement is 23,out of which 9 has been completed.
552.	32	LB-236	Jodhpur~~Providing inspection arrangement/facilities at piers and abutments on major/important various ROBs on Jodhpur division.	18500	78	Revise estimate has been sanctioned. Work will be started this month.
553.	32	LB-234	Jaipur~~Jaipur~~Providing inspection arrangement/facilities at abutments on various ROBs on Jaipur division.	24998	14211	Inspection arrangement of 48 nos. ROBs has been completed and final bill under preparations.

554.	32	LB-233	Hisar~~Bathinda~~Provision of side pathway for steel girders and inspection platforms at each pier & abutment	20500	6463	Work has been completed physically. Work completed physically. Final bill has been passed. Process for deletion from IRPSM.
555.	32	LB-231	Suratgarh~~Bikaner~~ Provision of side pathway for steel girders and inspection platforms at each pier & abutment	12500	4056	Work completed physically. Final variation has been vetted by accounts. Final bill has been paid and will be process for deletion from IRPSM.
556.	32	LB-225	Jodhpur-Replacement of existing steel girders of bridge in JU-MJ , RKB-JSM Section total 7 spans of 9.15 by PSC slabs under ADEN/Line/JU & ADEN/JSM.	15517	0	Bridge No.2A (1x9.14) RKB-JSM Section Not feasible due to site constraint as Bridge is in skew alignment, bridge No.71 E (1x9.15) UP & DN, Br.No.72 (1x9.15) UP & DN, Not feasible as raising of track is not possible due to existing JU yard near to bridge sites., Bridge no. .99 A (2x9.15), on JU-MJ Section is not feasible as proposed lifting of track is not possible in running track.Work is being reviewed as per instruction given by HQ.
557.	32	-	HP- PNU Sec: - Repl/ Rebuilding of Minor bridges by precast RCC box.(Br. Nos.795 & 820) (Total=02 Br.)	20212	13969	Contract awarded. Rebuilding of Br 820 Completed. Br No 795 GAD submitted to HQ for approval on 30.08.24
558.	32	-	Ajmer~~MD-PNU Strengthening of Substructure and Replacement of existing plate girder/Fish bellied girders upto 12.20m Span of Major/Important	239342	386	Loa has been issued .2nos GAD of bridges have been approved and 06 nos under signature of divisional officers.
559.	32	-	Ajmer~~Palanpur~~Replacement of bedplates & elastomeric Bearings, provision of inspection ladders on steel girders, repairing of bed	6686	765	6 nos bridges bearing have been replaced out of 8 nos bridge.
560.	32	-	Ajmer~~Palanpur~~Augmentation of inspection facilities by providing Inspection Platform on various Major/Important Bridges	15563	0	Inspection arrangement of 09 nos bridges has been completed out of total scope of 21nos and work in under progress.

561.	32	-	Madar Jn.~~Palanpur~~Replacement of Bedplates of Br.no.792 (UP)	3383	0	Work has been completed in the month of Feb-2024 and tender has been clubbed with inspection arrangement and bearing replacement work.
562.	32	-	Madar Jn.~~Palanpur~~Provision of inspection facilities and other maintenance work at Br. No(29 nos. br.)	13230	0	Re- Tender was opened on 01/07/24 and same is under TC.
563.	32	-	Ajmer-Chittourgarh - Providing Curtain, Drop Wall, Bridge Plaque, Inspection stairs on Bridges	5994	0	LOA issued on dated 19.06.2024 and work is under progress.
564.	32	-	Replacement of RCC slab with PSC slab of Br. No. 28, 30 31& 33 on ROK-BNW Sec & steel girder with PSC slab of Br. No.11,22&35 on RE-HSR Sec	32955	22163	GAD under approval of Bridge No. 117 & 135 due to skew bridge. Bridge No.11, 22, 35of RE-HSR section completed in all respect .Jacketing of Bridge No. 117 & 135 completed but PSC slab yet to be casted as GAD is under approval. (Finally:- Replacement of existing of existing steel girder with PSC slab of Bridge No. 117 & 135(BNW-ROK) & Bridge No. 11 ,22 & 35 on RE-HSR section). (Bridge removed 28,30,31, 33 & 134.) Contract rescinded on 08.11.23.
565.	32	-	Bathinda~~Strengthening of sub structure of Br. No. 28 & 72 by jacketing to make them fit for 25T-2008 loading on BTI-LGH section.	33026	29815	Work completed. Final bill paid in April 24.
566.	32	-	Replacement of Steel girder with PSC slab of Br. No. 142 (1 x 9.14m) on ROK-BNW section.	7184	583	Work completed. But can not be completed finally being clubbed with above.
567.	32	-	Strengthening of super structure of bridges by replacing of slab/girder to make them fit for 25 T-2008 loading.	151219	0	Work sanctioned on 22.03.23. Estimate sanctioned 19.05.23. HMH-contract awarded on 06.11.23.BNW-Tender opened on 04.07.23 & 28.07.23 & 18.12.23 but no offer received. Re-tender opened on 25.08.23 & 16.01.24 but discharged. SSA-contract awarded on 14.11.23.Work is in progress (9%). As per directions of HQ some of the bridges are to be constructed new being less

						bearing capacity. Hence estimate will be framed and work shall be executed accordingly.
568.	32	-	Provision of Box Culvert (1.00x1.20m) alongwith catch water drain to pass waste water under the track at km- 68/1-2 on SURP-SDLP.	7575	0	Work sanctioned on 28.12.22. Detail estimate sanctioned. Tender opened on 31.10.23, 15.12.23 & 25.01.24 but no response. Fresh tender to be floated.
569.	32	-	Hanumangarh jn~~Sadulpur~~Metalliz ing &painting of steel bridge girder Br(5nos.)	23828	0	Detailed estimate has been sanctioned by competent authority. LOA has been issued on 06.06.24 and Work is under progress.
570.	32	-	Bikaner~~Improvement of minor bridges in kolayat-phalodi, lalgarh-kolayat, suratgarh-nathwana and suratgarh-anupgarh section over Bikaner division.	13300	0	Work sanctioned on 29.11.23. Tender opened on 04.01.24 & awarded on 29.01.24. Work is in progress.
571.	32	-	Jaipur~~Sawaimadhop ur~~ADEN/Line/Jaipur Sub. Division – Replacement of RCC slab with PSC Slab at bridge no. 41-A between JP-SWM section	13119	6975	Work is in progress
572.	32	-	Phulera~~Madar Jn.~~Replacement of Existing bridge with RCC Box/PSC slab of Bridge no. 237, 279 & 270.	24325	7338	Work is in progress
573.	32	-	Re-Girdering of Br. No. 223 UP on JP-FL section for replacement of existing corroded plate girders.	18312	0	Tender has been published on 02.03.24 and tender has been finalized and LOA has been issued on 14.05.24 and PO for fabrication of girder has been placed.
574.	32	-	Jaipur~~Rewari~~Rew ari~~Providing Drainage pipes at 47 nos. Major & important PSC Bridges of JP div.	1802	0	Detail estimate has been sanctioned and tender has been finalized on 06.06.24 and work is under progress.
575.	32	-	Jaipur~~Sawaimadhop ur~~Metallizing at 02 no. br. girder also metallizing at 12 nos. side pathway of steel	14404	0	Detail estimate has been sanctioned and tender has been finalized on 06.06.24 and work is under progress.

			bridge girder			
576.	32	-	Instrumentation of Railway Bridges on North Western Railway (03 nos bridges)	19826	0	Detailed Estimate has been sanctioned by competent authority. NIT has been published and tender opened on 31.07.24 and tender is under evaluation.
577.	32	-	Rewari~~Jaipur~~Replacement of Bearings , Providing inspection arrangement and painting etc. work on ROBs	24336	0	Detailed estimate has been sanctioned and Tender open on 28.06.24 and tender has been discharge and same will invited.
578.	32	-	ADEN-Line-JP sub division-Replacement of RCC box culvert by providing segmental boxes size 1x2 m at Bridge No 7 and removing old Boxes	6497	0	Detail estimate under preparation.
579.	32	-	Merta road~~Jodhpur~~Replacement of steel girder by PSC slab bridges no.39 of 9.15m span MTD-JU section over Jodhpur Division	2015	0	Detailed estimate sanctioned tender has been finalized on 04.06.24 and GAD under preparation.
580.	32	-	Phulera~~Jodhpur~~Replacement of steel girder by PSC Girder bridges (Total 4 no. Bridges) of 12.20 m span in the jurisdiction of Sr.DEN/East	18647	0	Detailed estimate sanctioned tender has been finalized on 04.06.24 and GAD is under preparations.
581.	32	-	Samdari~~Bhildi jn.~~Replacement of steel girder by PSC Girder bridges (3 Bridge) of 12.20 m span in the jurisdiction of Sr.DEN/ West over JU DIV.	20978	0	Detailed estimate sanctioned tender has been finalized on 04.06.24 and GAD is under preparations.
582.	32	-	Replacement of steel girder by PSC Girder bridges of 12.20 m span in the jurisdiction of Sr.DEN/Central over Jodhpur Division .	6993	24	Detailed estimate sanctioned tender has been finalized on 04.06.24and GAD under preparations.

583.	32	-	Repair of bridges by doing epoxy grouting in bed blocks masonry abudments, pointing, painting, marking (93 no. Bridges) of under ADEN/MTD	18389	0	Work awarded on 13-12-23. Work in progress.
584.	32	-	Phulera~~Nawa city~~Strengthening of bridge approaches in cess widening, stone pitching, slop protection , toe wall etc in FL-NAC section --	24990	0	Work in Progress.
585.	32	-	Strengthening of bridge approaches in cess widening, stone pitching, slop protection , toe wall in DNA-NAC, MKN-PBC & DNA-RTGH	15124	20440	Work in progress
586.	32	-	Phulera~~Merta road~~Replacement of ballast retainer, PSC Slab/RCC Slab of (10 no. Bridge)Br. no.18 ,. 23 ,25,. 38 , 66,82, 83 FL-DNA & 47,50,54	16526	0	Work in Progress.
587.	32	-	Phulera~~Degana~~Replacement of 0.61 mt. multiple span (Total 8 no. Bridges) bridge no. (Br.no. 46 span 5x0.61,) by RCC box(Precast single unit)	22323	22323	Work in progress
588.	32	-	New R.C.C Box bridges at breach prone locations in RKB-PLC section at km 111/3-4 , 111/4-5 ,117/3-5 ,123/1-2 .	22178	0	Work in progress.
589.	32	-	New bridges at breach prone locations in PLCJ-JSM section at km 136/4-5 , Km 252/2-3 , Km 253/6-7 , 254/0-1(1x 2.5mx1.25m)	23800	9428	Work in progress.
590.	32	-	R.C.C Box Bridge at breach prone locations in RKB-PLC section at km 108/9-109/1 (2X 5MX3M)	9293	4051	Work in progress

591.	32	-	RCC box bridges in lieu of existing ballastless slab bridge (Span 5x0.61m) & (Span 4x0.61m) in Luni and Bomadra yards for replacing existing wooden	18587	0	Work in progress
592.	32	-	Strengthening to bridges, by providing pointing, painting, marking of DL, HFL, flooring, apron, epoxy etc. under sub-division ADEN/JSM	24649	0	Work in progress
593.	32	-	Strengthening of bridge no.85,92,26 ,80A (DN & UP)95A , 103 A,105,73,74,2, 26A of JU-MJ,JU-SWF,PPR-BARA Section under ADEN/LINE	24950	2097	Tender awarded on 28.08.2023. Work in progress
594.	32	-	Strengthening of Minor bridges of JU-MJ,JU-SWF,PPR-BARA Section under ADEN/LINE of SR.DEN/Central section	24910	12308	Work awarded on 28.08.2023. Work in progress.
595.	32	-	Strengthening to 28 bridges, by providing pointing, painting, marking of DL, HFL, flooring, apron, epoxy etc. on LN-SMR-BLDI section under ADEN/SMR	24849	3275	Work awarded on 13.07.23 &Work is in progress.
596.	32	-	Provision of additional bridge at Km. 618/052 & rehabilitation of bridge No. 81. etc in JUCT-RKB section under ADEN/Line/JU.	22703	0	Estimate under preparation.
597.	32	-	Replacement of 0.61 m multiple span bridge no.70,81,84 by RCC box (Precast single unit) span 1x2.6x1.35,, 2x2.85x1.5 & 2x2.3x1.35 FL-DNA section.	8321	0	Tender to be Re-invited.

598.	32	-	Samdari~~Bhildi jn.~~Bhildi jn.~~Painting and Metallizing of steel bridge girder Br.(7 nos. bridges)	12274	0	Detailed estimate has been sanctioned and tender has been finalized and LOA issued on 06.06.24 work is under progress.
599.	32	-	Construction of RCC box Br.at Km.176/1-2(2x3.0x2.5m)along with adjoini protection wall, Pitching & other work at breaches locations in SMR-BLDI Sec.	22966	0	Tender awarded. Work to be started.
600.	32	-	Construction of RCC box Br. at Km.170/6-7 (2x4.0x3.0m) along with protection wall, Pitching & other work at breaches locations in SMR-BLDI Sec.	23348	0	Tender awarded. Work to be started.
601.	32	-	Construction of RCC box Br at Km.70/9-71/0(1 x 5.0 x 2.5m)along with protection wall, Pitching & other work at breaches locations in SMR-BLDI Sec.	23225	0	Tender under finalization.
602.	32	-	Construction of RCC box Br. at Km.31/8-9 (2 x 5.0 x 2.5m) along with protection wall, Pitching & other work at breaches locations in SMR-BLDI Sec.	23165	0	Tender finalized, work is to started
603.	32	-	Construction of RCC box Br. at Km.30/4-5 (2 x 3.0 x 2.5m) along with protection wall, Pitching & other work at breaches locations in SMR-BLDI Sec.	23923	0	Tender finalized, work is to started
604.	32	-	Construction of RCC box br. at Km.56/6-7 with adjoining protection wall, Pitching and other work at breaches locations in Samdari-Bhildi sec.	24950	0	Tender under finalization.
605.	32	-	Construction of RCC box br at Km.100/0-3 with adjoining protection wall, Pitching and other work at	23500	0	Tender under finalization.

			breaches locations in Samdari-Bhildi Sec.			
606.	32	-	Construction of RCC box br at Km.105/0-1 with adjoining protection wall, Pitching and other work at breaches locations in Samdari-Bhildi Sec..	24850	0	Tender under finalization.
607.	32	-	Construction of RCC box br at Km.126/3-4 with adjoining protection wall, Pitching and other work at breaches locations in Samdari-Bhildi Sec.	24900	0	Tender under finalization.
608.	32	-	Construction of RCC box br at Km.155/0-1 with adjoining protection wall, Pitching and other work at breaches locations in Samdari-Bhildi Sec.	24700	0	Tender awarded work to be started.
609.	32	-	Construction of RCC box br at Km.218/2-3 with adjoining protection wall, Pitching and other work at breaches locations in Samdari Bhildi sec..	24975	0	Tender awarded work to be started.
610.	51	PB-397	North Western Railway - Improvement of various staff amenities like water supply arrangement/ medical facilities in various hospitals/ electric wiring in staff quarters etc.(PB#1251/NR/2023-24)	0	0	
611.	51	PB-395	North Western Railway - Construction of new quarters for staff/officers at various (PB#1252/NR/2023-24)	0	0	
612.	51	PB-396	North Western Railway - Replacement of old/dilapidated quarters at various locations of Indian Railways (PB#1253/NR/2023-24)	0	0	

613.	51	-	Ajmer:-Provision of pipeline network near 51 tank to RE Quarters, near STS Hostel colony, Construction colony and various officers' bungalows	13910	0	40%
614.	51	-	Ajmer Providing 300 KL capacity OHT for storage of water at Frazer Road Colony & connecting pipeline	11996	0	2%
615.	51	-	Haripur-Provision of RCC OHT 1.25 Lac Litres with 1.50 lac litres GLR laying pipeline from Borewell (near Br. 509)	12300	0	
616.	51	-	ADEN/DNRP sub division:- Providing 12 units Type II staff quarters and its related work i.e. Approach road,boundary wall etc	20902	0	
617.	51	-	Lunkaransar~~Lunkaransar:- Construction of 13 Nos. Type-II quarters in lieu of low lying quarters no. T-9/2,T-10/2,T-11/2,T-12/2,E-1/1,E-3/4.	23745	0	40%
618.	51	-	Bikaner~~Construction of 02 Type-V houses for Officers at Bikaner.	12488	0	
619.	51	-	Provision of STP (01 - 120 KLD and 01 50KLD capacity) and other allied works in RPF and Goods Railway colony, Bikaner.	19999	0	
620.	51	-	Prov. of borewell for staff quarters at Churu, Bigga, Napasar & Parsneu stations (01 no. at each station) & Replacement of corroded pipeline at Churu	13477	0	
621.	51	-	ADEN (SIKAR) Sub Division:- Providing 12 Units. Type II quarters in lieu of old abandoned quarters for	24961	0	

			Gang No. 43,44 & 46, in SIKR-LHU section			
622.	51	-	Augmentation of water supply scheme capacity & improvement to distribution network at Rewari staff colony and repair of pipe line between RE-AIA.	22500	0	
623.	51	-	Jaipur~~Jaipur - Repair of Iron doors, Gauzed wire on windows, Jali door etc at staff qtrs. in Ganpati nagar & Loco colony, Jaipur.	8219	0	2
624.	51	-	Jaipur~~Jaipur- Construction of New one unit (Type V) qtr. At 343 B Loco colony.	3557	0	
625.	51	-	Repair to roof leakage in quarters at RE & BKI railway colony.	6000	0	
626.	51	-	Repair to roof leakage of Relay room, battery room and SM chamber at BWL, AIA, HSI and BKI stations.	4500	0	
627.	51	-	Improvement in basic facilities in RE and BKI staff colonies.	20000	0	
628.	51	-	Providing RCC overhead tank (One lac), 20 meter staging and sump of 25000 litre with pipe line etc. at each station of NWH, DOB, NUA & RSH.	24492	0	
629.	51	-	ADEN (RGS) Sub Division: - Providing 16 units Type II quarters in lieu of old abandoned quarters for Gang No. 22, 23, 24 & 26 in JP-RGS section.	23972	0	

630.	51	-	ADEN (SIKAR) Sub Division:- Providing 15 units Type II quarters in lieu of old abandoned quarters for Gang No. 1,2 & 3 SIKR-CUR section.	22893	0	
631.	51	-	JP- Div. - Providing web-based valve atomization System.	19648	0	
632.	51	-	Ratangarh jn~~Degana~~Improvement of staff quarters in Degana-Ratangarh section	20000	0	
633.	51	-	Balotra~~Replacement of 12 unit Type II quarters on condition basis at Balotra station under ADEN/ Barmer of Jodhpur Division	19899	0	
634.	51	-	Barmer~~Replacement of 12 Unit Type II quarters & 2- Unit Type III quarters on condition basis at Barmer station under ADEN/Barmer	24478	0	
635.	51	-	Merta road~~Bikaner~~ Construction of new Staff Quarters at Marwar Mundwa, Chilo, Alai & Bhadwasi station (15 no. Type -II)	24938	0	
636.	51	-	Improvement of water supply arrangement by providing RO plants, replacement of old corroded pipe line & U/G water tank at JOR, MON & RNV stations	24799	0	
637.	53	PB-435	North Western Railway-Upgradation/Modernisation of Infrastructure at good sheds (PB#1302/NR/2023-24)	0	0	
638.	53	PB-433	North Western Railway-Ballastless Track for Station Development (PB#1300/NR/2023-24)	0	0	

639.	53	PB-437	North Western Railway-Comprehensive sewage treatment plant (Phase-II) (PB#1304/NR/2023-24)	0	0	
640.	53	PB-431	North Western Railway-Integration of Metro stations with Railway Stations (PB#1298/NR/2023-24)	0	0	
641.	53	PB-432	North Western Railway-Major Upgradation of Railway Stations on Indian Railways(Phase-IV) (PB#1299/NR/2023-24)	0	0	
642.	53	PB-439	North Western Railway-Minimum essential amenities & facilities for Divyangjan at stations (other than telecom, lift & quick watering system) (Phase-II) (PB#1306/NR/2023-24)	0	0	
643.	53	PB-438	North Western Railway-Minimum essential amenities - Telecom, expansion of information system to facilitate Divyangjan and other passenger amenity items (Phase - II) (PB#1305/NR/2023-24)	0	0	
644.	53	PB-436	North Western Railway-Provision of Escalators on Railway platforms with average footfall more than 25000 per day (Phase-II) (PB#1303/NR/2023-24)	0	0	
645.	53	PB-442	North Western Railway-Provision of foot over bridges and/or high-level platforms at stations (Phase - III) (PB#1309/NR/2023-24)	0	0	
646.	53	PB-440	North Western Railway-Provision of lifts at stations (Sugamya Bharat Abhiyan) (Phase - II) (PB#1307/NR/2023-24)	0	0	

647.	53	PB-434	North Western Railway-Setting up of quick watering arrangement systems at stations (PB#1301/NR/2023-24)	0	0	
648.	53	PB-441	North Western Railway-Soft upgrades/improvements at stations (PB#1308/NR/2023-24)	0	1138	
649.	53	PB-443	North Western Railway - Setting up of Quick watering arrangement at stations (62/Suppl. Dec'23/NR/2023-24)		0	
650.	53	-	Fatehnagar~~Soft improvement i.e. Station buildin, PF Shelters, RCC porch circulating area etc at FAN Stations underAmrit Bharat Scheme	74993	37327	0
651.	53	-	Soft improvement Station building, Second Entry, RCC porch ,circulating area etc at RPZ Station Amrit Bharat Scheme	92385	24520	
652.	53	-	Mavli jn.~~Soft improvement i.e. Station building, Second Entry, Facade, PF Shelters, etc at MVJ Stations under Amrit Bharat Scheme	86494	25835	
653.	53	-	Soft improvement of station , PF surfacing and PF covering at PF No. 2 & 3 and circulating area with second entry at BHL Amrit Bharat Scheme	46711	15114	
654.	53	-	Dungarpur~~Soft improvement Facade station building and PF Shelters at DNRP station and PF Shelters at DNRP and RPZ under Amrit Bharat Scheme	88958	38843	

655.	53	-	Sojat road~Soft improvement i.e. Station building, Second Entry, PF Shelters, porch, Improvement to Roads, Improvement to Toilets, etc.	90769	23668	70%
656.	53	-	Soft improvement Station building, Facade PF Shelters, RCC porch, circulating area etc at KIN Stationsunder Amrit Bharat Scheme	69190	18803	
657.	53	-	Soft improvement Entrance Hall with waiting Room, Second Entry, Facade Roads at Pindwara under Amrit Bharat Scheme	73484	21198	70%
658.	53	-	Somesar~~Soft improvement i.e. Entrance hall with Waiting Room, Booking counters, Second Entry, Facade Improvement , PF Shelters, porch etc	71385	948	75%
659.	53	-	Marwar jn.~~Soft improvement i.e. Facade Improvement , PF Shelters, porch , Improvement to Toilets, Improvement to interiors , etc at Marwar Jn.	48073	6887	50%
660.	53	-	Falna~~Soft improvement i.e. Parking cum Waiting Room in crculating area at main entry , Facade Improvement , PF Shelters, porch etc	57033	10238	50%
661.	53	-	Rani~~Soft improvement i.e. Second Entry, Facade Improvement , PF Shelters, porch , Improvement to interiors , Improvement to Toilets etc	57690	8692	45%

662.	53	-	Jawaibandh~~Soft improvement i.e. Second Entry, Facade Improvement , PF Shelters, porch , Improvement to interiors , etc	60053	10105	40%
663.	53	-	AII DIV – Electric Work due to Augmentation/Strengthening of power supply arrngmnt at 15 Stns.	65001	1395	2%
664.	53	-	Beawar~~Soft improvement of BER station shortlisted under Amrit Bharat Scheme	60026	24012	
665.	53	-	Bijainagar~~Soft improvement i.e. of BJNR Station under Amrit Bharat Schme	66699	32704	
666.	53	-	Rani~~Extension of existing FOB from 6M Wide to 12 M Wide at Rani Station shortlisted under Amrit Bharat Scheme	37045	0	
667.	53	-	Dungarpur~~Dungarpur~~Provision of FOB 12m wide FOB at DNRP stations shortlisted under Amrit Bharat Scheme.	46288	0	
668.	53	-	Provision of FOB 12 M Wide at Pindwara Station over IR tracks shortlisted under Amrit Bharat Scheme.	63860	0	
669.	53	-	Fatehnagar~~Fatehnagar~~Provision of FOB and High Level PF at Platform no 2 at FAN station shortlisted under Amrit Bharat Scheme.	63199	0	
670.	53	-	Kapasan~~Provision of FOB 12 m wide FOB at KIN stations shortlisted under Amrit Bharat Scheme.	62288	0	

671.	53	-	Marwar jn.~~Provision of FOB 12 M Wide at Marwar jn. Station shortlisted under Amrit Bharat Scheme.	71808	0	20%
672.	53	-	Ranapratapnagar~~Provision of FOB 12m wide FOB at RPZ stations shortlisted under Amrit Bharat Scheme.	62288	0	
673.	53	-	Provision of FOB 12 M Wide at Sojat Road Station over IR tracks shortlisted under Amrit Bharat Scheme.	64061	0	40%
674.	53	-	Extension of existing FOB from 3M Wide to 12 M Wide over IR tracks at Somesar Station shortlisted under Amrit Bharat Scheme.	61799	0	
675.	53	-	Provision of FOB 12 M Wide at Falna Station over IR tracks shortlisted under Amrit Bharat Scheme.	64055	14816	
676.	53	-	Provision of FOB 12 M Wide at Jawai Bandh Station over IR tracks shortlisted under Amrit Bharat Scheme.	63830	6085	
677.	53	-	Mavli jn.~~Provision of FOB 12m wide FOB at MVJ stations shortlisted under Amrit Bharat Scheme.	71987	10537	
678.	53	-	AII Div. - Electrical work due to Provision/extension of FOB 3m/6m/12m wide FOB & High level PF etc. at 15 stations	40203	4920	2%
679.	53	-	Bijainagar~~Provision of FOB 12m wide at BJNR station shortlisted under Amrit Bharat Scheme.	35294	0	
680.	53	-	Bhilwara~~Provision of FOB 12m wide at BHL station shortlisted under Amrit Bharat Scheme.	57188	0	

681.	53	-	Beawar~~Provision of FOB 12m wide at BER station shortlisted under Amrit Bharat Scheme.	51598	0	
682.	53	-	AII Div.- Electrical work due Soft improvement i.e. Stn bldng, Sec. Entry, RCC porch,Entrance hall, Impromnt to Roads, Toilets, etc at 15 stations.	65824	2594	10%
683.	53	-	AII Div. - Electrical work due to Platform Shelters & Lightings at 15 stations under Amrit Bharat Scheme	30003	15157	13%
684.	53	-	Provision of cable tray for proper cabling arrangement at 15 Stations over AII Div.	74992	20758	15%
685.	53	-	Adarshnagar~~Dungar pur~~Provision of Lifts at 7 stations in AHO-UDZ-DNRP section over Ajmer Division.	59520	5947	2%
686.	53	-	Provision of back up power supply arrangement at 15 stations over AII Div.	35000	15780	15%
687.	53	-	Madar Jn.~~Palanpur~~Minim um essential amenities telecom expansion of information system to facilitate divyangjan and other passenger amenity items	54759	17268	0
688.	53	-	Ajmer~~Himmat nagar~~Minimum essential amenities telecom expansion of information system to facilitate divyangjan and other passenger amenity items	45564	23735	
689.	53	-	AII Div :Provision of Lifts at 08 stns (BER,SOD,MJ,SOS,RA NI,FA,JWB,PDWA) in MD-PNU section under	56107	2350	2%

			Amrit Bharat Scheme.			
690.	53	-	Provision of furniture and other commercial item for 15 station in MD-PNU & AHO-UDZ section covered under Amrit Bharat Scheme over Ajmer Division."	36397	0	
691.	53	-	Dungarpur~~ Dungarpur~~ Provision of passenger facilities for Divyangjan i.e. at DNRP	9935	0	
692.	53	-	Beawar~~ Provision of passenger facilities for Divyangjan i.e. at BER	9882	0	
693.	53	-	Kapasan~Provision of passenger facilities for Divyangjan i.e. at Kapsan	11440	1383	
694.	53	-	Mavli jn.~ Provision of passenger facilities for Divyangjan i.e. at MVJ	12338	0	
695.	53	-	Ranapratapnagar~~Ra na Pratap nagar - Provision of passenger facilities for Divyangjan i.e. at Rana Pratap nagar	14941	4139	
696.	53	-	Fatehnagar~~ Provision of passenger facilities for Divyangjan i.e. at FAN	9741	1	
697.	53	-	Marwar jn.~~Provision of passenger facilities for Divyangjan i.e. at Marwar Jn. Station	18020	0	
698.	53	-	Sojat road~~Provision of passenger facilities for Divyangjan i.e. at Sojat Road Station	18918	1343	

699.	53	-	Somesar~~Provision of passenger facilities for Divyangjan at Somesar Station	32657		
700.	53	-	Falna~~Provision of passenger facilities for Divyangjan i.e. at Falna Station	14810	0	
701.	53	-	Rani~~Provision of passenger facilities for Divyangjan i.e. at RANI station	12183	0	
702.	53	-	Provision of passenger facilities for Divyangjan i.e. at JWB	18858	0	
703.	53	-	Bijainagar~~ Provision of passenger facilities for Divyangjan i.e. at Bijainagar	11488	0	
704.	53	-	Provision of passenger facilities for Divyangjan i.e. at PDWA	18020	0	
705.	53	-	Bhilwar - Provision of passenger facilities for Divyangjan i.e. at BHL	14180	1230	
706.	53	-	AII Div :Electric Work due to Provision of LED Signage Boards & Station Name Boards at 15 Stations.	24985	0	0
707.	53	-	AII Div. - TRD work in connection with the provision of FOB and/or HLPFs at stations	10000	0	
708.	53	-	AII Div- Development of Goods Shed Provision of Furniture &Other items for Goods office and Merchant Rooms etc. at Stations JWB, DRB, UMRA DNRP	4470	0	

709.	53	-	AII Div- Umra Development of Goods Shed Approach Road, Drainage, Covered Shed, Drinking Water, Rest Room, Goods office, Merchant Room, etc	24523	0	
710.	53	-	Major upgradation of Bikaner railway station over Bikaner division.	4713228	0	
711.	53	-	Provision of 10 Nos. Lifts at stations of Amrit Bharat Station Scheme over Bikaner Division (HSR-6, BNW-2 & SSA-2).	58226	0	0
712.	53	-	Provision of 11 Nos. Lifts at stations of Amrit Bharat Station Scheme over Bikaner Division (HMH-2, LGH-2, CUR-3, SDLP-3 & SGNR-1).	61359	0	0
713.	53	-	Kosli~~Soft upgradation of Kosli railway station under Amrit Bharat Station Scheme.	66325	9269	85%
714.	53	-	Hisar~~Soft upgradation of Hisar railway station under Amrit Bharat Station Scheme.	99941	30088	88%
715.	53	-	Gogameri~~Soft upgradation of Gogameri railway station under Amrit Bharat Station Scheme.	73412	32174	80%
716.	53	-	Churu~~Soft upgradation of Churu railway station under Amrit Bharat Station Scheme.	84298	20788	45%
717.	53	-	Lalgarh~~Soft upgradation of Lalgarh railway station under Amrit Bharat Station Scheme.	99991	22806	65%

718.	53	-	Hanumangarh jn~~Soft upgradation of Hanumangarh Jn railway station under Amrit Bharat Station Scheme.	98061	30156	80%
719.	53	-	Mandi dabwali~~Soft upgradation of Mandi Dabwali railway station under Amrit Bharat Station Scheme.	74090	30651	80%
720.	53	-	Mahendragarh~~Soft upgradation of Mahendragarh railway station under Amrit Bharat Station Scheme.	70692	5544	45%
721.	53	-	Ratangarh jn~~Soft upgradation of Ratangarh railway station under Amrit Bharat Station Scheme.	83815	26793	60%
722.	53	-	Sriganganagar~~Soft upgradation of Sriganganagar railway station under Amrit Bharat Station Scheme.	99503	39723	65%
723.	53	-	Sadulpur~~Soft upgradation of Sadulpur railway station under Amrit Bharat Station Scheme.	76067	31959	75%
724.	53	-	Bhiwani~~Soft upgradation of Bhiwani Jn railway station under Amrit Bharat Station Scheme.	80670	16161	94%
725.	53	-	Sirsa~~Soft upgradation of Sirsa railway station under Amrit Bharat Station Scheme.	75873	13577	85%
726.	53	-	Charkhi dadri~~Soft upgradation of Charkhi Dadri railway station under Amrit Bharat Station Scheme.	58690	14121	85%
727.	53	-	Suratgarh~~Soft upgradation of Suratgarh railway station under Amrit Bharat Station Scheme.	99983	39505	70%

728.	53	-	Bhiwani~~Provision of FOB 12 mtrs wide at Bhiwani Jn station of Bikaner Division under Amrit Bharat Station Scheme.	72992	0	0
729.	53	-	Provision of FOB 12m wide at Mahendragarh & Extension of existing FOB 6M wide at Hisar station station under Amrit Bharat station Scheme"	87561	0	0
730.	53	-	Lalgarh~~Provision of FOB 12 mtrs wide at Lalgarh station of Bikaner Division under Amrit Bharat Station Scheme.	79540	3361	14%
731.	53	-	Sriganganagar~~Provision of FOB 12 mtrs wide at Sriganganagar station of Bikaner Division under Amrit Bharat Station Scheme.	99810	0	5%
732.	53	-	Sadulpur~~Provision of FOB 12 mtrs wide at Sadulpur station of Bikaner Division under Amrit Bharat Station Scheme.	91564	1537	10%
733.	53	-	Mandi dabwali~~Provision of FOB 12 mtrs wide at Mandi Dabwali station of Bikaner Division under Amrit Bharat Station Scheme.	56912	0	0
734.	53	-	Provision of FOB 06 mtrs wide to augment under construction 06 mtrs FOB at Hisar station of Bikaner Division under Amrit Bharat Station Scheme.	103141	0	0
735.	53	-	Gogameri~~Provision of FOB 12 mtrs wide at Gogameri station of Bikaner Division under Amrit Bharat Station Scheme.	60121	1934	0

736.	53	-	Charkhi dadri~~Provision of FOB 12 mtrs wide at Charkhi Dadri station of Bikaner Division under Amrit Bharat Station Scheme.	71680	0	0
737.	53	-	Suratgarh~~Provision of FOB 12 mtrs wide at Suratgarh station of Bikaner Division under Amrit Bharat Station Scheme.	102534	7120	25%
738.	53	-	Sirsa~~Provision of FOB 12 mtrs wide at Sirsa station of Bikaner Division under Amrit Bharat Station Scheme.	85598	0	0
739.	53	-	Churu~~Provision of FOB 12 mtrs wide at Churu station of Bikaner Division under Amrit Bharat Station Scheme.	93267	1471	28%
740.	53	-	Ratangarh jn~~Provision of FOB 12 mtrs wide at Ratangarh station of Bikaner Division under Amrit Bharat Station Scheme.	89685	39579	35%
741.	53	-	Kosli~~Provision of FOB 12 mtrs wide at Kosli station of Bikaner Division under Amrit Bharat Station Scheme.	66914	0	0
742.	53	-	Hanumangarh jn~~Provision of FOB 12 mtrs wide at Hanumangarh Jn station of Bikaner Division under Amrit Bharat Station Scheme.	75807	0	7%
743.	53	-	Provision of MEA Telecom items at 15 stations over Bikaner division under Amrit Bharat Station Scheme	99674	81019	80%
744.	53	-	Bhiwani city~~Upgradation / modernization of infrastructure at Bhiwani City Goods shed over Bikaner Division.	58853	0	25%

745.	53	-	Kalan wali~~Upgradation / modernization of infrastructure at Kalanwali Goods shed over Bikaner Division.	94087	0	0
746.	53	-	Bhattu~~Upgradation / modernization of infrastructure at Bhattu Goods shed over Bikaner Division.	99381	0	0
747.	53	-	Mandi dabwali~~Upgradation / modernization of infrastructure at Mandi Dabwali Goods shed over Bikaner Division.	67209	0	
748.	53	-	Banwali~~Upgradation / modernization of infrastructure at Banwali Goods shed over Bikaner Division.	51274	0	
749.	53	-	Sri vijay nagar~~Upgradation / modernization of infrastructure at SriVijaynagar Goods shed over Bikaner Division.	111505	0	
750.	53	-	Bhattu~~Soft upgradation of Bhattu station of Bikaner Division under Amrit Bharat Station Scheme.	122600	0	
751.	53	-	Kalan wali~~Soft upgradation of Kalanwali station of Bikaner Division under Amrit Bharat Station Scheme.	87600	0	
752.	53	-	Hansi~~Soft upgradation of Hansi station of Bikaner Division under Amrit Bharat Station Scheme.	160400	0	
753.	53	-	Raisingnagar~~Soft upgradation of Raisinghnagar station of Bikaner Division under Amrit Bharat Station Scheme.	85800	0	

754.	53	-	Mandi adampur~~Soft upgradation of Mandi Adampur station of Bikaner Division under Amrit Bharat Station Scheme.	118300	0	
755.	53	-	Soft upgradation of Loharu station of Bikaner Division under Amrit Bharat Station Scheme.	161500	0	
756.	53	-	Anupgarh~~Soft upgradation of Anupgarh station of Bikaner Division under Amrit Bharat Station Scheme.	141300	0	
757.	53	-	Sirsa~~Upgradation / modernization of infrastructure at Sirsa Goods shed over Bikaner Division.	173226	0	
758.	53	-	Suratgarh~~Upgradation / modernization of infrastructure at Suratgarh Goods shed over Bikaner Division.	108890	0	
759.	53	-	Satroad~~Upgradation / modernization of infrastructure at Satrod Goods shed over Bikaner Division.	105259	0	
760.	53	-	Raman~~Upgradation / modernization of infrastructure at Raman Goods shed over Bikaner Division.	112366	0	
761.	53	-	Lalgarh~~Upgradation / modernization of infrastructure at Lalgarh Goods shed over Bikaner Division.	181942	0	
762.	53	-	Hanumangarh jn~~Upgradation / modernization of infrastructure at Hanumangarh Jn Goods shed over Bikaner Division.	164308	0	
763.	53	-	Kalana~~Extension to 405 mtrs and raising of rail level platform to high level at Kalana halt station over Bikaner	14663	0	0

			Division.			
764.	53	-	Providing architectural and Technical Consultancy for upgradation of 06no. Stations over Bikaner Division under Amrit Bharat Stn Scheme	5088	0	25%
765.	53	-	Provision of Coach Guidance System at 09 stations (09 PFs) of Bikaner Division having stoppage of 06 or more reserved coaches trains.	24769	0	
766.	53	-	Provision of Coach Guidance System at 08 stations (10 PFs) of Bikaner Division having stoppage of 06 or more reserved trains.	24338	0	
767.	53	-	Rewari~~Alwar~~Alwar ~~Provision of Lifts at Alwar-03 & Rewari-05 Stations of Jaipur Division under Amrit Bharat scheme	44999	1363	0
768.	53	-	Naraina~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at NRI Station.	90758	59750	55%
769.	53	-	Phulera~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at FL Station.	98201	33708	50%
770.	53	-	Asalpur jobner~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at JOB station.	63885	18915	55%
771.	53	-	Sikar~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at SIKR Station.	110109	36312	58%

772.	53	-	Ringas~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at RGS Station.	93252	55304	82%
773.	53	-	Narnaul~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at NNL Station.	95361	23630	50%
774.	53	-	Nim ka thana~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at NMK Station.	81857	18396	50%
775.	53	-	Bandikui~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at BKI Station.	93823	35884	60%
776.	53	-	Alwar~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at AWR Station.	79605	16330	40%
777.	53	-	Jhunjhunu~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at JJN Station.	87784	27235	65%
778.	53	-	Fatehpur shekhawati~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at FPS Station.	94703	71591	86%
779.	53	-	Rajgarh~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at RHG Station.	62555	37615	85%
780.	53	-	Rewari~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at RE Station.	97440	51239	75%
781.	53	-	Khairthal~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at KRH Station.	59495	43032	85%

782.	53	-	Dausa~~JP Division :- Soft UP gradation work in connection with Amrita Bharat Station at DO Station.	75107	24310	70%
783.	53	-	Sikar~~JP Division – Provision of FOB work in connection with Amrit Bharat station at SIKAR Station.	44069	51	1%
784.	53	-	JP Division- Provision of 12m wide FOB work in connection with Amrita Bharat station scheme at Ringas Station	40712	27	1%
785.	53	-	P Division- Provision of 12m wide FOB work in connection with Amrit Bharat station scheme at Nim ka thana Station	39155	571	1%
786.	53	-	Naraina~~JP Division – Provision of high level platform with Amrit Bharat station at NRI Station.	33464	14208	90%
787.	53	-	JP Division- Provision of 12m wide FOB work in connection with Amrit Bharat station scheme at Jhunjhunu Station	38317	466	1%
788.	53	-	Ringas~~JP Division - Minimum essential amenities work for Divyangjan work in connection with Amrit Bharat station at RGS Station.	25722	10	5%
789.	53	-	Narnaul~~JP Division - Minimum essential amenities work for Divyangjan work in connection with Amrit Bharat station at NNL Station.	33066	45	5%
790.	53	-	Telecom, expansion of information system to facilitate Divyangjan and other passenger amenity items for 6 stations: NNL, NMK,RGS, SIKR, JJN,FPS	44338	19938	55%

791.	53	-	Telecom, expansion of information system to facilitate Divyangjan and other passenger amenity items for 6 stations: RE, KRH, AWR, RHG,BKI, DO	37294	20538	75%
792.	53	-	JP Division- Provision of 12m wide FOB work in connection with Amrita Bharat station scheme at Alwar Station.	83943	11	1%
793.	53	-	Provision of Lifts at Neem ka Thana -02, Ringus-01, SIKR-02 & JJN-01 Stations Jaipur Division under Amrit Bharat scheme	30000	0	0
794.	53	-	JP Division- Provision of 12m wide FOB work in connection with Amrit Bharat station scheme at Dausa Station	40999	87	10%
795.	53	-	JP Division- Provision of 12m wide FOB work in connection with Amrit Bharat station scheme at Rajgarh Station	61938	30	40%
796.	53	-	Naraina~~JP Division – Provision of foot over bridges with Amrit Bharat station at NRI Station.	41204	0	15%
797.	53	-	Asalpur jobner~~Jaipur Division- Provision of 12m wide FOB in connection with Amrit Bharat Station at JOB Station.	38477	78	15%
798.	53	-	Phulera~~Phulera:- Re development of FL Station High level platforms facilities. in connection with Amrit Bharat station.	27938	26556	92%
799.	53	-	JP Division- Provision of 12m wide FOB work in connection with Amrit Bharat station scheme at Khairthal Station	41935	49	20%

800.	53	-	Fatehpur shekhawati~~JP Division – Provision of FOB work in connection with Amrit Bharat station at FPS Station.	38973	0	
801.	53	-	JP Division- Provision of 12m wide FOB work in connection with Amrit Bharat station scheme at NNL Station.	35092	0	0
802.	53	-	Kishangarh : Provision of 04 nos. Escalators at Kishangarh station.	43505	419	0
803.	53	-	Rewari~~Rewari~- Provision of 04 Nos. Escalators at Rewari Station.	49927	378	0
804.	53	-	Asalpur jobner~Raising of PF no. 1, 2 & 3 s to High Level and exte to 576m in connection with Amrit Bharat Station.	43422	26946	60%
805.	53	-	Asalpur jobner~~Asalpur Jobner - Asalpur Jobner Goods Shed (JOB) -Development of Goods Shed/Freight Terminal with all facilities	70000	0	
806.	53	-	JP Division- Provision of 12m wide FOB work in connection with Amrit Bharat station scheme at Rewari Station	113037	0	1%
807.	53	-	JP Division- Provision of 12m wide FOB work in connection with Amrit Bharat station scheme at Bandikui Station	111300	66	10%
808.	53	-	Phulera~~Phulera:- Re development of FL Station FOB. In connection with Amrit Bharat station.	168695	5111	15%

809.	53	-	Kanakpura~~Kanakpura~~Kanakpura Goods Shed (KKU) - Development of Goods Shed/Freight Terminal with all facilities	110938	0	0
810.	53	-	Alwar~~Alwar Goods Shed (AGS) - Development of Goods Shed/Freight Terminal with all facilities	112780	0	0
811.	53	-	Nindhar benar~~Nindhar Benad~~Nindhar Benad Goods Shed (NDH) -Development of Goods Shed/Freight Terminal with all facilities	140458	0	0
812.	53	-	Khori~~Khori - Upgradation /Modernization & Augmentation of Goods Shed/Freight Terminal at existing KORI goods shed	246600	0	0
813.	53	-	Jerthidadhia~~Jerthi Dadia~ Jerthi Dadia Goods Shed (JDD) - Development of Goods Shed/Freight Terminal with all facilities.	137600	0	0
814.	53	-	Sanganer~~JP Div.- Consultancy work in connection with Major station Redevelopment of Sanganer in Jaipur-Sawai Madhopur section.	5467	0	
815.	53	-	Bandikui~~Jaipur~~Provision of Lifts at Dausa-02 & Bandikui-02 Stations of Jaipur Division under Amrit Bharat scheme	19200	181	0
816.	53	-	Telecom, expansion of information system to facilitate Divyangjan and other passenger amenity items for 3 stations: JOB, FL, NRI	19219	7769	37%

817.	53	-	Phulera~~Phulera:- Re devel of FL Station Minimum essential amenities and facilities for Divyagjan . In connection with Amrita Bharat station.	20828	795	32%
818.	53	-	Naraina~~JP Division - Minimum essential amenities work for Divyangjan work in connection with Amrit Bharat station at NRI Station.	12067	0	33%
819.	53	-	Dausa~~JP Division- Minimum Essential Amenities wok for Divyangjan work in connection with Amrita Bharat station at DO Station.	20973	44	60%
820.	53	-	Rajgarh~~JP Division- Minimum Essential Amenities wok for Divyangjan work in connection with Amrita Bharat station at RHG Station.	20589	10	75%
821.	53	-	Sikar~~JP Division - Minimum essential amenities work for Divyangjan work in connection with Amrit Bharat station at SIKAR Station.	21222	43	5%
822.	53	-	Fatehpur shekhawati~~JP Division - Minimum essential amenities work for Divyangjan work in connection with Amrit Bharat station at FPS Station.	19422	0	5%
823.	53	-	Jhunjhunu~~JP Division - Minimum essential amenities work for Divyangjan work in connection with Amrit Bharat station at JJN Station.	19422	0	5%
824.	53	-	Asalpur jobner~~Jaipur Division- Minimum Essential Amenities work for Divyangjan work in connection with	22013	0	35%

			Amrit Bharat Station at JOB Station.			
825.	53	-	Rewari~~JP Division-Minimum Essential Amenities wok for Divyangjan work in connection with Amrita Bharat station at RE Station.	24213	49	60%
826.	53	-	Alwar~~JP Division-Minimum Essential Amenities wok for Divyangjan work in connection with Amrita Bharat station at AWR Station.	21369	44	40%
827.	53	-	Khairthal~~JP Division-Minimum Essential Amenities wok for Divyangjan work in connection with Amrita Bharat station at KRH Station.	18704	27	70%
828.	53	-	Bandikui~~JP Division-Minimum Essential Amenities wok for Divyangjan work in connection with Amrita Bharat station at BKI Station.	21624	54	60%
829.	53	-	Nim ka thana~~JP Division - Minimum essential amenities work for Divyangjan work in connection with Amrit Bharat station at NMK Station.	24023	4	5%
830.	53	-	Phulera~~Phulera:- Provision of 02 lifts at FL station under Amrit Bharat Scheme	23866	0	0
831.	53	-	Provision of 16 OSOP Sale Outlets (Trolleys) at various stations of JP Division	3794	0	90%
832.	53	-	Balance work of 12m wide FOB i.e. stair work, granite, railing & steel work (shed over deck) in connection	10076	0	

			with Amrita Bharat scheme at NNL Station.			
833.	53	-	Shri madhopur~~SMPR - Provision of Coach Guidance Display System at Shri Madhopur station of Jaipur Division	5428	0	
834.	53	-	Provision of Coach Guidance Display System at stations (Chirawa, Chomu Samod & Dehar Ka Balaji) of Jaipur Division	16284	0	
835.	53	-	Baswa~~Baswa - Provision of Coach Guidance Display System at Baswa station of Jaipur Division	5428	0	
836.	53	-	Bansthali niwai~~Banasthali Niwai - Provision of Coach Guidance Display System at Banasthali Niwai station of Jaipur Division	5428	0	
837.	53	-	Ren~~Soft upgradation of Ren station under Amrit Bharat station Scheme.	68402	8234	
838.	53	-	Nokha~~Soft upgradation of Nokha station under Amrit Bharat station Scheme.	55676	26294	
839.	53	-	Didwana~~Soft upgradation of Didwana station under Amrit Bharat station Scheme.	73565	18873	
840.	53	-	Deshnok~~Soft upgradation of Deshnok station under Amrit Bharat station Scheme.	68328	44546	

841.	53	-	Sujangarh~~Soft upgradation of Sujangarh station under Amrit Bharat station Scheme.	90429	27283	
842.	53	-	Degana~~Degana~~Soft upgradation of Degana station under Amrit Bharat station Scheme.	73358	24741	
843.	53	-	Jalore~~Jalore~~Soft upgradation of Jalore station under Amrit Bharat station Scheme.	74011	20099	
844.	53	-	Gotan~~Soft upgradation of Gotan station under Amrit Bharat station Scheme.	83787	7721	
845.	53	-	Merta road~~Soft upgradation of Merta Road station under Amrit Bharat station Scheme.	80696	14674	
846.	53	-	Ramdevra~~Soft upgradation of Ramdevora station under Amrit Bharat station Scheme.	75389	32559	40%
847.	53	-	Nagaur~~Soft upgradation of Nagaur station under Amrit Bharat station Scheme.	60211	7487	
848.	53	-	Barmer~~Soft upgradation of Barmer station under Amrit Bharat station Scheme.	66509	22223	
849.	53	-	Marwar bhinmal~~Soft upgradation of Marwar Bhinmal station under Amrit Bharat station Scheme.	73075	35067	
850.	53	-	Phalodi~~Soft upgradation of Phalodi station under Amrit Bharat station Scheme.	72658	15397	15%

851.	53	-	Balotra~~Soft upgradation of Balotra station under Amrit Bharat station Scheme.	85843	40891	
852.	53	-	Gotan~Provision of FOB 12 M. wide at Gotan station over IR tracks to provide end to end connectivity under Amrit Bharat Station Scheme	73222	0	
853.	53	-	Ren~Provision of FOB 12 M. wide at Ren station over IR tracks to provide end to end connectivity under Amrit Bharat Station Scheme	69039	0	
854.	53	-	Merta road~~Provision of FOB 12 M. wide at Merta Road station over IR tracks to provide end to end connectivity under Amrit Bharat Station Scheme	66054	0	
855.	53	-	Balotra~~Balotra~~Provision of FOB 12 M. wide at Balotra station over IR tracks to provide end to end connectivity under Amrit Bharat Station Scheme	68574	0	
856.	53	-	Nagaur~ Provision of FOB 12 M. wide at Nagaur station over IR tracks to provide end to end connectivity under Amrit Bharat Station Scheme.	68574	0	
857.	53	-	Barmer~~Provision of FOB 12 M. wide at Barmer station over IR tracks to provide end to end connectivity under Amrit Bharat Station Scheme	67353	0	
858.	53	-	Jalore~~Provision of FOB 12 M. wide at Jalor station over IR tracks to provide end to end connectivity under Amrit Bharat Station	68964	0	

			Scheme			
859.	53	-	Provision of Passenger amenities at Platforms at 02 Stations other passenger amenities over FOB's of stations Under Amrit Bharat Scheme.	70539	23777	
860.	53	-	Sujangarh~~Provision of FOB 12 M. wide at Sujangarh station over IR tracks to provide end to end connectivity under Amrit Bharat Station	68574	0	
861.	53	-	Didwana~~Provision of FOB 12 M. wide at Didwana station over IR tracks to provide end to end connectivity under Amrit Bharat Station Scheme	68573	326	
862.	53	-	Nokha~~Provision of FOB 12 M. wide at Nokha station over IR tracks to provide end to end connectivity under Amrit Bharat Station Scheme	68574	0	
863.	53	-	Provision for facilities for Diviyangjan (other than Telecome) at various station (05 station) of Jodhpur Division SUJH, GOTN, JOR, REN & RDRA	62933	22437	
864.	53	-	Provision for facilities for Diviyangjan (other than Telecome) at various station (05 station) of Jodhpur Division MBNL, BLT, NGO,DIA & DSO	78104	0	
865.	53	-	Provision for facilities for Diviyangjan (other than Telecome) at various station (05 station) of Jodhpur Division MTD,DNA,NOK, BME & PLC	58248	4549	

866.	53	-	Marwar bhinmal~~Provision of FOB 12 M. wide at Marwar Bhinmal station over IR tracks to provide end to end connectivity under ABSS	64380	0	
867.	53	-	Phalodi~~Provision of FOB 12 M. wide at Phalodi station over IR tracks to provide end to end connectivity under Amrit Bharat Station Scheme	64380	506	
868.	53	-	Degana~~Provision of FOB 12 M. wide at Degana station over IR tracks to provide end to end connectivity under Amrit Bharat Station Scheme	65766	0	
869.	53	-	Electric Work in c/w Augmentation/Strengthening and Back up of power supply arrangement at 15 Stations over JU Div under ABSS.	48599	0	
870.	53	-	Electrical work of SigNages, Facade lighting, LED based name board and Green energy measures at 15 Nos stations of JU Div.under Amrit Bharat Scheme	84445	750	
871.	53	-	Provision of 02 nos. Elevators (Lifts) each at 08 numbers of stations (DSO, NOK, NGO,MTD, SUJH, DIA, DNA & REN) for central FOB under Amrit Bharat S	66614	0	
872.	53	-	Provision of 2 nos. Elevators (Lifts) each at 07 numbers of stations (GOTN, PLC, RDRA,BLT,BME,JOR & MBNL) for central FOB under Amrit Bharat Scheme	58287	0	

873.	53	-	Provision of Passenger amenities work for 07 stations of Jodhpur division under Amrit Bharat Scheme	53825	36305	
874.	53	-	Provision of Passenger amenities work for 06 stations of JU Division Under Amrit Bharat Scheme	51320	31731	
875.	53	-	Jodhpur Division: Soft upgradation of at various stations by providing PF shelter & Hording under Amrit Bharat station Scheme.	34999	0	
876.	53	-	Ramdevra~~Provision of FOB 12 M. wide at Ramdevra station over IR tracks to provide end to end connectivity under Amrit Bharat Station Scheme	68574	0	
877.	53	-	Raising of medium level platform no. 1 of Pipar City Halt (HG-2),& Rail level Gagaria halt (HG-2) and Ramsar Halt (HG - 2) stations	51863	0	
878.	53	-	Nawa city~~Nawa city~~Development of Customer facilities at Goods shed of Nawa City station	70925	0	
879.	53	-	Development of New Goods shed at Marwar Mundwa station	49708	0	
880.	53	-	Gotan~~Gotan~~Development of Customer facilities at Goods shed of Gotan station	69493	0	
881.	53	-	Development of New Goods shed at Bhawi station	68947	0	

882.	53	-	Development of New Goods shed at Parbatsar Mela Maidan	49771	0	
883.	53	-	Badwasi~~Development of Customer facilities at Goods shed of Badwasi station	66842	0	
884.	53	-	Thaiyat hamira~~Development of Customer facilities at Goods shed of Thaiyat Hamira station	49060	0	
885.	53	-	Deshnok~~Development of Customer facilities at Goods shed of Deshnok station	66112	0	
886.	53	-	Barmer~~Development of Customer facilities at Goods shed of Barmer station	29447	0	
887.	53	-	Baniya sanda dhora~~Development of Customer facilities at Goods shed of Baniya Sanda Dhora station	48936	0	
888.	53	-	Jalore~~Development of Customer facilities at Goods shed of Jalor station	79236	0	
889.	53	-	Phalodi~~Development of Customer facilities at Goods shed of Phalodi station	29556	0	
890.	53	-	Development of New Goods shed at Chilo station	82894	0	
891.	53	-	Bhagat ki kothi~~Bhagat ki kothi~~Development of Customer facilities at Goods shed of Bhagat Ki Kothi station	184226	0	

892.	53	-	Development of Customer facilities at Goods shed of SONU station	124763	0	
893.	53	-	Pokran~~Pokran~~Provision of new FOB at Pokaran station of 3.66 metre width under Umbrella works 390 of 2022-23	20000	0	
894.	53	-	Pokran~~Pokran~~Renovation of existing goods platform into HL passenger platform at Pokaran station.	14998	0	
895.	53	-	Bhagat ki kothi~~Provision of Pradhan Mantri Bhartiya Janaushadhi Kendra (PMBJK) outlet at Bhagat Ki Kothi (NSG - 3) station.	1286	0	
896.	53	-	Provision of additional Platform shelter at Degana, Deshnok, Gotan and Sujangarh stations under ABSS over JU division.	20941	0	
897.	53	-	Provision of additional Platform shelter at Marwar Bhinmal, Ramdevra, Didwana and Balotra stations under ABSS over JU division.	17355	0	
898.	53	-	Provision of additional platform shelter at Nagaur, Nokha, Barmer and Merta road Stations under ABSS over JU Division.	20941	0	
899.	53	-	Provision of additional Platform shelter at Ren, Phalodi and Jalor stations under ABSS over JU division.	22038	0	
900.	53	-	Jodhpur cant~~Jodhpur cant~~Provision Foot over bridge at Jodhpur Cant (NSG - 6) station.	19482	0	

901.	53	-	Raniwara~~Provision of quick watering arrangement system at Raniwara station in JU Division	24911	0	
902.	53	-	Makrana~~Provision of an additional Foot Over Bridge end to end landing at Makrana station.	23999	0	
903.	53	-	Gudha~~Provision of FOB at Gudha (NSG - 6) station.	23065	0	
904.	53	-	Kuchaman city~~Kuchaman city~~Provision of coach indication boards along with train display boards and clocks at PF - 2 of Kuchaman City station	4213	0	
905.	53	-	Luni~~Provision of coach indication boards along with train display boards and clocks at PF - 1 & 2 of LUNI station	7401	0	
906.	53	-	Raniwara~~Raniwara~~Provision of coach indication boards along with train display boards and clocks at PF - 1 of Raniwara station	4213	0	
907.	53	-	Dhanera~~Provision of coach indication boards along with train display boards and clocks at PF - 1 of Dhanera station	4213	0	
908.	53	-	Provision of coach indication boards & SLDB at PF – 2 of Bhagat Ki Kothi and Rai ka bag stations	12213	0	
909.	53	-	Provision of coach indication boards & SLDB at PF – 1 & 2 of Mokalsar and PF - 1 of Modran stations	16834	0	

910.	53	-	Samdari~~Provision of coach indication boards & SLDB at PF – 1,2 & 3 of Samdari station.	18361	0	
911.	53	-	Provision of coach indication boards & SLDB at PF – 2 of Makrana and PF – 1 & 2 Nava City stations.	16834	0	
912.	53	-	Sambhar lake~~Provision of coach indication boards & SLDB at PF – 1 & 2 of Sambhar Lake station	10728	0	
913.	64	PB-463	North Western Railway - Construction of boundary wall/ compound wall at vulnerable locations of Golden Quadrilateral/Golden Diagonals/high density routes and on approaches of major cites vulnerable for encroachment (PB#1369/NR/2023-24)	0	0	
914.	64	PB-462	North Western Railway - Construction/improvment of service buildings, Hospitals, Institutes, community halls, roads (other than station approach roads), hostels, parks stadium, infrastructure for track machine staff/protection work for safety of track etc. (PB#1374/NR/2023-24)	0	0	
915.	64	PB-464	North Western Railway - Provision of CCTV/Tunnel monitoring System/ Fire fighting system & other allied works in RPF posts/outposts/Railway Tunnels, etc. and construction/ Replacement/ Modification/upgradation of barracks/office	0	0	

			building/ etc. for RPF/ Other Central Armed Forces (PB#1370/NR/2023-24)			
916.	64	-	Supply, installation and commissioning of 09 nos. CCTV cameras at BI, MVJ, BJNR, NSD, SOD, MD Jn., JWB, PDWA and PUHT.	2970	2225	0
917.	64	-	Provision of 6 bedded model male barrack at Mavli Junction with all basic amenities and furniture as per barrack template's	3745	0	
918.	64	-	Provision of Boundary Wall to Prevent encroachment and trespassing in Jurisdiction of ADEN/Marwar jn.	9947	9692	99%
919.	64	-	ADEN/RPZ Sub Div – Provision of 3790m long Boundary wall with unserviceable sleepers to prevent Cattle Run-over in GSD-PMO section.	4985	1538	80%
920.	64	-	Provision of Boundary Wall to prevent encroachment and trespassing in jurisdiction of ADEN/ABR	9947	4518	99%
921.	64	-	Provision of boundary and Compound wall to prevent encroachment in Ajmer City Area PRCC wall 541 Rm RRM wall 1450Rm	11997	4147	90%
922.	64	-	Provision of Boundary Wall to Prevent encroachment and trespassing in Jurisdiction of ADEN/Bhilwara (Length 4850 M, Using US Sleepers and Rails)	4994	0	
923.	64	-	AII (RPF's Company Reserve, Ajmer)-Modernization and upgradation RPF barracks.	5620	0	

924.	64	-	ADEN/RPZ Sub.Div.:- Provision of 16250 meter long boundary Wall at Vulnerable locations to prevent encroachment and CRO in COR-UDZ section.	23361	0	5%
925.	64	-	Construction of RCC boundary wall to safegaurd track and as well as to avoid encroachments between Bathinda B cabin and Bathinda Jn. (2.400 Kms)	20729	0	0
926.	64	-	Provision of B/Wall to prevent trespassing/ encroachment with use of released PRC sleepers in ADEN/AWR section 13000Rm.	13881	10255	100%
927.	64	-	Khairthal~~Khairthal at RE end – Providing Boundary wall Total 900 RM at Re end of KRH station	5334	0	5%
928.	64	-	Rewari~~Jaipur~~Provision of B/Wall to prevent trespassing/ encroachment with use of released PRC sleepers in ADEN/BKI section Total 12000 RM.	15839	15839	100%
929.	64	-	Provision of 1000Rm RCC B/Wall with PRC panel & cast in situ column, 9000Rm sleeper fencing to prevent trespassing/encroachment under ADEN/AWR.	22006	0	22%
930.	64	-	Provision of 1000Rm RCC B/Wall with PRC panel & cast in situ column, 9000Rm sleeper fencing to prevent trespassing/encroachment under ADEN/BKI.	22006	0	

931.	64	-	Jaipur~~Provision of installation of 06 CCTV Cameras at Armory situated at RPF Armory Jaipur station.	591	0	0
932.	64	-	JP-Division – Up gradation of old RPF barracks of Jaipur Division.	6722	0	
933.	64	-	Jaipur~~RPF post Jaipur- Contraction of Video Surveillance System Control Room.	1970	0	
934.	64	-	Jaipur~~Provision of hostel facility DNB (PG) Doctors 18 Nos. by construction of 2nd floor on existing old OPD building of CH / JP	9899	0	30%
935.	64	-	Jaipur~~Construction of separated medical store building adjacent existing conference building of central hospital JP	12498	0	5%
936.	64	-	ADEN (RGS) Sub Divi.- Construction of Boundary wall at NNL, PCMK, GND, COM station and RE station approach to protect Railway land from encroachment.	22985	0	
937.	64	-	Installation of CCTV and construction of Control Room at DPA, GTJT & BNLW Railway Station.	10719	0	
938.	64	-	Provision of 12 Nos CCTV Cameras at RPF post Gandhinagar Jaipur, Bandikui, Alwar, Rewari, Ringus and Phulera each 02 No's CCTV Cameras for Armory .	962	0	
939.	64	-	New construction RPF out post Sikar and BNLW10-10 Bed barrack with centralizes cooling system and furniture.	15999	0	

940.	64	-	JP Division-Augmentation of community hall at JP, FL, BKI and SIKR station.	23998	0	
941.	64	-	Jaipur-SWM-Providing boundary wall between Km 91/0 to 131.40 in SWM-JP section premises to prevent encroachment (1500 RM)	17997	0	
942.	64	-	Jaipur~~Work of office building and shed for Jaipur laundry.	24377	0	
943.	64	-	Provision of fencing 60.0 km (with U/S Sleeper) along the railway track to prevent tracepasser/CRO in Phulera -Jodpur, Degana	30696	0	
944.	64	-	Jodhpur~~Construction of office accommodation for GSU unit at Jodhpur	9844	0	
945.	64	-	Degana~~Out Post building with 10 bedded barrack at Out Post Degana	8769	0	
946.	64	-	Nagaur~~Out Post building with 04 bedded rest room against existing building at Out Post Nagaur	3646	0	
947.	64	-	Nokha~~Out Post building with 04 bedded rest room against existing building at Out Post Nokha	3721	0	
948.	64	-	Out Post building with 04 bedded rest room against existing building at Out Post Ramdevra station.	3687	0	

Chapter-6

Survey & Construction Department

Construction Projects & Engineering works -2023-24.

SN	Particulars of works	Yea of Sanction	Anticipated Cost of Project. (in Cr.)	Exp. Up to Mar.-24	Physical progress as on 31.03.2024
A	**New Line-11**				
1.	Dausa-Gangapur city (94.65 km)	1996-97	950.00	1020.76	99.99
2.	Ratlam-Dungarpur Via. Banswara (188.85 km)	2011-12	4500.00	197.63	7.50
3.	Pushkar- Merta (59 km)	2013-14	967.23	0.78	0.00
4.	Ras-Merta (59 Km).	2023-24	947.00	0.00	0.00
5.	Taranga Hill-Abu Road via Ambaji-(89.38 km).	2017-18	2798.16	178.32	4.70
6.	Neemuch-Badi SadriNew line Project (48.35 km)	2017-18	495.18	122.02	9.00
7.	Gudha- Thathana Mithri -Const of Dedicated test Track Ph-I (22.8Km)	2018-19	353.48	303.99	87.00
8.	Dedicated test Track for RDSO Ph-II (37.5Km)	2019-20	466.42	139.50	31.00
9.	NWR-BG line between Ringus-Khatu shyamji (17.9km)(PB#NR/2023-24)	2023-24	0.00	0.00	0.00
		Total		**2152.50**	
B	**Gauge Conversion-14**				
1.	Nathdwara-Nathdwara Town (9.6km) MavliJn.-Bari Sadri (82.01 Km) MMof Ajmer- Chittaurgarh - Udaipur (300Km)	1996-97	1200.00	974.28	All-COR-UDZ UDZ- UMRA commissioned, MVJ-BI (100%) & NDT-NDIT (0%)
2..	Jaipur-Ringus-Churu & Sikar- Loharu (320.04 km)	2008-09	1200.00	1215.58	100.00
3..	Suratpura-Hanumangarh- riganganagar (240.35 km) & Hanumangarh bye Pass	2008-09	896.13	795.15	96.00
4.	DevgarhNathdwaraGC(82.54 km) part of marwar – Mavli GC Project	2017-18	968.92	56.53	17.00
			Total	**3041.54**	
5.	Sirmuttra –GangapurCity NL (75.65 km) part of Dholpur – Sirmuttra GC project .**NCR Pink Book**	2010-11	622.41	0	0.00
		Total incl.NCR		**3041.54**	

C	**Doubling-15**				
1.	Phulera-Degana (108 km)	2015-16	701.81	691.09	99.90
2	Degana-RaiKaBagh(145 km)	2018-19	808.85	902.45	99.90
3.	SawaiMadhopur-Jaipur (131.27 Km)	2019-20	1203.89	0.00	0.00
4.	Luni-Samdari-Bhildi(271 Km)	2023-24	3085.59	0.00	0.00
5.	Ajmer-chanderiyah (178.28km)	2020-21	1634.79	0.00	0.00
6.	SawaiMadhupur-Bypass Line (6.98 km)	2020-21	239.54	49.47	0.00
7.	Rewari-Khatuwas Doubling (27.73 Km)	2020-21	352.41	1.30	12.00
8.	Churu-Ratan garh Doubling (42.81 KM)	2022-23	422.60	43.54	37.00
9.	Manharu-Bhiwami Khera Doubling (31.50 KM)	2023-24	413.09	0.07	22.00
10.	Khatuwas-Narnual Doubling (24.12 KM)	2023-24	313.31	4.13	20.00
11.	Bhiwani-Dhob bahali Doubling (24.30 KM)	2023-24	471.06	11.97	18.00
12.	Churu -Sadulpur (57.82 KM)	2023-24	468.64	0.00	0.00
13.	Marwar Bye Pass line (3.9 KM)	2023-24	71.21	0.00	0.00
			Total*	**1704.02**	
D	**Traffic facility-16**				
S.N	**Particulars of works**	**Year of Sanction**	**Cost of works**	**Exp. Up to Mar.-24**	**Physical progress as on 31.03.2024**
1.	Rewari-Sadulpur - Bypass line	2012-13	64.03	61.73	72.00
2.	KhatipuraPhase-II Coach Care Complex	2019-20	204.78	2.40	5.00
			Total	**64.13**	
E	**Passenger Amenities-53**				
1.	Udaipur		355.60	64.97	25.00
2.	Jaipur		716.88	93.70	42.00
3.	Gandhi Nagar Jaipur		212.48	52.64	56.00
4.	Jodhpur		493.49	1.93	6.00
5.	Jaisal mer		140.14	30.29	60.00
6.	Bikaner			0.00	0.00
	Total	**1918.62**		**243.53**	
		G.Total		**7205.72**	

Chapter-7

Mechanical

Workshops Performance (2023-24)

1. Workshop

1.1.1 **Ajmer Group of Workshop** – It comprises of Loco Workshop and Carriage Workshop. Each of these workshops is headed by Dy. CME. CWM (SAG) is overall in-charge of these workshops. Loco workshop undertakes POH of BG wagons, POH of DEMUs(DPC+DTC+TC), POH of MEMU, POH of SPART/SPARME and POH/IOH of Tower wagons**.** Carriage Workshop undertakes POH of ICF & SS-2/SS-3 of LHB BG coaches, POH of DEMU and IOH of ICF/LHB Bogies and POH of Palace on Wheels. In addition to above, various RSP works related to BG coaches and wagon is taken at both workshops.

1.1.2 **Jodhpur Workshop** - This workshop is headed by CWM (SAG) and undertakes POH of ICF BG coaches,SS-2/SS-3 of LHB BG coaches, IOH of ICF/LHB Bogies and RSP works related to ICF/LHB coaches.

1.1.3 **Bikaner Workshop** – This workshop is headed by CWM (JAG) and undertakes POH of BG Wagon, POH of MG coaches, IOH of ICF/LHB Bogies and RSP works related to BG wagon**.**

Salient features of these workshops are listed below:

S.N.	Description	Ajmer (L)	Ajmer (C)	Jodhpur	Bikaner
1.	Total area of workshop (Sq.M.)	1,60,000	2,50,000	1,15,339	1,70,545
2.	Covered area of workshop (Sq. M.)	66,703	84,293	55,817	35,052
3.	Length of rail track (Mtrs.)	5,692.10	8,630	5,400	7,500
4.	Average electricity consumption per month (In units)	96305.25	132879	99385	46093
5.	Average salary bill per month(Rs. in Lacs)	1053	1345	1078	489.07
6.	Available Railway Quarters	563		363	51
7.	Consumption of Energy (HSD, Kerosene, Furnace oil) per month (In KL)	4.19	6.778	3.834	3.54

2. OUTTURN OF WORKSHOP-

POH outturn of various activities of different workshops during the year 2023-24 is listed below.

Sr	Description	Ajmer(L)	Ajmer(C)	Jodhpur	Bikaner
1.	BG coach POH in VU	-	919	955	-
2.	MG coach POH in VU	-	-	-	37
3.	BG wagon POH in VU	1645	-	-	1369
4.	DEMU/DPC in VU	59	124	-	-
5.	SPART/SPARMV	14	-	-	-
6.	MEMU(MC+TC) POH	76	-	-	-
7.	IOH of Tower wagon	5	-	-	-
8.	POH of Tower wagon	5	-	-	-

3. ROLLING STOCK PROGRAMME AND DEPOSIT WORK-

In addition to POH activities workshop also undertake various works for modification/ up gradation of rolling stock under RSP. Works done by the workshop in this regard during 2023-24 are listed below.

S.N.	Description of RSP works	Ajmer (L)	Ajmer (C)	Jodhpur	Bikaner	Total
1.	Conversion of ICF Coaches into high speed NMGHS coaches.	-	65	28	-	93
2.	Up gradation of coach toilets of AC coaches.	-	42	-	-	42
3.	Provision of Fire detection system in AC coaches.	-	325	-	-	325
4.	Provision of Fire detection & suppression system for Power Cars.	-	2	-	-	2
5.	Provision of Fire detection & suppression system for Pantry	-	10	-	-	10

	Cars.					
6.	Modification of air brake pipe line & associated fitting in coaches.	-	34	48	-	82
7.	Provision of Pressurization flushing system in LHB Non-AC Coaches.	-	38	-	-	38
8.	Retrofitment of revised wiring with modified junction boxes and connectors in coaches.	-	25	-	-	25
9.	Complete assembled FIAT Bogies with 160 KN Air spring.	-	19	6	-	25
10.	Provision of 160 KN Air spring assemblies for LHB Bogies.	-	15	-	-	15
11.	Twin pipe conversion of Wagons.	333	-	-	197	530
12.	Complete renewal of end wall, side wall and flooring of BOXN wagons.	8	-	-	5	13
13.	Retrofitment of high capacity high tensile CBC, Constant contact side bearers CCSB and non metallic Snuber wedge on wagons.	72	-	-	165	237
14.	Up gradation and rehabilitation of BOXN wagons to BOXNR.	8	-	-	0	8
15.	Special repairs of wagons	300	-	-	200	500

3. ASSISTANCE TO DIVISION–

Workshops also supply IOHed BG coach bogies and wheel sets to divisions for replacement in coaches, wagons & locos, as required to keep them in road worthy condition. Coach bogies and wheel sets of coaches and wagons which were supplied to divisions during 2023-24 are as follows:

S.N.	Description	Ajmer Loco	Ajmer Carriage	Jodhpur	Bikaner
1.	IOH of Bogies for BG Coaches (ICF)	-	737	795	1008
2.	SS-1 of Bogies for BG coaches (LHB)	-	691	256	-
3.	BG ICF Wheel	-	386	261	205
4.	LHB Coach's Wheel	-	817	123	108
5.	BG Diesel Loco Wheel	175	-	108	-

5. SCRAP DISPOSAL (2023-24)-

S.N.	Description	Ajmer (L)	Ajmer (C)	Jodhpur	Bikaner	Total
1.	Ferrous in MT	3671.364	2581.881	2938.360	2587.042	11778.647
2.	Non Ferrous in MT	180.070	47.319	996.891	16.829	1241.109
	G. Total	3851.434	2629.200	3935.251	2603.871	13019.756

6. COST OF POH –

Costs of POH of different types of Rolling stock during 2023-24 were as under.

(Cost is in Rs '000')

S.N..	Type of Stock	Ajmer Loco	Ajmer Carriage	Jodhpur	Bikaner
1.	BG Coach PCV NAC	-	2140	1439	-
2.	BG Coach OCV NAC	-	1518	1398	-
3.	BG Coach PCV AC	-	3781	2382	-
4.	BG Coach OCV AC	-	2140	-	
5.	MG Coach PCV NAC	-	-	-	839.7
6.	MG Coach OCV	-	-	-	834
7.	BG Wagon	516	-	-	490.5
8.	DPC POH	4970	-	-	-

7. INCENTIVE -

All the workshops of this railway are covered under incentive scheme. Important parametersrelated to incentive during 2023-24 are indicated below:

Description (Avg. per month)	Ajmer Loco	Ajmer Carriage	Jodhpur	Bikaner
Incentive %	41.9	44.1	45.2	46.5
Absenteeism	12.6	11.8	11.7	15.3
DW Booked	399.5	1246.3	899.0	364.7
EIW Booked	192.8	260.8	136.3	113.7
Load Lifted Per DW	226.6	253.6	255.9	247.6
Incentive Earned Amount (in Lacs)	34.74	109.63	83.32	34.49
Over Time (in Lacs. Monthly Avg.)	0.42	0.26	2.14	0.37

8. AVERAGE POH CYCLE TIME (in Days as per WISE)-

POH cycle of different stocks is given below for the year 2023-24

S.N.	Type of Stock		Ajmer Loco	Ajmer Carriage	Jodhpur	Bikaner
1.	ICF BG Coach (POH)	AC	-	9.03	11.73	-
		Non-AC	-	9.41	15.57	-
2.	LHB BG Coach	AC	-	10.12	10.37	-
		Non-AC	-	8.64	7.93	-
3.	MG Coach (POH)		-	-	-	11.75
4.	BG Wagon (POH)		5.88	-	-	6.46
5.	DEMU/DPC POH		12.68	5.49	-	-
6.	EMU/MEMU		12.25	-	-	-
7.	SPART/SPARMV		10.14*	-	-	-

* WISE figures are not available

9. QUALITY ASSURANCE-

All coaches and wagons POH in the workshop are offered for inspection to Neutral Train Examiner. All cases of sick marking of coaches within 100 days are critically examined to take necessary remedial measures. Performance during 2023-24 has been as under:

9.1 Sick marking of coaches within 100 Days for the year 2023-24.

S.N.	Type of Stock	Ajmer Carriage	Jodhpur	Bikaner
1.	BG Coach	11	06	-
2.	MG Coach	-	-	0

9.2 Sick marking of wagons within 90 Days for the year 2023-24

S.N.	Type of Stock	Ajmer Loco	Bikaner
1.	BG Wagon	0	0

10. NEW M&P ITEMS COMISSIONED- M&P items are commissioned in the workshop as per requirement to keep pace with changing work requirement. Following M&P items were included in workshop during the year 2023-24.

S.N.	Consignee	Name of Item	Qty.	Cost In Rs.000
1	Dy.CME (L)/AII	Laser Engraving Machine	1	314
2	Dy.CME (L)/AII	Air plasma cutting Machines (405)	4	452
3	Dy.CME(C)/AII	Laser Engraving Machine for marking on copper tag for LHB Spring	1	296
4	Dy.CME(C)/AII	Diesel Operated Fork lift Truck 3T	1	880
5	Dy.CME (L)/AII	Electrically Driven Air Compressor 55 CFM	1	684
6	Dy.CME(C)/AII	Portable Single Operator Rectltler Based (lgbt) Double Bridge Type Dc Arc Welding Set Suitable For Manual Are Welding 400 Amp with CAMC	10	350
7	Dy.CME(C)/AII	Portable single Operated rectifier based IGBT Double bridge type DC are welding set suitable for manual Arc welding 400Amp with CAMC	5	174
8	Dy.CME(C)/AII	Diesel operated forklift truck 3 T	1	1054
9	Dy.CME(C)/AII	HYD pusher & puller for LHB anti roll bar	1	478
10	Dy.CME(C)/AII	HYD, PRESSING System for Primary Springs of LHB Coaches	1	1450
11	CWM/BKN	CTRB installer cum Puller for LHB coaches	1	594.72
12	CWM/BKN	High Pressure Hot Water Jet Cleaning Machine	1	592

13	CWM/BKN	Hydraulic Pressing System for primary Spring of LHB Coach bogies	1	377.6
14	CWM/JU	Hydraulic machine for assembly and disassembly of draft gear	1	1928
15	CWM/JU	Supply, installation and commissioning of Abrasive cut off machine for cutting the hardened component along with all standard accessories	1	951
16	CWM/JU	Digital brinell hardness testing machine	1	570
17	CWM/JU	Centre Lathe	1	1180
Sr.	**Consignee**	**Name of Item**	**Qty.**	**Cost In Rs.000**
18	CMT/AII	Supply, installation and commissioning of Automatic digital melting point apparatus	1	597
19	Dy.CME(C)/AII	Multi head Hyeraulic Swaging unit size up to 1'' with tooling kit	1	531
20	Dy.CME(C)/AII	Air Plug Gauge	1	678
21	Dy.CME(C)/AII	¾" Square Drive 18 V Battery operated Torque Wrench	1	531
22	Dy.CME (L)/AII	Profile Cutting Machine	1	96
23	Dy.CME (L)/AII	Air Plasma Cutting Machines	4	428
24	Dy.CME (L)/AII	Computerized DV Test Bench	1	974
25	Dy.CME (L)/AII	Battery operated Platform Truck CAP 02 T/Dsl Shop	1	474
26	Dy.CME (L)/AII	Fork lift truck 03 T/Dsl Shop	1	1250
27	Dy.CME (L)/AII	IGBT Welding sets 400 amps	21	1073
28	Dy.CME(C)/AII	AJTB Lathe mc	1	23053
29	CWM/JU	Static Weigh Bridge	1	2952

30	Dy.CME/L/AII	Oil Filteration plant	1	1618
31	Dy.CME(C)/AII	Heavy Duty Turning Lathe/Cenre Lathe	1	5893
32	Dy.CCMT/AII	OES Lab Spectrometer	1	7115
33	Dy.CME (L)/AII	Static Weigh Bridge(Rail cum Road)	1	2918
34	CWM/JU	AJTB Lathe mc	1	23053
35	Dy.CME(C)/AII	Grit Blasting plant	1	9600
36	CWM/JU	Radial drilling machine	1	2379
37	Dy.CME(L)/AII	Guillotine shearing machine double column CAP 16x3100 mm	1	4020
	TOTAL		**76**	**101558.32**

11.0 New Activities &Major Achievements of Workshop in the year 2023-24:-

a) New Activities-

- NWR has started Rejection Analysis of major components of coaches and wagons during maintenance in workshops. It includes Cause-Wise Failure, Make-Wise Failure & Age-Wise Rejection of components over a time period with the help of Google Studio tool in one click.

b) Major Achievements-

1. Ajmer (C) WS done POHed/SS2/SS3 of 919 BG coaches against the target of 752 BG coaches which includes SS2/SS3 schedule of 533 LHB coaches whereas Jodhpur WS has POHed of 955 BG coaches against the target of 912 BG coaches which includes SS2 schedule of 89 LHB coaches.
2. Ajmer (L) WS done POHed of 1645 BG wagons against the target of 1636 BG Wagons.
3. Ajmer (L) WS done POHed of 76 MEMUs against the target of 72 MEMUs.
4. Bikaner WS has POHed of 1369 BG wagons against the target of 1352 BG Wagons.
5. Carriage workshop, Ajmer has achieved Best Cycle time over IR in POH of ICF AC & MEMU coaches in FY 2023-24.
6. During 2023-24, 3487 bogies which include 947 LHB bogies have been given IOH by NWR workshops.
7. During 2023-24, 530 wagons have been provided with twin pipe modification.

8. 2 Centre of Excellence, 1 in Ajmer Carriage Workshop & 1 in Bikaner Workshop have been developed in FY 2023-24.

9. All workshops of NWR have acquired all important certification i.e. IMS (including Environment Management), 5S (Certification for Workplace Management System), ISO 3834-2:2005 (for Welding Quality Management), ISO:50001:2011 (for Energy Management), GreenCo Rating, etc. to ensure good quality of maintenance and friendly working environment. Three workshops i.e. Ajmer-Carriage, Ajmer-Loco & Jodhpur-Carriage are having GreenCo Gold Rating whereas Bikaner has Silver Rating.

10. Successfully accomplished the target of 2500 nos. of youth under Rail Kaushal Vikas Yojna (RKVY) which was short duration training in four trades i.e. Electrician, Fitter, Welder& Machinist. Total 2587 nos. of youth trained at the end of FY 2023-24 after launching this scheme from Sept. 2021 onward.

11. Conversion of MG coaches into Heritage tourist Coaches for Mawali- Marawar Section done by Ajmer Carriage Workshop, which was highly appreciated by Honourable Rail Minister.

12. Aastha Train Revamp: Successfully completed the Periodic Overhaul (POH) and complete refurbishment of the Aastha special.

***

C&W Performance (2023-24)

(A) COACHING PERFORMANCE (BG)

S.N.	Items	2022-23		2023-24	
		Target	Actual	Target	Actual
01.	Ineffective %age AC coaches	6	3.24	6	5.61
02.	Ineffective %age NAC coaches	5	2.8	5	5.43
03.	Coach Detachment (Territorial)	4	1	4	6
04.	Coach Detachment (Ownership)	2	0	0	3
05.	Hot Axle (own)	0	0	0	0
06.	Fire incident (own)	0	0	0	0
07.	Train-parting (own)	NA	0	NA	0

(B) FREIGHT PERFORMANCE (BG)

S.N	Item	2022-23		2023-24	
		Target	Actual	Target	Actual
1	Ineffective %age	2.05	2.03	2.50	2.40
2	Detachments	20	4	4	9
3	Train Parting	10	9	8	3
4	Hot axle	67	68	61	31

Detachment: - Majority of the cases are on centre Pivot Broken (4 cases). Compliance of RDSO guidelines for operation and maintenance of BVZI wagon to stop failure.

(C) COACHING & WAGON DEPOTS.

BG	Division			
	AII	BKN	JP	JU
	Depots			
Major Coaching depot	MDJN, UDZ	BKN,SGNR, LGH	JP	JU
Medium Coaching depot	--	BNW, HSR	--	BME, MTD (DEMU Shed)
Minor Coaching depot	--	--	--	--
Only Terminating Examination	AII, MJ, ABR	SOG CUR	RE, SIKR, BKI	JSM, BGKT
Only Enroute Examination	ABR, AII	SOG,CUR	BKI, RE, SIKR	MTD

Wagon depot 'A' category	--	--	FL	--
MG Depot	MJ	--	--	--

Capacity of Washing Lines & Sick Lines as on March 2023. (BG)

Div.	Depot	Holding	Washing line Capacity (LHB Coaches)				Total	Sick line capacity	
								Covered space (Coaches)	
			1	2	3	4		Line-1	Line-2
AII	MDJN	328	26	26	26	--	3	6	6
	UDZ	354	22	24	--	--	2	2	2
BKN	BKN	322	22	22*	--	--	2	3	3
	LGH	97	24	--	--	--	1	3	3
	SGNR	362	22	24	--	--	2	3	3
	BNW	111	17**	--	--	--	1	1	--
	HSR	22	24	--	--	--	1	3	3
JP	JP	555	24	24	24	-	3	6	6
JU	JU	538	24	24	22	22	4	8	2
	BME	174	22	--	--	--	1	2	--
	BGKT	--	24	--	--	--	--	--	--
	Total	**2863**	-	--	--	--	21	--	--

* LHB coaches can not be placed due to curve at W/L

** LHB Coaches are not being maintained at BNW.

DEMU

Div	Depot	Holding	Automatic Coach Washing Plant With Washing Apron Capacity (Cars)	Running Repair Capacity (Cars)	Tyre Training Machine	Heavy Repair shed
JU	MTD	165	12 cars (MTD)	2 pits Lines (12 car each)	01	2 Line in heavy repair sheds with 02 pits of one coach length on each line.

DEMU Failure/Ineffective

Year	Holding		Average Ineffective		Ineffective %		Failure Data as per ICMS
	DPC	TC	DPC	TC	DPC	TC	
2022-23	36	129	4.37	8.8	12.14%	7.14%	49
2023-24	36	129	4.36	11.2	12.12%	8.66%	35

Sick line at Phulera Freight depot: -

Berthing capacity under covered shed. (In meter & VUs)	In meters	In VU's
	80X20 =160Mtrs	8 Wagons

Phulera ROH depot: -

Berthing capacity under shed. (In meter & VUs)	**In meters**	**In VU's**
	100X23 =2300Mtrs	10 Wagons

Setting up of Mechanized laundries:-

Identified Depot/location	**Whether on Departmental or BOOT model**	**Capacity/day (2-Shift of 8 hrs.) TPD**
BKN	Departmental	5
JU	Departmental	11.8
UDZ	Departmental	6.5
JP	Departmental	8.5
SGNR	BOOT	5
BME	Departmental	1.9
AII	Departmental	2
	Total	**40.7**

Coaching Maintenance Management System (CMMS) Development.

1. CMM is implemented in all coaching depots
2. As per RB instructions, all coaching trains maintenance and their BPC are being issue through CMM.
3. Training to all coaching depot of CMM applications are being imparted by CRIS through VC.
4. A Separate unit is also available in coach history for any unusual occurred & Rail Madad complaints.
5. Daily ineffective could be seen on homepage of CMM.

Safety Drives.

Following safety drives were launched in NWR in 2023-24 to super checks maintenance practices, safety standards in coaches/wagons operations.

SD. No.	Subject	Rly. Board's ref. letter No. / NWR's letter No.	Period
05/2023	Week long Safety Drive for the month of April 23	NWR/HQ/Safety/SD/5/23 RB Letter No. 2023/Safety-I/3/3 dated: 05.04.2023	7 days w.e.f. 10.04.23 to 16.04.23
06/2023	Week long Safety Drive for the month of May 23	NWR/HQ/Safety/SD/6/23 RB Letter No. 2023/Safety- I/3/3 dated: 01.05.2023 RB Letter No. 2023/Safety- I/3/3 dated: 07.05.2023	7 days w.e.f. 08.05.23 to 14.05.23
07/2023	Safety Drive regarding strict observation of rules in shunting.	NWR/HQ/Safety/SD/7/23	15 days w.e.f. 16.05.23 to 30.05.23
08/2023	Foot plating by CLI with nominated crew for complete beat.	NWR/HQ/Safety/SD/8/23 RB Letter No. 2023/Safety/Electrical /3 dated: 22.05.2023	30 days w.e.f. 23.05.23 to 21.05.23
09/2023	Week long special safety drive on Container Trains.	NWR/HQ/Safety/SD/9/23 RB Letter No. 2023/Safety(DM) /12/1 dated: 30.05.2023	7 days w.e.f. 01.06.23 to 07.06.23
10/2023	Week long safety drive.	NWR/HQ/Safety/SD/10/23 RB Letter No. 2023/Safety(Inquiries) /22/5 dated: 05.06.2023	7 days w.e.f. 06.06.23 to 12.06.23
11/2023	Week long safety drive for the month ofJune 23	NWR/HQ/Safety/SD/11/23	7 days w.e.f.

		RB Letter No. 2023/Safety-I/3/3 dated: 29.05.2023	12.06.23 to 18.06.23
12/2023	Intensive 15 day's safety drive.	NWR/HQ/Safety/SD/12/23 RB Letter No. 2023/Safety-I/3/3 dated: 07.06.2023	15 days w.e.f. 08.06.23 to 22.06.23
13/2023	Week long safety drive for the month of July- 23	NWR/HQ/Safety/SD/13/23 RB Letter No. 2023/Safety-I/3/3 dated: 28.06.2023	7 days w.e.f. 10.07.23 to 16.07.23
14/2023	Safety Drive on Monsoon Precaution.	NWR/HQ/Safety/SD/14/23	15 days w.e.f. 19.07.23 to 04.08.23
15/2023	Week long safety drive for the month of Aug.- 23	NWR/HQ/Safety/SD/15/23 RB Letter No. 2023/Safety-I/3/8 dated: 01.08.2023	7 days w.e.f. 07.08.23 to 13.08.23
16/2023	Safety Drive regarding Fire Incidences	NWR/HQ/Safety/SD/16/23 RB Letter No. 2023/Safety-I/3/3 dated: 26.08.2023	15 days w.e.f. 27.08.23 to 10.09.23
17/2023	Week long safety drive for the month of Sep.. 23	NWR/HQ/Safety/SD/17/23 RB Letter No. 2023/Safety-I/3/9 dated: 29.08.2023	7 days w.e.f. 11.09.23 to 17.09.23
18/2023	Week long safety drive for the month of Oct.. 23	NWR/HQ/Safety/SD/18/23 RB Letter No. 2023/Safety-I/3/10 dated: 27.09.2023	7 days w.e.f. 09.10.23 to 15.10.23
19/2023	Winter preparedness drive.	NWR/HQ/Safety/SD/19/23 RB Letter No. 2005/Elect(TRS)/440/23 dated: 10.10.2023	15 days w.e.f. 16.10.23 to 31.10.23

20/2023	Intensive safety drive.	NWR/HQ/Safety/SD/20/23 RB Letter No. 2023/Safety(Imp)/3/10/1 dated: 30.10.2023	2 weeks w.e.f. 31.10.23 to 14.11.23
21/2023	Week long safety drive for the month of Nov.. 23(Revised)	NWR/HQ/Safety/SD/21/23 RB Letter No. 2023/Safety-I/3/11 dated: 06.11.2023	7 days w.e.f. 15.11.23 to 21.11.23
22/2023	Week long safety drive for the month of Dec.. 23	NWR/HQ/Safety/SD/22/23 RB Letter No. 2023/Safety-I/3/12 dated: 06.11.2023	7 days w.e.f. 11.12.23 to 17.12.23
01/2024	Week Long Safety Drive for the month of Jan'2024	NWR/HQ/Safety/SD/01/2 RB Letter No. 2024/Safety-I/3/1 dated: 02.01.2024	07 days w.e.f. 08.01.24 to 14.01.24
02/2024	Intensive Safety Drive.	NWR/HQ/Safety/SD/02/24 RB Letter No. 2023/Safety (Imp)/3/10/2 dated: 11.01.2024	15 days w.e.f. 15.01.24 to 29.01.24
03/2024	Week Long Safety Drive for the month of Feb'2024	NWR/HQ/Safety/SD/03/24 RB Letter No. 2024/Safety-1/3/2 dated 07.02.2024	07 days w.e.f 12.02.24 to 18.02.24

Modifications & Other Important works.

1. During 2023-24, training has been arranged to officers, Supervisors & technicians for operation & maintenance of Vande Bharat Train.
2. FIBA pipe line layout was shifted as per RDSO instructions resulting in failures of FIBA related items has reduced from 15 to 5 of NWR trains over NWR. All eligible 633 coaches are covered.
3. To arrest wheel shelling modification in air Brake pipe line and its fittings in LHB coaches are provided in all eligible 540 coaches.
4. Total 1749 warranty cases of valuing Rs 6.02 Cr. were settled during 2023-24.
5. **DPT** – DPT testing of knuckle of 473 coaches were done in division and 15 knuckles were found defective.
6. 32 trains (16 pairs) of Astha special has been run by NWR to AY with linen & OBHS services from 28.01.2024. & 12.03.2024 in short notice.
7. 03 Nos of Vande Bharat train has been operated over NWR, 12977/78 from AII to DEC (Extended to CDG), 12461/62 JU to SBIB & 20979/80 UDZ to JP on 12.04.2023, 07.07.2023 & 23.09.2023 respectively.
8. Total 10 Trains (18 rakes) have been converted from ICF stock to LHB stock during 2023-24.
9. Total 27 Nos. manual type FDSS systems have been upgraded in to automatic type FDSS systems during 2023-24.
10. 334 Nos. AC coaches have been provided with fire and smoke detection system (FSDS) during 2023-24.
11. 2 power cars & 10 pantry cars have been provided with fire detection cum suppression system (FDSS) during 2023-24.
12. Laundry capacity have been augmented by 13.7 TPD in during 2023-24(BKN-2TPD, JU-9.8, BME-1.9 TPD)

OBHS & Linen Services- OBHS service has been provided in 182 trains & Linen services has been provided in all AC coaches.

Infrastructure Development

1. Quick watering systems have been commissioned at CUR in May 2023 and ABR in Jan-24.This will facilitate full watering of all coaches and will help in increasing passenger satisfaction.
2. Under floor wheel Lathe Machine at MD Depot is under commissioning.

3. All weather Rolling in-out huts have been provided at AII, ABR, MJ, UDZ, BNW, SGNR, SOG, BKN, CUR, HSR, JP, RE, BKI, FL, SIKAR, JU, BME, BGKT, JSM, MTD

Sanction of rolling stock over NWR tracks.

1. GM sanctioned obtained for running of 08 type of coaching stocks. (LWSCZDCAA, LWLRRM2, LWFAC2, LWACCN2, LWACCN2, LWFBAC2, LWFCZAC2 & LWSCZAC2.)

2. GM sanction obtained for Running of 02 type of Freight stock. (ACTI- 11t, BCFCM- 22.8t.)

3. Updating of all CRS/GMs sanctions of wagons, coaches, breakdown cranes & SPART on Rolling Stock sanction management (ROSMAS), Indian Railway Portal.

4. Increase the speed of 140T Breakdown cranes (Gottwald A1 and Gottwald A2 design) after obtaining sanction from competent authority.

***

EnHM Performance for GM Narrative Report (2023-24)

Consent to Operate (CTOs):-

1.

09 Good Sheds have been obtained CTOs from SPCB under the Water and Air Act in 2023-24**.** Apart from these 32 Goods Sheds have already been obtained CTOs out of 93 Goods Sheds over NWR. Remaining sheds are under process for obtaining CTOs.
04 Private Sidings have been obtained CTOs from SPCB under the Water and Air Act in 2023-24**.** Apart from this 24 Sidings have already been obtained CTOs out of 32 siding over NWR. Remaining Sidings are under process for obtaining CTOs.
All 33 identified stations have already obtained CTO from SPCBs under water & Air act in compliance of directions issued by Hon'ble NGT.
All workshops and DSL/DEMU sheds have already been obtained CTO from SPCBs under water & Air act.

2

ISO certifications:-

All 04 Workshops and 33 major Railway Stations of NWR have already achieved ISO-14001 (EMS) certification.

Green Rating:-

3

Bikaner Workshop has improved rating from Bronze to Silver during the 203-24 and 14 Establishments/Units have already achieved Green Rating Certification over NWR.
Apart from these, 18 Establishments/Units under process for achieving the certification out of these, 10 at NWR level and 08 units of NWR have been nominated & informed to CME (Plg.)/CR for certification through centralized contract as advised by RB.

Water conservation (Implementation of Indian Railway Water Policy'2017)

4

i **Automatic Coach Washing Plants:-**

ACWP installation is under process at 02 depots (JP & BGKT) and 09 ACWPs have already commissioned at coaching depots over NWR for cleaning/washing of coaches.

ii **ETP/STP/ WRP:-**

01 Effluent Treatment Plant (ETP) at Bikaner Workshop has been installed during the year 2023-24. Apart from these, 25 ETPs, 09 STPs and 06 WRPs have already installed at deferent location over NWR.

iii **Rain Water Harvesting:-**

Rooftop Rain Water Harvesting system have been provided at 08 locations during the year 2023-24.

iv **Water Audits**:-

Water audits have already conducted at major establishments and 33 identified railway stations in compliance of the orders of Hon'ble NGT.

v **Use of water efficient fittings:-**

Taps with aerator and WC with dual flush system installed at DRM office, Div. Rly. Hospital & Rly. Stn./JU. Waterless urinals installed at DRM office, JP & JU at various locations over NWR.

5 Waste Management measures.

i **Composting pits/plants/OWCs:-**

Composting pits/plants/SWMPs/OWCs have already been provided/installed at 33 major Railway Stations over NWR.

ii **Material Recovery Facility (MRF):-**

MRF has been installed at Suratgarh Railway Station in 2023-24 and installation is under progress at 08 stations of Bikaner division. Apart from these MRFs have already been installed at 25 major stations.

iii Memorandum of understanding for disposal of MSW with ULBs (Municipal bodies):

MOUs have been executed with local bodies for disposal of Municipal solid waste (MSW) at 03 Railway Stations i.e. AII, JU & BGKT in 2023-24 and under process at 04 stations. Apart from these MoUs have already been executed at 26 stations over NWR.

6. Environment Related Works (ERWs):-

07 Environment Related Works have been completed during the year 2023-24.
16 works (ERWs) of Rs. 12.55 Cr. have been sanctioned under ERW provisioning in the year 2023-24 and which are under progress at various stages in different field units over NWR.

7 Energy Conservation:

i Solar Power Plant:-

500 kWP rooftop solar power plants has installed at Bikaner Workshop 2023-24. Presently BKNWS have "Net Zero" power consumption.

40 kWp rooftop solar power plants have been installed at Loco Workshop Ajmer in 2023-24.
470.79 kWp Solar Power Plants have been installed at Carriage Workshop, Ajmer during 2023-24.
210 kWp solar power plants, solar power heater, solar street light, solar water pump have already installed at JU-WS.

ii Energy Audits:-

Energy audits conducted at 23 locations of JP division during the year 2023-24. Moreover, energy audits have already conducted at 33 major railway stations in compliance of the orders of Hon'ble NGT.

8 Tree Plantation on Railway land:-

518508 saplings were planted over NWR during the year 2023-24.

9 Other Special efforts in conjunction with Environment Initiatives.

i World Environment day:-

World Environment Day 2023 was observed on the theme "focus on solution to plastic pollution under the campaign Beat Plastic Pollution". On the occasion various activities were organised to create awareness to conserve environment through Nukkad natak, Rallies, paintings, etc

ii Swachhta Pakhwara:-

North Western Railway was observed Swachhta Pakhwara/Swachhta Hi Sewa from 15 Sept to 02 Oct 2023 on the theme 'Garbage free India' to make a cleaner & greener Railway. Railway aim to make garbage free rail through cooperation of responsible citizen that they do not litter the stations and trains and dispose garbage in nominated bins only". Massive Shramdan done at all units over NWR on the occasion of Mahatma Gandhi Jayanti- 2023.

iii Awards:-

Bureau of Energy Efficiency, Government of India, Ministry of Power has awarded "Shunya Plus" label certificate to the Administrative building of Diesel Loco and Wagon Workshop, Ajmer for a period of 03 years on 27.03.2024 as the Electrical energy Generated by the Solar plant installed on the rooftop of this building is more than the Electrical energy consumed.
Clean Government office survey competition was organized by Municipality Bhilwara under cleanliness survey 2024. Municipality Bhilwara awarded cleanliness certificate on 8.3.2024 to Bhilwara railway station for securing 1st Position in cleanliness survey.

***

Chapter-8

ELECTRICAL

1.0 INFRASTRUCTURE

1.1 GENERAL POWER SUPPLY:

S. No.	Assets	2022-23	2023-24
1	Electrified Stations	**578**	**579**
2	Electrified Quarters	**24873**	**24434**
3	Transformers	**299**	**299**
4	Diesel Generating Sets	**148**	**151**
5	Electric Pumps	**982**	**984**
6	Water Coolers	**1164**	**1106**
7	Lifts	**74**	**79**
8	Escalators	**43**	**43**

1.1 TRD :

S. No.	Assets	2022-23	2023-24
1	SPs/SSPs	**203**	**266**
2	TSSs	**35**	**39**
3	Tower Wagon shed	**16**	**24**
4	Tower Wagon	**49**	**57**
5	OHE/PSI Depots	**36**	**46**

2.0 YEARLY PERFORMANCE OF ELECTRICAL DEPARTMENT

A. General Power Services

S. No.	Item	Target for 2023-24	Performance		% Variation (w.r.t. 2022-23)
			2022-23	2023-24	
3	**Loss of punctuality on Electric account (Power Supply)**	0	0	0	0
4	**Energy conservation**				
a	Non-traction Energy consumption of commuted load per year (In million units)	94.761422	99.74	100.732089	0.99
b	**Specific Electric Energy Consumption (In KWH/KW)**	49	57.91	50.46	-12.86

B. TRD & Railway Electrification :

1. The North Western Railway (NWR) has achieved a significant milestone in railway electrification for the second year in a row, securing the top position among all Zonal Railways in IR. During 2023-24, NWR successfully electrified 1127 route kilometers (RKMs), bringing the total electrified BG route network to an impressive 92% (5094 RKMs). This achievement contributes to cleaner and more efficient railway operations across the Indian Railway Network.

2. Total 06 sidings (6.46TKM) have been electrified during the year. Detail of sidings is given below:

   "Birla Cement siding at Kharia Khangar, J. K. Cement siding at Gotan, Military siding at Nokhra yard, Track Machine siding at Nokhra yard, Military & track machine siding at Bap yard and Track Machine siding at Bap yard."

3. Total four TSSs i.e. Merta Road, Pipar Road, Ding & Satrod have been commissioned through open access to purchase power supply at cheaper rates during the year 2023-24.

C. DIESEL LOCOMOTIVE PERFORMANCE

Diesel and Running performance.

1. Average Loco holding of BG was 336.92 in the year 2023-24. (HHP-247 ABR-59.50, BGKT-180.50 & ALCO-ABR-89.92)
2. BG diesel locomotives outage (Coaching + Freight) maintained as 163.06 against the target of 155.80 for the Year 2023-24
3. Ineffective % of HHP & ALCO locomotives was maintained as 4.36% & 9.05% against the target of 5% &10% respectively.
4. Loco failure/ 100 loco/month was achieved 16.82 in Year 2023-24 against 18.93 in last year 2022-23.
5. Direct punctuality loss/ 100 Mail Link/Month on loco account was achieved 11.21 in year 2023-24 against 9.28 in last year 2022-24.
6. Specific fuel consumption of NWR BG Diesel locomotives for passenger and freight service is given below:-

Type	Service	2022-23	2023-24
BG Locomotives	Passenger	3.48	3.44
	Freight	1.82	1.76

7. NWR is first in condemnation disposal of ALCO spares and one of the fastest in condemnation disposal of ALCO locos.
   - Condemnation of ALCO diesel locomotives
   - 12 ALCO condemned locomotives, on age-cum-condition basis (age more than or equal to 30 years) have been sold in FY 2023-24. Out of these 12 locos, 03 were sold to CONCOR in working condition and the remaining 09 were sold as scrap.
   - 16 surplus Alco Locos (Age between 15 to 30 Yrs) have been declared condemned on surplus and under-aged basis by Railway Board on 31.10.2023. These locos have been sold as scrap on 02-02-2024 & 15.02.2024. Out of these, 04 have been delivered and 12 are remaining.
   - Furthermore, 41 Alco Locos (Age between 15 to 30 Yrs) have also been condemned on surplus and under-aged basis by Railway Board on 27.02.2024 and subsequently handed over to stores for their disposal on 28.02.2024. Out of these 13 Locos have been auctioned so far.
8. Disposal of surplus sub assemblies of ALCO locomotives

The details of surplus sub assemblies vetted by finance are as under:-

Shed	Items	Value in Rs.
ABR diesel shed	7	4,79,78,695/-
Ajmer Diesel shop	13	1,39,98,311/-
NWR	20	6,19,77,006/-

Out of them 17 sub assemblies have been sold as scrap value Rs. 5,42,36,439.

9. HHP locomotive sale price/reserve price submitted to RITES for 12281 WDG4 export purpose.
   NWR has declared condemned loco no. 12281 WDG4/BGKT and sent to BLW for gauge modification work for export purpose through RITES.

   Sale price/reserve price of condemned HHP loco no. 12281/WDG4 of BGKT is calculated as Rs. 3,39,49,648.13 (Inclusive of incident charges @ 2% i.e. Rs. 5,91,715/- and departmental charges @ 12.5 % i.e. Rs. 37,72,183.13) and without applicable GST & TCS.

10. Scrap disposal in Diesel sheds during the year is as under:-

Year	Ferrous	Non Ferrous
2022-23	689.934	39.391
2023-24	784.276	44.733

11. ALCO locomotives links have been reduced to 0 from 29 links.
12. Wheel parameters i.e. Root wear, Flange wear, Tread wear, Flange thickness, Flange slope etc. are being measured by Laser Wheel Profile Meter at ABR diesel shed. The least count and accuracy of this Laser Wheel Profile Meter is 1.01 mm & 0.1 mm respectively.
13. So far, total 3271 Running staff (1620 LP, 1499 ALP & 152 CLI) have been trained to operate Electric locomotives against on roll 3677 up to March 2024. 59 Running staff (01 CLI, 44 LP & 14 ALP) are under training.
14. Saving of 8721 KL HSD oil amounting to Rs. 81 Crore has been achieved by shutting down the idle diesel locomotives during the year 2023-24.
15. Total Fuel Management has been implemented and commissioned in RDI/Churu w.e.f.16.3.2024
16. 1433 KL bio diesel blended HSD oil issued during 2023-24 (June-23 to March-23)
17. Mandatory Energy Audit of NWR traction energy was carried out by assigning the Accredit Energy Auditor as per BEE guidelines.

D. Electric Loco Highlights:

(i) Till now, 157 pair Mail/Exp. coaching trains have been switched on electric traction over NWR. (i.e. 60 %Approx.) The switching on Electric traction apart from resulting in substantial saving in energy bill shall also eliminate change of traction.

(ii) Share of Freight GTKM on Electric traction as on March-24 is 26% against about 13% in March-2023.

(iii) GM sanction had obtained for operation of different class of electric locomotives over NWR electrified sections (i.e. WAP1, WAP5, WAP7, WAG5, WAG7, WAG9/9h/9HC, WAG9HH, WAG11 & WAG12B etc. on BG section of NWR. These classes of electric locomotives already running over Indian Railway.



WAG-11



WAG-12B

(iv) NWR having 111 electric loco homing till March-24. Out of 111, 10 locos are homed at ABR Shed. (8-WAP4 & 2-WAG7) & 101 locos are homed at BGKT shed (23-WAP7 & 78-WAG9HC).

(v) In RE-JP-MD-PNU section of NWR, 39 pairs of coaching trains are running at speed of 130 kmph with electric locomotives over NWR.

3.0 SAFETY

3.1 **Rewiring of staff quarters:** 1166 nos. staff quarters have been rewired during the year 2023-24.

3.2 **Checking of earth resistance in staff quarters and service buildings:** During the year 2023-24, the earth resistance of 100% staff quarters and 100% service buildings have been checked for proper continuity and their value are within the limit.

3.3 **Electrical Safety Week:** This Railway observed Electrical Safety Week from **1st May, 2023 to 7th May-2023**. During this week, various activities including power point presentations on safety issues, exhibition and other safety awareness programs, training of staff etc. were organized to inculcate safety consciousness amongst the users.

3.4 **Safety Drives:**

The following safety drives have been launched during the year 2023-24:-

S.N.	Name of Drive	Period	
		From	To
A.	**General Services**		
1	Confirmation on provisioning and working of leakage protection in all electrical installations and assets over station area and service buildings	19.04.23	25.04.23
2	Special Drive for all electrical Installations of General Services for checking of earthing and ELCB/RCCB/RCBO in regard to availability and proper functioning	27.06.23	06.07.23
3	Pre-Monsoon Special Drive	10.06.23	24.06.23
4.	Special Drive for Checking Solar-Water Heater and Geyser	24.11.23	05.12.23
5.	Pre-Summer Drive for checking of Pumps, Water Coolers, Air-conditioner etc. in regards proper functioning	25.02.24	11.03.24
B.	**TRD**		
1	TRD Installations – Pre-Summer drive	01.04.23	30.04.23
2	Pre-Monsoon drive to improve punctuality performance.	19.05.23	20.06.23
3	10 days safety drive to check soundness of earthing system	26.06.23	05.07.23

4	Week long safety drive for regulating equipments of OHE	10.07.23	16.07.23
5	15 days Special Drive for making Railway men as well as public, aware and to take all precautions against high voltage overhead wire in newly electrified sections	07.08.23	21.08.23
6	15 days special drive for Cyber Security of SCADA	15.09.23	29.09.23
7	Winter drive to improve punctuality performance.	09.10.23	20.11.23
8	Winter drive to improve OHE punctuality performance.	23.10.23	16.11.23
9	TRD Installations – Pre-Summer drives	20.03.24	31.03.24

4.0 Passenger Amenities

4.1 **Lifts:** 2 nos. at Ajmer- station and 01 no. at SGNR station, have been commissioned during 2023-24.

4.2 **Escalators:** NIL escalators have been commissioned during 2023-24.

5.0 System Improvements:

5.1 During the year 2023-24, Electrification of 1127 RKM/1528 TKM has been done over NWR.

5.2 1166 nos. Railway Quarters rewired over NWR during 2023-24.

6.0 Highlight –

6.1 **LED Light:** 100 % LED type luminaries done during 2023-24.

6.3 **Energy Audit: Investment grade Energy Audits** of **69** locations over NWR have been conducted during 2023-24.

6.4 **Occupancy Sensors: 201 nos. Occupancy sensors** installed during 2023-24.

6.5 **Automation/IOT based devices**: **168 nos**. Automation/IOT based online monitoring & control of electrical equipment/assets over NWR have been installed during 2023-24.

6.6 **Power Factor Rebate:** The Power Factor **Rebate of Rs. 109.81276 Lac** has been obtained from Discoms on electricity bills during the year 2023-24 for maintaining PF above 0.96.

6.7 **Airport standard illumination station**: 07 nos. stations with airport standard illumination having footfall more than 2000 have been completed during 2023-24.

6.8 **Net Zero Energy building/stations: 07 nos. Net Zero Energy building/stations have been completed** during 2023-24.

6.9 **BLDC Fans: 4703 nos**. **conventional fans** have been replaced by **BLDC fans** over NWR during 2023-24

6.10 **Energy Conservation Week:-** Energy Conservation Week was observed from 11th to 17th December, 2023 over NWR, seminars / workshops / Technical presentations, slogan, essay and drawing & painting competitions and display of banners and posters on Energy Conservation were organized.

6.11 **BEE 5 Star rated equipment's** : 4195 nos. **BEE 5 Star rated equipment's** installed during 2023-24.

6.12 During 2023-24, **4** TSSs of NWR have been commissioned.

6.13 **Non conventional Energy sources:-**

- **A. 28 No. Solar Geysers** has been installed in Rest-House/Lobbies/Retiring –rooms/Hospitals/Running-Rooms/Canteens/Base-Kitchen during 2023-24.
- **B. 146 No. Solar Street Light has been** provided during 2023-24.
- **C. 14 No. Solar Water Cooler has been** provided during 2023-24.
- **D. 2240 kWp solar power plant has been** installed over NWR during 2023-24**.**

7.0 Works Progress: 2023-24

A. CAPEX utilization 104.85% of RBG (Expenditure- 77.21 Cr. vise RBG -73.63 cr.)

B. Works completed and deleted from IRPSM – 18 Nos.

C. Works sanctioned – 50 nos. (Rs. 173 Cr.)

<<<>>>

CHAPTER – 9

SIGNAL & TELECOMMUNICATION

Statistical information pertaining to Signal & Telecommunication Department as on 31.03.2024 is furnished below:

1. SIGNALLING:

9.1.1 Signalling Standard

The distribution of interlocked stations and those provided with rudimentary interlocking on this railway is as follows:-

Gauge	Standard – II ®		Standard – I ®	
	31.03.23	31.03.24	31.03.23	31.03.24
BG	422	432	19	16
MG	-	-	-	-
Total	422	432	19	16

Gauge	Rudimentary (Modified Non-Interlocking)		Grand Total	
	31.03.23	31.03.24	31.03.23	31.03.24
BG	-	-	441	448
MG	3	3	3	3
Total	3	3	444	451

9.1.2 Method of Block Working :

Different types of systems of Working & Block in different section on this railway are as mentioned below:-

Sr. No	Type of Working	BG		MG		Total	
		31.03.23	31.03.24	31.03.23	31.03.24	31.03.23	31.03.24
1	Absolute Block System						
1.1	Single line Token Instrument (Section)	0	0	5	5	5	5
1.2	Single line token-less instrument(Section) TLBI/DIADO	48	17	0	0	48	17
1.3	UFSBI/SSBPAC	295	328	0	0	295	328
1.4	BPAC (UAC-Analog)	0	0	0	0	0	0
1.5	Double Line Block Instrument (Section)	111	109	0	0	111	109
1.6	a) Continuous Track Circuit (Section)	12	11	0	0	12	11
1	Automatic Signalling	01	08	0	0	01	08
2	One Train Only system	5	5	0	0	5	5

9.1.3 Signalling details for 2023-24

(i) Two Aspect Semaphore Signalling (Total no. of stations):

Route	Double line	Single line	Multiple line	Total
B - Route	0	0	0	0
D - Route	0	0	0	0
MG	0	3	0	3
Total	0	3	0	3

(ii) Multiple Aspect Signalling:

(a) Multiple Aspect Colour Light Signalling (Total no. of stations):

Route	Double line	Single line	Multiple line	Total
B - Route	86	10	0	96
D - Route	35	317	0	352
Total	121	327	0	448

(iii) Power Signalling (Total no. of stations):

(a) Total RRI/PI/EI

Route	Double line	Single line	Multiple line	Total
B - Route	86	10	0	96
D - Route	35	316	0	351
Total	121	326	0	**447**

(b) Route Relay interlocking

Route	Double line	Single line	Multiple line	Total
B - Route	1	0	0	1
D - Route	0	7	0	7
Total	1	7	0	**8**

(c) Panel Interlocking

Route	Double line	Single line	Multiple line	Total
B - Route	19	10	0	29
D - Route	0	149	0	149
Total	19	159	0	**178**

(d) Electronic Interlocking

Route	Double line	Single line	Multiple line	Total
B - Route	66	0	0	66
D - Route	35	160	0	195
Total	101	160	0	**261**

9.1.4 Track Circuits

Area / Location	Double line	Single line	Multiple line	Total
FM to FM	121	327	0	448
FM to BSL (straight)	121	327	0	448
FM to BSL (Turn Out)	121	327	0	448
FM to Home (straight)	121	327	0	448
FM to Home (Turn out)	121	327	0	448
Loop Line	121	327	0	448

9.1.5 Classification of stations:-

Gauge	SPL Class		A Class		B Class		C Class	
	Double line	Single Line	Double line	Single Line	Double line	Single Line	Double line	Single Line
BG	2	1	0	0	119	326	17	0
MG	0	0	0	0	0	3	0	0

9.1.6 Level Crossing Gates

	Description	31.03.23	31.03.24
A)	No. of manned gates provided with telephone	939	928
B)	No. of gates provided with interlocking	555	557

9.1.7 Provision of safety device (As on 31.03.2024):

Safety device provided	Route	Spl Class		A Class		B Class		C Class		Total	
		WSL	OSL	WSL	OSL	WSL	OSL	WSL	OSL	WSL	OSL
(A) Lifting Barrier	Trunk	0	0	0	0	0	0	0	0	0	0
(B) Telephone		0	0	0	0	0	0	0	0	0	0
(C) Warning Bell		0	0	0	0	0	0	0	0	0	0
(A) Lifting Barrier	Other	49	73	11	24	25	29	234	112	319	238
(B) Telephone		49	73	11	24	25	29	234	598	330	598
(C) Gate Warning Bell		49	73	11	24	25	29	234	112	319	238

2. MAJOR ACHIEVEMENTS

NWR : Performance at a glance (2023-24)

A Major Achievements

SN	Work	Targets of Railway for 2022-23	Cumulative progress till the end of Mar'23	% Achievements(During 2022-23)	Targets of Railway for 2023-24	Cumulative progress till the end of Mar'24	% Achievements (2023-24)
1	Provision of PI/EI/RRI	26	22	85%	18	17	95%
2	Std.I to II (R) (No. of stn)	4	4	100%	4	3	75%
3	Track Circuit (Location)	-	-	-	-	-	
4	BPAC (No. of B/section)	18	18	100%	11	13	118%
5	Automatic signaling (RKM)	-	-	-	50	56.57	113%
6	IBS (Nos.)	1	1	100%	-	-	-
7	Elimination of Token Instruments (No. of stations)	6	6	100%	-	-	-

8	Elimination of Mech Signalling (No. of stns.)	4	4	100%	4	3	75%
9	LC Gate Interlocking (No. of Gate)	27	50	185%	12	14	116%
10	Laying of Quad Cable (Km)	38	88	232%	157	12	7.6%
11	Laying of OFC (Km)	38	38	100%	52	93	178%

B. <u>Key Highlights / Achievements during 2023-24</u>:-

1	□□□□□□□□□□, □□□□□□, □□□□□ , □□□□, गोविंदी □□□□□□, □□□□, □□□□□□□□, □□□□□, □□□□□ □□□□, □□□ □□□□□□□, □□□□□□□, □□□□□□□□ □□□□□□ □□□□□, □□□□□□, □□□□□□□□, □□□□□□□, □□□□□□□ □□□ □□□□□ □□□□□□ □□ □□□□□□ □□□□□□□□□ □□□□□□□ □□□□□□□□□□□□ □□□□□□□□□□ (□□□) □□□□□□□ □□□□□ □□□ □□□ □□□□□ **2023-24** □□ □□□□□ □□□□□□ □□□ □□ **17** □□□□□□□□ □□ □□□□□□□□□□□□□ □□□□□□□□□□ □□□□□ □□□□□ □□□ □
2	□□□□□ -□□□□□□ □□□ □□□□□□□□ – □□□□□ □□□□□□□ block □□□□□□ □□□ □□□□□□□□ □□□□□□□□□□□ □□□□□□ □□□□□ □□□□ □□□ □□ (Commissioned)□ □□□□ □□□□ □□□□ □□ □□ block □□□□□□ □□ □□□ □□□ □□ □□□□ □□ □□□ □□ □□□□□□ □□□□□□ □□□□ □□ □□□ □□ □□□□□ □□□□ □□□ □□□□□□ □□□□□ □□□□ □□ □□□□□ □□□□□□ □□□ □□ 24-202356.57 □□□□□□□□ □□□ □□ □□□□□□□□ □□□□□□□□□□□ □□ □□□□ □□□□ □□□□
3	□□□□□□□ □□□□□ □□ □□□□ □□□ 14 □□□□□□□ □□□□ □□□□□ □□□□□□ □□ □□□□□□□ □□ □□□□ □□□ □□ I 23 □□□□□□ □□ □□□□□□□□□□ □□□□□□□□ □□□□□□ □□□ 24 □□□□□□□□□□ □□□□□□ □□□ □□□□□ □□□
4	□□□□□□□□, □□□□□□, □□□□□□□□, □□□□□□ □□□□□, □□□□□□ □□□□□ □□ □□□□□ □□□□ □□□ □□□□□□ □□□□ □□□□□ □□□□□□ □□ □□□□□□□□ □□□□□ □□□□□□ □□□□□□ □□□□□ □□□□□□ □□□□□□ □□□□ □□□□ □□□ □□□ □□ I □□□□ □□□□□ □□□□□□ □□ □□□□□□ □□□□□ □□□□□□ □□□□□□ □□□□□ □□□□□□ □□□□□□ □□ □□□ □□ □□□□□□ □□□ □□□□□ □□□□□□ □□ □□□□□ □□□□□□ □□□ □□ □□□□□□□ □□□□□□□□ □□□ □□□□□ □□□□ □□□/
5	5 □□□□□□□□ □□ □□□□□□□□□ □□ □□□□□ □□ □□□□□□ □□□ □□ □□□□□□□□ □□□□□□□ □□ □□□ □□ □□□□□□□, □□□□□□, □□□□□, □□□□ □□□ □□□□□ □□□□□□□□ □□ □□□□□□ □□□ □□□□□□□□□□ □□□□□ □□□□□□□ □□□□ □□ □□, 78 □□□□□□□□ □□ □□□□□□□□□ □□□□□ □□□□□□ □□ □□ □□ I 03 □□□□□□□□ □□□□□□□ □□□□□□□ □□□ □□□ □□□□□□, □□ □□□□□ □□□□□□□□ □□□□□ □□□□□□□ □□□□ □□ □□ I 122 □□□□□□□□ □□ □□□□□□ □□□□□□ □□□□□□ □□□□□□ □□□□□□ □□□□ □□ □□□ I 6 □□□□□□□□ □□ 25 W- □□ □□ □□ □□□ □□□□□ □□□
6	□□□ □□□□□□□□ □□□□□□□□□ □□ □□□□□□□ □□ □□□□□□ □□□□□□ □□□ □□ □□ □□□□□ □□□□□□ □□ □□□□□□□□ □□□ □□ □□ □ □□□ □□ □□□□□ □□ □□□□ □□ □
7	□□□□□□, □□□□, □□□□ □□□ □□□□□ □□□□□□ □□ □□□□□□□□ □□□ □□□□ □□ □□□□□ □□□□ □□ □□□□ □□□□

8	[illegible] 03.04.2023 [illegible] 07.08.2023 [illegible]
9	[illegible] 45669 16696 3.2 43000/- 6.9 [illegible]
10	[illegible]
11	[illegible] 11 [illegible]
12	102 [illegible] SMS [illegible]
13	[illegible] 2023-24 [illegible] 39 [illegible]
14	[illegible] 2023-24 [illegible] 105 [illegible]
15	93 RKM [illegible] OFC [illegible] 12 RKM [illegible] quad [illegible]
16	26 [illegible]

17	[illegible] 24 [illegible] 26.02.2024 [illegible] ( ) [illegible] 101 [illegible] 12.03.2024 [illegible] 38 [illegible] I [illegible]

a. **Staff Position (As on 31.03.24)**

a.	**Details of Signal & Telecommunication**	**Sanctioned**	**Operated**
i)	Supervisory staff in Group 'C'	320	290
ii)	Technical Maintainer in Group 'C'	1210	1023
iii)	Khallasi & other staff in Group 'D'	849	654
b.	**Other categories**	**100**	**85**

b. Details of Gazetted Cadre (As on 31.03.2024)

Grade	**CSTE/Open Line**				**Construction**				**Other Dept.**	
	Revenue		**WC**		**Revenue**		**WC**		**Revenue**	
	Sanc.	**Optd.**	**Sanc.**	**Optd.**	**Sanc.**	**Optd.**	**Sanc.**	**Optd.**	**Sanc.**	**Optd.**
□□.□.□□.	**2**	**2**	**0**	**0**	**0**	**0**	**0**	**0**	**0**	
□□.□.□□.	**4**	**5**	**0**	**0**	**1**	**1**	**0**	**0**	**3**	**CVO ADRM/JP CPM/GSU/All**
□□.□□./ □□.□. □□.	**10**	**10**	**0**	**0**	**2**	**3**	**2**	**2**	**5**	**Sr.DSO/BKN Dy.CSO/S&T Dy.CSTE/GSU/All Dy.CSTE/GSU/BKN Dy.CSTE/GSU/JP Dy.CSTE/GSU/JU**
□□.□□.	**9***	**10**	**0**	**0**	**1**	**0**	**6**	**5**	**0**	**0**
□□.□□.	**17**	**16**	**0**	**0**	**3**	**0**	**6**	**5**	**1**	**ASTE/Training /ZRTI**
□□□	**42**	**43**	**0**	**0**	**7**	**4**	**14**	**12**	**9**	**10**

i) *One vacant post SS revenue (PC:10RE6P010) transfer from CORE to NWR for two financial Year 2022-23, 2023-24

ii) 02 Sr. scale post of construction are being utlised by Operating dept. as DOM/C/HQ & DOM/G/BKN

iii) 01 Jr scale post of ASTE/Proj./All utlised as AEN/Proj/JP under Dy CSTE/Proj./JP

c. Total no. of staff recruited through Railway Recruitment Board during 2023-24

S. No	Category of staff	No. of Staff Panel recd. from RRB	No. of Staff reported duty	Remarks
1	Appr. SSE/Sig.	-	-	-
2	Appr. SSE/Tele	-	-	-
3	Appr. SSE/Drg.	-	-	-
4	Appr. JE/Sig.	12	07	Employee Notice 1/2018-19
5	Appr. JE/Tele	10	06	Employee Notice 1/2018-19
6	Appr. JE/Drg.	-	-	
7	Appr. SM-III	43	05	Employee Notice 1/2018-19
8	Appr. TCM-III	15	03	Employee Notice 1/2018-19
9	Appr. SM-II	-	-	

d. Total no. of posts created during 2023-24 (for Division):

Group C – Nil

Group D –NIL

e. DISTUs for the year 2023-24 (Division-wise):

S. No.	Division	DESU	DETU	DISTU
1	**Ajmer**	279431	202598	482029
2	**Bikaner**	577683	138202	715885
3	**Jaipur**	303090.66	204982.72	508073.38
4	**Jodhpur**	258786	172889	431675
	Total	1418990.66	718671.72	2137662.38
	ZISTU	2137662.38		

a. Signalling Works:

Works executed during 2023-24 are as under :-

S. No.	Division	No. of Station / Section	Name of Station / Section
9.5.1(a)	**Route Relay Interlocking**		
1	Ajmer	NIL	
2	Bikaner	NIL	
3	Jaipur	Nil	
4	Jodhpur	NIL	
	Total	NIL	
9.5.1(b)	**Panel Interlocking**		
1	Ajmer	NIL	
2	Bikaner	NIL	
3	Jaipur	NIL	
4	Jodhpur	NIL	
	Total	**NIL**	
9.5.1(c)	**Solid State Interlocking**		
1	Ajmer	1	□□□□
2	Bikaner	3	□□□□□□, □□□□, □□□□□
3	Jaipur	6	□□□□□□□ , □□□□□□□□ □□□□□□ □□□□□ , □□□□□□, □□□□□□□□, □□□□□□□, □□□□□□□
4	Jodhpur	7	□□□□□□□□□□, □□□□□ , □□□□□□□ □□□□□□, □□□□, □□□□□□□□, □□□□□ □□□□ , □□□ □□□□□□□,
	Total	**17**	

9.5.1(d)	**Data Logger Equipment**		
1	Ajmer	1	□□□□
2	Bikaner	3	□□□□□□, □□□□, □□□□□
3	Jaipur	6	□□□□□□□ , □□□□□□□□ □□□□□□ □□□□□ , □□□□□□, □□□□□□□□, □□□□□□□, □□□□□□□
4	Jodhpur	7	□□□□□□□□□□, □□□□□ , □□□□□□□ □□□□□□, □□□□, □□□□□□□□, □□□□□ u□□□□, □□□ □□□m□□,
	Total	**17**	
9.5.1(e)	**IPS System**		
1	Ajmer	1	□□□□
2	Bikaner	3	u□□□□□□, □□□□, □□□□□
3	Jaipur	6	□□□□□□□, □□□□□□□□ □□□□□□ □□□□□ , □□□□□□, □□□□□□□□, □□□□□□□, □□□□□□□
4	Jodhpur	7	□□□□□□□□□□, □□□□□ , □□□□□□□ □□□□□□, □□□□, □□□□□□□□, □□□□□ □□□□, □□□ □□□m□□,
	Total	**17**	
9.5.1(f)	**BPAC**		
1	Ajmer		
2	Bikaner	4	Jhunpa-Siwani, Siwani-Charaud,Charaud-Hisar, Suratpura-Jhunpa
3	Jaipur	7	Baniyana,Baniyana-Salempura Arniya Khurd, Salempura Arniya Khurd-Lalsot, Lalsot- Mandawari, Mandawari-Bamanwas, Bamanwas-Khuntala, Khuntala-Gangapur City.
4	Jodhpur	2	Jenal-Odhava, Odhava- Bhildi
	Total	**13**	
9.5.2	**Yard Remodelling**		
1	Ajmer	3	MarwarJn, Udaipur, Bhimal,

2	Bikaner	10	Satroad,Lahli, Hansi, Manheru, Suratgarh, Shiwani Sudsar,Ellenabad,Tahsil Bhadra,Kalanwali
3	Jaipur	5	Gehlota, Bawal, Jhunjhunu, Siras Phulera
4	Jodhpur	12	Raniwara, Nokha, Nagaur, Balotra, Barmer,Sonu, Bhimarlai, Govindi Marwar, Gudha, Sambhar Lake, Nanwa City, Naya Khardiya
	Total	30	

Status of Track Circuiting:

S. No.	Division	Total No. of Station / Section	Name of Station / Section
9.5.3(a)	**FM – FM**		
1	Ajmer	90	MDJN-PNU-44, AII-COR-UDZ-32, NDT, BI, UDZ-HMT-12
2	Bikaner	132	BKN-RTGH-SDLP-19, RE-SDLP-HSR-18, RE-HSR-15, HSR-BTI-11, BKN-SOG-BTI-29, KLYT-PLC-8, SRPR-SGNR-7, SOG-SRPR-APH-6, BNW-ROK-4, HMH-SGNR-3, HMO-SURP-12
3	Jaipur	105	RE-BKI-JP-MD-41,JP-SWM-10,RE-RGS-FL-25, SIKR-LHU-7, Sikar,Laxmangarh Sikar, Ramgarh Shekhawati, Bisau, Churu, Palsana, Goriyan, Chota gudha JP-RGS-7, Dausa-Gangapur-6
4	Jodhpur	121	FL-JU-MJ-36, LN-MBF-20, SMR-BLDI-23, DNA-RTGH-7, RKB-JSM-22, MTD-BKN-12, PLCC,
	Total	**448**	
9.5.3(b)	**FM - BSL (Straight)**		
1	Ajmer	90	MDJN-PNU-44, AII-COR-UDZ-32, NDT, BI, UDZ-HMT-12
2	Bikaner	132	BKN-RTGH-SDLP-19, RE-SDLP-HSR-18, RE-HSR-15, HSR-BTI-11, BKN-SOG-BTI-29, KLYT-PLC-8, SRPR-SGNR-7, SOG-SRPR-APH-6, BNW-ROK-4, HMH-SGNR-3, HMO-SURP-12
3	Jaipur	105	RE-BKI-JP-MD-41,JP-SWM-10,RE-RGS-FL-25, SIKR-LHU-7, Sikar,Laxmangarh Sikar, Ramgarh Shekhawati, Bisau, Churu, Palsana, Goriyan, Chota gudha JP-RGS-7, Dausa-Gangapur-

			6
4	Jodhpur	121	FL-JU-MJ-36, LN-MBF-20, SMR-BLDI-23, DNA-RTGH-7, RKB-JSM-22, MTD-BKN-12, PLCC,
	Total	**448**	
9.5.3(c)	**FM – BSL (Turn Out)**		
1	Ajmer	90	MDJN-PNU-44, AII-COR-UDZ-32, NDT, BI, UDZ-HMT-12
2	Bikaner	132	BKN-RTGH-SDLP-19, RE-SDLP-HSR-18, RE-HSR-15, HSR-BTI-11, BKN-SOG-BTI-29, KLYT-PLC-8, SRPR-SGNR-7, SOG-SRPR-APH-6, BNW-ROK-4, HMH-SGNR-3, HMO-SURP-12
3	Jaipur	105	RE-BKI-JP-MD-41,JP-SWM-10,RE-RGS-FL-25, SIKR-LHU-7, Sikar,Laxmangarh Sikar, Ramgarh Shekhawati, Bisau, Churu, Palsana, Goriyan, Chota gudha JP-RGS-7, Dausa-Gangapur-6
4	Jodhpur	121	FL-JU-MJ-36, LN-MBF-20, SMR-BLDI-23, DNA-RTGH-7, RKB-JSM-22, MTD-BKN-12, PLCC,
	Total	**448**	
9.5.3(d)	**Home – FM (Straight)**		
1	Ajmer	90	MDJN-PNU-44, AII-COR-UDZ-32, NDT, BI, UDZ-HMT-12
2	Bikaner	132	BKN-RTGH-SDLP-19, RE-SDLP-HSR-18, RE-HSR-15, HSR-BTI-11, BKN-SOG-BTI-29, KLYT-PLC-8, SRPR-SGNR-7, SOG-SRPR-APH-6, BNW-ROK-4, HMH-SGNR-3, HMO-SURP-12
3	Jaipur	105	RE-BKI-JP-MD-41,JP-SWM-10,RE-RGS-FL-25, SIKR-LHU-7, Sikar,Laxmangarh Sikar, Ramgarh Shekhawati, Bisau, Churu, Palsana, Goriyan, Chota gudha JP-RGS-7, Dausa-Gangapur-6
4	Jodhpur	121	FL-JU-MJ-36, LN-MBF-20, SMR-BLDI-23, DNA-RTGH-7, RKB-JSM-22, MTD-BKN-12, PLCC,
	Total	**448**	
9.5.3(e)	**Home – FM (Turn Out)**		
1	Ajmer	90	MDJN-PNU-44, AII-COR-UDZ-32, NDT, BI, UDZ-HMT-12
2	Bikaner	132	BKN-RTGH-SDLP-19, RE-SDLP-HSR-18, RE-HSR-15, HSR-BTI-11, BKN-SOG-BTI-29, KLYT-PLC-8, SRPR-SGNR-7, SOG-SRPR-APH-6, BNW-ROK-4, HMH-SGNR-3, HMO-

			SURP-12
3	Jaipur	105	RE-BKI-JP-MD-41,JP-SWM-10,RE-RGS-FL-25, SIKR-LHU-7, Sikar,Laxmangarh Sikar, Ramgarh Shekhawati, Bisau, Churu, Palsana, Goriyan, Chota gudha JP-RGS-7, Dausa-Gangapur-6
4	Jodhpur	121	FL-JU-MJ-36, LN-MBF-20, SMR-BLDI-23, DNA-RTGH-7, RKB-JSM-22, MTD-BKN-12, PLCC,
	Total	**448**	
9.5.3(f)	**Loop Line**		
1	Ajmer	90	MDJN-PNU-44, AII-COR-UDZ-32, NDT, BI, UDZ-HMT-12
2	Bikaner	132	BKN-RTGH-SDLP-19, RE-SDLP-HSR-18, RE-HSR-15, HSR-BTI-11, BKN-SOG-BTI-29, KLYT-PLC-8, SRPR-SGNR-7, SOG-SRPR-APH-6, BNW-ROK-4, HMH-SGNR-3, HMO-SURP-12
3	Jaipur	105	RE-BKI-JP-MD-41,JP-SWM-10,RE-RGS-FL-25, SIKR-LHU-7, Sikar,Laxmangarh Sikar, Ramgarh Shekhawati, Bisau, Churu, Palsana, Goriyan, Chota gudha JP-RGS-7, Dausa-Gangapur-6
4	Jodhpur	121	FL-JU-MJ-36, LN-MBF-20, SMR-BLDI-23, DNA-RTGH-7, RKB-JSM-22, MTD-BKN-12, PLCC,
	Total	**448**	
9.5.4	**Status of Interlocking of LC Gates**		
	Div	**Total**	**Achievement during the year**
1	Ajmer	49	
2	Bikaner	186	**LC-36, 18, 67A, 16, 139, 134, 125,32**
3	Jaipur	145	**LC-134**
4	Jodhpur	177	**LC-152, 39, 2, 237,52**
	Total	**557**	**14 Nos**
9.5.5	**Status of Gate Telephones**		
1	Ajmer	88	
2	Bikaner	295	

3	Jaipur	215	
4	Jodhpur	330	
	Total	**928**	

b. **Summary of signaling works completed during the year 2023-24 with corresponding figures for the year 2022-23**

Signalling Works:

S. No.	**Type of Work**	**No. of works completed during the year**	
		2022-23	**2023-24**
1	Raising of standard of interlocking (Stns)	04	03
2	Provision of Tokenless Block Instruments- B/sec	-9	-31
3	Elimination of Token Instruments -B/sec	06	0
4	Provision of Double line lock and Block Instruments-B/sec	06	05
5	Provision of Track Circuiting / Axle Counter in Block section for track clearance (no. of sections) directional working	-	-
(A)	Double line with track circuiting / Axle counter	06	05
(B)	Single line with track circuiting / Axle counter	42 Locations	48 Locations
6	Provision of Block hut	-	-
7	Provision of track circuiting	-	-
(i)	FM to FM	04	07
(ii)	FM to BSL (Straight)	07	07
(iii)	FM to BSL (Turn out)	08	10

(iv)	Home to FM (Straight)	07	07
(v)	Home to FM (Turn out)	08	10
(vi)	Loop line	08	10

ii. **Signalling Works: Position of the line capacity works**

S. No.	**Type of Work**	**No. of works completed during the year**	
		2022-23	**2023-24**
1	Provision of New X-ing stations including block hut	04	01
2	Construction of new lines (length / number of stations opened)	-	06
3	Conversion of Single to Double line	06	05
4	Remodeling of yard	01	39
5	Provision of additional loop	02	04
6	Provision of power signaling	22	17
(A)	Panel interlocking/Electronic Interlocking	22	17
(B)	Route Relay interlocking	0	0

TELECOM

a. Telecom Achievement for the year 2023-24

SN.	Assets	Unit	As on 31.03.2023	Added during 2023-24	As on 31.03.2024	Remarks
1	**Telephone Exchanges**					
a)	**Main Exchanges**					
i)	Electronic	Nos.	40	0	40	
		Lines	13986	0	13986	
b)	**Intercom Exchanges**					
i)	Electronic	Nos.	11		11	
		Lines	802		802	
2	**Telegraph/ Teleprinter sections:-**	**NIL**				
3	**Microwave Links (7GHz):-**	**NIL**				
4	**UHF Links:-**	**NIL**				
5	**Overhead Alignment**					
i)	Rly. Owned	Rkm	0	0	0	
ii)	BSNL Rented	Rkm	0	0	0	Surrendered.
6	**Telecommunication Cables**					
a)	**Rly. Owned**	Unit				
i)	OFC only	Rkm	105	0	105	
ii)	OFC + 4/6 Quad cable	Rkm	5316	94	5410	DO-GGN section
iii)	4/6 Quad cable only	Rkm	97	-81	16	Remaining Only in MVJ-NDT section.
iv)	RE Quad cable	Rkm	0		0	
b)	**BSNL Rented**					
i)	RE Quad cable	Rkm	0		0	

7	**18 GHz Links**	**Rkm**	0		0	
8	**Train Control Systems**					
a)	**Total Controlled Sections**	**Nos.**	19		19	
b)	**Controlled Sections fitted with:**					
i)	DTMF Equipments	Nos.	18		18	
ii)	Solid State Equipment	Nos.	1		1	
iii)	Other type of way station Equipment	Nos.	0		0	
c)	**Total controlled stations**	**Stns**	439	6	445	
d)	**Controlled stations fitted with:**					
i)	DTMF Equipments	Stns.	430	6	436	
ii)	Solid State Equipment	Stns.	9		9	
iii)	Other type of way station Equipment	Stns.	0		0	
e)	**Total Non-controlled Sections**	**Nos.**	3	0	3	PPR- Bilara, MTD-MEC & MKN-PBC
f)	**Total Non-controlled Stations**	**Stns.**	3	0	3	Bilara, Merta City, Parbatsar
9	**Passenger Amenities**					
a)	**Stations fitted with:**	Unit				
i)	Conventional Public Address System	Stns.	270	78	348	
ii)	Auto Announcement System	Stns.	86	0	86	
iii)	Coach Guidance System	Stns.	51	5	56	Bijainagar, Narnaul, Phalodi Jn, Sikar(PF-1,2,3) & Jalore

						(PF-1)
iv)	Electronic Train Display Board	Stns.	53	3	56	Bijainagar, Narnaul Raisinghnagar,
v)	NTES information display system	Stns.	50	0	50	
vi)	High speed Wi-Fi	Stns.	419	0	419	
vii)	Closed circuit TV	Stns.	34	1	35	STNL
10	**Mobile Train Radio Communication**	**Rkm**	**0**		**0**	
11	**VHF communication provided for**					
a)	**Driver – Guard Communication**					
i)	5 watt VHF sets	Nos.	3542	251	3793	
ii)	25 watt VHF sets	Nos.	525	6	531	Including 6 new sets in DO-GGN section
b)	**Other applications**					
i)	5 watt VHF sets	Nos.	2075	25	2100	
ii)	25 watt VHF sets	Nos.	222		222	
12	**Satellite Telephone**					**Annexure – A**
		Nos.	10		10	
13	**Railnet Connectivity**					
i)	LAN connections	Nos.	3038	55	3093	
ii)	DSLAM connections	Nos.	1631	0	1631	
	Other Achievements	Unit				
A.	**PRS**	Locations	48	-5	43	
B.	**UTS cum PRS**	Locations	275	39	314	

C.	**UTS**	Locations	310	0	310	
D.	**CMS**	Locations	27	0	27	
E.	**TMS**	Locations	51	0	51	
F.	**ICMS**	Locations	22	0	22	
G.	**V-SAT for FOIS**	Locations	5	0	5	
H.	**Saving due to transfer of Circuits from BSNL to Rly. Media**	Lakhs of Rs.	512.83	7.27	520.1	

Annexure – A

9.7.12 Telephone numbers for Disaster Management

Div / Zonal Hq.	**Accident Information Telephone No.**	**ISD Phone No.**	**Satellite Telephone**		**Emergency Control Office phone No.**	
			Location	**Number**	**Rly**	**BSNL**
Ajmer	0145-1072	0145-2421048	ART- Abu Road	8991112827	096-44610	0145-2421048
			Test Room	8991112828		0145-2428652
Bikaner	0151-1072	0151-2200120	ART- Lalgarh	8991112829	097-44608, 44612, 44613	0151-2200120
			Test Room	8991112830		
Jaipur	0141-1072	0141-2202369	ART- Jaipur	8991112833	095-44610	0141-2202369
			Test Room	8991112834		0141-2200878
Jodhpur	0291-1072	0291-2431453	ART- Jodhpur	8991112831	098-44610	0291-2431453
			Test Room	8991112832		
NWR/HQ	-	0141-2725805	HQ Exchange	8991112825	095-25680, 25681	0141-2725805
				8991112826		0141-2725806

****

Chapter-10

STORES DEPARTMENT

.1 Materials Management Department is responsible for ensuring timely availability of right quality of materials required for operation maintenance and POH/IOH activities of rolling stock apart from materials required for the construction organization. There are three major stores depots attached to workshops at Ajmer, Jodhpur & Bikaner and three Diesel depots i.e. Ajmer, ABU Road, BGKT-Jodhpur and also Three carriage & wagon depot i.e. WSD/AII, CSD/AII,WSD/FL Apart from these there are four divisional depots at JP,JU,AII & BKN division. General Stores depot at Ajmer & Jodhpur caters to the material needs of workshops & divisions. Materials Management Department also caters the need of Stationery, Tickets, Uniform & general purpose items required for day to day use.

2. Zonal Materials Management Department of NWR is located at Jaipur, and headed by PCMM and assisted by 4 CMMs, 6 Dy.CMMs (05 posted at HQ & 01 posted at CH/JP) and 03 SS and 02 JS officers. Presently, there are 81 class III and 09 class IV staff posted in the HQ office.

3. The field organization comprises of three district stores depots headed by Dy.CMMs i.e. Ajmer, Jodhpur & SMM at BKN. Ajmer district has eight depots (GS, C&W, LSD, DSL , DL-ABR, WSD/FL ,DSD/AII & Divisional depot at JP) Jodhpur district has three depots (JU, BGKT and Divisional depot JU) & BKN district has two depots (BKN depot & Divisional depot BKN.)

3. The divisional stores are headed by Sr.DMMs and assisted by ADMMs and they have mainly been entrusted with the full responsibility of meeting with NS demands of divisional indenters up to Rs.10 Cr, collection & distribution of Imprest items from stores depots to Imprest holders on the division, supply of uniform & stationery of their division. They have also been given powers for purchase of stock items of value Rs.50 lakhs in emergencies. Sr. Divisional Material Managers are also responsible for identification, mobilization, sale of scrap & timely delivery of divisional scrap to purchasers.

10.2 Major achievements during the year:

- Purchase activities are being monitored on daily basis as a result of that field unit has complied 91184 demands i.e.97.70% of total 89083 demands received during 2023-24 which has resulted in improved availability of material.
- The scrap worth Rs. 217.62 Crs. was sold during the year 2023-24. Surpassing the target of Rs. 220.0 Crs. 100% auctions are being done through e-auction only.
- Inventory Turnover Ratio (without fuel) of 28.75% was achieved in the year 2023-2024 against the target of 46%.
- NWR has successfully implemented E-procurement system (IREPS) & dispensed with all manual tendering. E-tendering has got its various inherent advantage of reduced tendering time & increases transparency, equity & fairness, customer friendliness.
- NWR has successful implemented 100% User depot Module (UDM) and also working smoothly of material receipt and distribution on line over all consignees in NWR.
- **Implementation of IMMS:-**

To achieve paperless working, NWR has migrated from MMIS to IMMS from 1st December 2016. All modules of IMMS, which includes HQ Module, Depot Module, LP Module, Bill Passing Module have been made operational from 1st December 2016. From all POs are being vetted through online & digitally signed & transmitted to vendors through e-mail in paperless mode.

10.3 WEBSITE & IT APPLICATIONS:-

Following documents / information in English & Hindi has been uploaded on website www.nwr.indianrailways.gov.in for wide publicity, transparency and easy accessibility to vendors:-

Sr. No.	Subject
1.	Stores Organization Chart and duties
2.	Tenders
3.	E-Procurement
4.	Auction program

5.	Auction catalogue
6.	IRS conditions of contract
7.	Instruction for tenderers
8.	SOR
9.	Schedule of Powers
10.	Bill Form
11.	Vendors with Stores Dept.
12.	Vendors registration Form.
13.	Registration policy
14.	List of safety items
15.	Arbitration cases

10.4 Purchase:

1. Value of Purchase during the year 2023-24 is:- (Value in Cr. of RS.)

Purchase of Fuel	Purchase other than fuel	Total
3758.53	473.26	4231.79

2. Statement of tender issued:-

Stock	Non-Stock	Total
4491	509	5233

3. Statement of purchase order placed:-

Stock	Non-Stock	Total
4301	742	5043

****

4. Availability of safety & vital items:-

Items	No. of items stocked	Stock available in No. of items	Percentage Availability
Safety	716	680	96.0
Vital	764	741	97.0

10.5 Performance of field units:

1. Group-wise issue of stock items:

Sr. No.	Group	Issues (in lac. of Rs.)
1.	10-29 (Diesel & Elect loco)	3947.49
2.	30-39 (C&W)	33017.69
3.	40-49(Electric)	5743.66
4.	50-59 (S&T)	434.60
5.	60-69 (M&P)	208.39
6.	70-78 (Gen.)	2794.57
7.	79 (Uniform)	3984.38
8.	80-89 (POL)	6418.70
9.	90-93 (Steel)	1205.74
10.	98 (Scrap)	4433.61
Total		**62188.83**

2. Inventory Status:-

Details of Receipts, Issues and Closing balance are given below TOR %

(Figures in Crores of Rs.)

Year	Opening Balance as on 1st April-2023	Cumulative Receipt up to Mar. 2024	Cumulative issues up to Mar.2024	Closing Balance as on 31st Mar. 2024	TOR %	
					Rly.Bd. Targets	Achieved
2023-24	116.56	687.27	621.89	181.94	46	29.26

3. Cost per unit of receipt & issues

Yearly expenditure on staff in Crs. of Rs.	Value of stores in Crs. of Rs. (Receipt +Issues)	Cost of transaction per Rs.100/- of stores
38.05	1142.37	3.33%

4. Cost per unit Purchase at HQ

Yearly expenditure on HQ staff in Crs. of Rs.	Value of stores Purchase in crs. of Rs. (with fuel)	Procurement Cost per Rs. 100/- of stores
15.54	4231.79	0.367%

5. Compliance of demands by field units:

Demands	Fully Complied	Partly complied	Percentage compliance
91184	97.70%	1138	97.70%

6. Stock verification of Stores Depots:

(a) Physical verification:

No. of items verified	% verified without discrepancy	Less than 1% discrepancy	More than 1% discrepancy
4714	100%	0.22%	0

(b) Loss and gain as a result of accounts and stock verification figures in lacks of Rs.

Loss	Gain	Net Loss	Net Gain
Nil	Nil	Nil	Nil

(c) Theft and loss

S. No.	Item	No. of class	Value
1	Nil	Nil	Nil

7. Over-stock & Surplus:

(a) Surplus Stock

S No.	Item	Value (Lac of Rs.)
1	Value at the commencement of the year.	313.90
2	Value at the end of the year.	884.10

(b) Over Stock

S.No.	Item	Value (Lac of Rs.)
1	Value at the commencement of the year.	1038.90
2	Value at the end of the year.	4020.0

(c) Inactive items:

S.No.	Item	Value (Lac of Rs.)
1	Value at the commencement of the year.	268.40
2	Value of items at the end of the year.	571.50

10.6 Scrap disposal:

1. Disposal of scrap: (value in Cr. of Rs.)

Year	Target	Disposal
2023-24	220	217.62

2. Category-wise disposal of scrap:

(a) Ferrous (M/T)

Sr. No.	Item	OB (MT)	Arising (MT)	Total (MT)	Disposal (MT)	CB (MT)	Value of Scrap disposed (Rs. In Cr.)
1	Rails	1003.824	14773.438	15777.262	15150.059	627.203	60.83
2	Other P Way	243.076	2898.982	3142.058	2990.838	151.220	10.58
3	Others	166.700	16473.494	16640.194	16424.336	215.858	63.03

(b) Condemned rolling stock (FWUs):

Sr. No.	Item	OB (No.)	Arising (No.)	Total (No.)	Disposal (No.)	CB (No.)	Value of disposal (Rs. in Cr.)
1	Wagon	0	222	222	222	0	10.64
2	Coaches	1	58	59	38	21	2.31
3	Locos	2	64	66	50	16	35.15
4	Others(in MT)	153.596	4156.968	4310.564	4285.280	25.284	17.72

(c) Non-Ferrous (M/T)

S.No.	Item	OB	Arising	Total	Disposal	CB	Value of scrap disposed (Rs. in Cr.)
1	N/F	39	1438.892	1477.892	1477.892	0	17.36

Note:- Direct sale to PRC sleeper of Rs. 0.00 Cr.

Chapter-11

Medical Department

1. **Introduction-**

Medical department of North Western Railway render preventive, promotive and curative health care services to more than 2.25 lakhs railway beneficiaries – 47135 employees, 103017 employee family, 35675 pensioners, 43990 pensioner family (as per UMID Portal data) by 129 sanctioned strength of IRHS including Dental officers, 36 HVSs and 972 paramedical staff over 1 Central Hospital, Jaipur, 3 Divisional Hospitals – Ajmer, Bikaner and Jodhpur and 31 Health units over NWR.

2. **The Central Hospital, Jaipur**

The Central Hospital, Jaipur was started by up gradation of existing divisional hospital, Jaipur in 2005. The Central Hospital, NWR, Jaipur renders comprehensive health care including preventive, promotive and curative services to 12219 railway employees and 12330 RELHS members of Retired Railway Employees Liberalized Health Scheme and a substantial number of dependents of the above two groups. Besides this also the patients referred from other zones and Divisions. 150 hospital bedded Central Hospital, JP was upgraded to 201 bedded hospital in Feb 2024 by transferring beds from different divisions.

- Gradual modernization of the central hospital is being done. After up gradation, there is phenomenal expansion in the facilities and services provided to the railway beneficiaries. High quality health care services are being provided by regular IRHS doctors, 45 Super specialty Private Empanelled Hospitals, 09 Private Empanelled Laboratories and 12 Honorary Visiting Specialists in the fields of Cardiology, Orthopedics, Nephrology, Medical Oncology, Radiology, Gastroenterology, Dentist, Dermatology, Pathology, ENT and Paediatrics and also by calling specialists on case to case basis. Various major and special major surgeries are being performed in Central Hospital like MIPH, PCNL, Phaco-surgeries, Radical Neck Dissection, OncoSurgeries like Commando operation, Ortho surgeries, ORIF, Plating TKR, THR, Arthroscopy and Laparoscopic surgeries like Lap. Cholecystectomy, Lap. Oophorectomy, Colonoscopies, Gastroscopies, Bronchoscopes etc. New services have been introduced like Haemodialysis, Arthroscopy, NCV Studies, PFT, CTMT, EEG & Holter Monitoring, laparoscopic Cholecystectomy, USG, Whole Body

Color Doppler, Automated Perimetery, Cystoscopy and Histopathology. Many sophisticated equipments have been procured in Central Hospital, Jaipur. Infrastructures for patient's care & comfort items have been commissioned in Central Hospital.

❖ Central Hospital Jaipur has been awarded Green Building Health Care Facility Platinum rated Certificate.

- It is a matter of pride that the Central Hospital, NWR, JP has been the recipient of National Energy Conservation Awards from Ministry of Power, Government of India from time to time in the year.

- Important achievements during year 2023-24 i.e. No. of Indoor patients admitted – 14186, No. OPD Patients attended – 340176, No. of Special Major Operations – 82, No. of Major Surgeries – 962, No. of Cataract Operations with IOL – 801, Haemodialysis – 2361, No. of CT Scans – 2357, No. of MRIs – 3515, Dental Procedures – 2872, Diagnostic Investigations – 619156, 24 Water Samples tested and 95.83% found fit. Non Railway Earnings – Rs. 8,48,826/-. Training to Doctors and paramedical staff had been imparted from time to time including HMIS.

- The following new technologies introduced and innovations have been done in CH/JP during 2023-24
- Implementation of HMIS Software in CH/JP.
- Super Specialty Urology Services.
- Hemodialysis.
- Medical Oncology services – In-house chemotherapy.
- Senior Citizen OPD and AC Waiting Room.
- Empanelled 45 Private Multi-Specialty Hospitals.
- Empanelled 09 Private Labs / Diagnostic Centers.
- Installation of High Speed Wi-Fi.
- Installation of CCTV Camera for security.
- Hospital Waste Management & Disposal.
- Solar Plant 50 KW.
- Sewage Treatment Plant (STP).
- Water Harvesting.
- Fire Fighting.
- E-Procurement.
- Tele-medicine services restarted in CH/JP with DH/AII & HU/FL.
- Security of Hospital – Wi-Fi and CCTV Camera installed in CH/JP.

- Computerized OPD Registration System and Token System in OPD, Lab and Dispensary.

- CH/NWR/JP entered MoU with Pink City Nursing College Jaipur for imparting Clinical Training to Nursing Students as per the Rly Bd guidelines.
- DNB post-graduation in General Medicine and Obst & Gynae available.
- List of the empanelled hospitals as per new Common MoU is displayed at reception for awareness of Railway Beneficiaries so that they can decide their choice of referral.
- Department wise 10 Mega Wellness Assurance Health Check-up Camps were organized and employee were examined. 100% of Gazetted and Non-gazetted employee's health check-up was done.
- 'Women Health Check-up Camp was organized on the occasion of "International Women Day" on 20.03.2024 at ROC, Jagatpura was done.

The Divisional Hospital Ajmer:-

The Ajmer Division of the North Western Railway renders comprehensive healthcare services to about 108992 Railway beneficiaries including 14892 serving employees & about 24517 Retired employees under the RELH Scheme. These services are provided through one Divisional Hospital at Ajmer, two Sub Divisional Hospitals at Abu Road and Rana Pratap Nagar, Udaipur and 02 First Aid posts at Ajmer Loco & Carriage workshops, 08 Health Units & 04 Lockup Dispensaries at various places in the Division. The Divisional Hospital at Ajmer

is 166 bedded & is one of the oldest Railway Hospitals in India, established in the year 1890. It also runs large medical and surgical wards, male and female separately and 8 bedded ICU, modern Labor Room and Children ward also. Treating almost 7613 indoor patient in the Period of 2023-24. Earlier it was famous for Advanced Orthopedic Surgeries, Now again Advanced Orthopedic Surgeries done at DRH Ajmer. During 2023-24 Orthopedic Surgeries Like THR, Total Knee Replacement, ACL Reconstruction-, Rotator Cuff Repair -, Bone Marrow Implant , PRP Therapy, Later Jet Procedure, Volar Distal Radius Plating, Autologus Osteochandral Transplant , Bipolar Prosthesis with spacer G Implantation and Arthroscopic BANKART Repair done at Divisional Hospita Ajmer. The Divisional Hospital at Ajmer is the only Hospital in the North Western Railway Zone where Endoscopic surgeries like TURP, Renal, Bladder & Ureteric Stone removal, PCNL, Ureteric Stenting, Laproscopic surgeries. Gynae surgeries like LSCS, Total Abdominal Hystrectomy. Veginal Hystrectomy,Laparotomy, Laproscopic surgeries like Lap cholecystectomy, Lapappendictomy, Hernioplasty, etc. Advanced ophthalmic surgeries like PCIOL with Phacoemulsification technique are being done on routine basis. Ajmer Division is

under the administrative control of DRM and headed by the Chief Medical SuperintendentNew Lift installed at new building for convenience of female patients

BIKANER Division:-

The Medical Department of North Western Railway renders comprehensive healthcare services to a sanctioned strength of 10,338 employees & their families including casual labour & staff of Construction Department . The 10285 members of Retired Railway Employees Liberalized Health Scheme also avail medical facilities in the Railway Hospitals & Health units. Total Railway beneficiaries are approx. 61208 in Bikaner division.

Jaipur Division:-

The Medical Department of Jaipur Division renders comprehensive health services to a sanctioned strength of 11238 employees & their families including staff of all Department & 8408 members of RELHS with their dependent family members also avail medical facilities in the Railway Hospitals & Health Units Jaipur Division is headed by Chief Medical Superintendent , Divisional Hospital at Jaipur has been upgraded to Central Hospital , Jaipur and is headed by MD/CH/JP has been providing medical services at Jaipur. There are two sub divisional Hospitals Bandikui & Rewari and 06 Health units , Namely , Alwar, Sikar, Ringus, phulera, HQ. & GTJT Further there are three Scale- I ARMEs available over the Division i.e. ARME Scale- I (BG) at Jaipur , SPARMV at Rewari and ARME Scale- II at RGS & Sikar, Lalsot.

Jodhpur Division:-

The Medical Department of North Western Railway renders comprehensive healthcare services to a sanctioned strength of 11430 employees & their families including casual labour & staff of Construction Department . The 8005 members of Retired Railway Employees Liberalized Health Scheme also avail medical facilities in the Railway Hospitals & Health units. Total Railway beneficiaries are approx. 62486 in Jodhpur division.

Important achievements of Medical Deptt. Of NWR :-

- No. of Indoor patients admitted 30041, No. OPD Patients attended -1255496, No. of Special Major Operations –132 No. of Major Surgeries –1567, Minor Surgeries-3507, No. of CT Scans- 4948 & MRIs – 7132, No. of Sterilizations 55, Immunizations for BCG 378, 2953 Bacteriological water sample tested and found fit 94.92%, 55658 Water Samples tested for Residual Chlorine and 92.47 % found fit, 162 Food Samples tested


under FSSA in which 144 no. samples (88.88%) found fit, 874 Food samples tested under Quality Control in which 97.02 % found fit, in annual wellness assurance checkup in NWR- Total 35608 Employees were covered (40.80%).

Other important achievements of Medical/NWR for the period of 2023-24 are as follows –

1. Worthy GM/NWR inaugurated 06 bedded ICU at CH/Jaipur on19.04.2023
2. Ayurvedic OPD was started at Central Hospital Jaipur on 11.08.2023 in collaboration with Ayurvedic institute. Railway beneficiaries start getting consultation and ayurvedic medicines free of cost.
3. A new latest technique 4 K-HUD orthoscope system installed at Divisional Railway Hospital Ajmer worth 42 lakhs resulting in facilitating complex orthopaedic surgeries at DRH/AII.
4. Under FSSAI Alwar, Gandhinagar, Ajmer, Bikaner and Jodhpur railway stations food vendors imparted Eat Right training. 06 big stations of NWR got Eat Right certificate from FSSAI.
5. 12 bedded oncology ward started at central hospital Jaipur. Railway beneficiaries start getting chemotherapy in-house. It is only urology center in entire Indian Railway where advanced urological procedures are being done. Direct recruited IRHS Sr DMO Mch Urology is rendering services at Central hospital Jaipur and Divisional Hospital Ajmer and doing almost 35-40 minor and 25-30 Major urological procedures are being done on monthly basis resulting railway revenue saving to the tune of almost 15 Lakhs per month.
6. Successful medical examination of 2050 and 5109 candidates sent by RRB Ajmer and RRC Jaipur respectively was conducted by various units of NWR during Rojgar Mela.
7. In view of increased load on Indoor department at Central Hospital, beds at CHJP increased from 150 to 201 (by transferring from other units).
8. Extensions of health facilities done at Rail Nikunj for railway beneficiaries.
9. For prevention and better health of railway beneficiaries multiple health checkup camps are being organized by various units all over NWR. Till 22.03.2024 more than 90% railway employees got benefit of these camps.
10. For ensuring availability of medicines to railway beneficiaries Annual Medical Indent 2024-25 was compiled and submitted to Stores department after finance concurrence 4 months prior in comparison to last year.
11. DRM Jodhpur inaugurated renovated maternity ward and laboratory department on 26.01.2024. A new machine worth 35 lakh is purchased and installed in

DRH/JU (From CRS Fund). Renovated Pharmacy AC waiting Hall for retired Railway beneficiaries and Male Medical Ward was inaugurated by DRM/JU on 15.08.2024.

12. Renovation work of Divisional Railway Hospital Bikaner got completed. During the same one new administrative block is constructed.
13. PCMD/NWR inaugurated one new latest technology Vitectomy Machine with Phaco-Emulsification having Straight Cutter worth 45 lakhs on 05.01.2024.
14. Worthy GM/NWR inaugurated newly constructed Urology modular OT with all latest equipments and renovation of Operation theatre complex.
15. For enhancing facilities for DNB residents, 09 room hostel facilities is being made available in building transferred from sports department.
16. Total 21 items for various specialties were sanctioned under M&P for the year 2023-24. It is first time in the history of NWR Medical Department that these much M&P items were sanctioned.

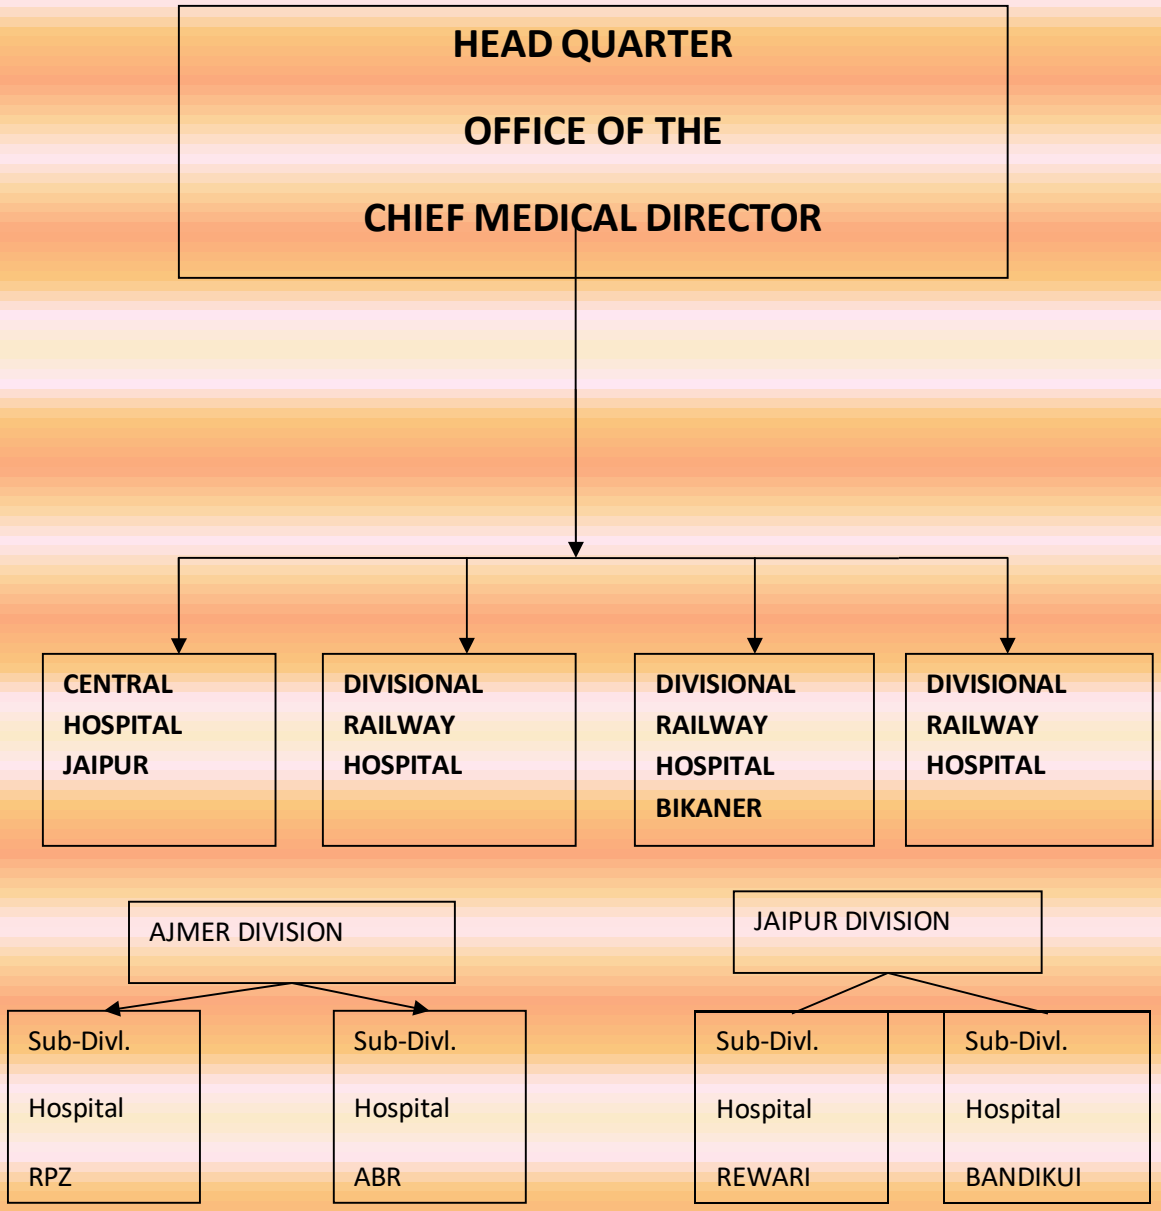
HEAD QUARTER
OFFICE OF THE
CHIEF MEDICAL DIRECTOR
CENTRAL HOSPITAL JAIPUR
DIVISIONAL RAILWAY HOSPITAL
DIVISIONAL RAILWAY HOSPITAL BIKANER
DIVISIONAL RAILWAY HOSPITAL
AJMER DIVISION
JAIPUR DIVISION
Sub-Divl. Hospital RPZ
Sub-Divl. Hospital ABR
Sub-Divl. Hospital REWARI
Sub-Divl. Hospital BANDIKUI

3. Man Power Resources:

3.1 Staff Strength - Medical

Sanctioned strength of Group A, B, C & D staff in Medical Department of NWR.								
Sr.	**Category**	**HQ Office**	**CH-JP**	**All**	**BKN**	**JP**	**JU**	**Total**
	Group A							
1.	Medical officers	4	26	35	22	16	24	**127**
2	Hosp. Adm.	-	1	-	-	-	-	**01**
3	Dy CMM	-	1	-	-	-	-	**01**
	Total of Gr..A	4	28	35	22	16	24	**129**
	Group B							
1.	APHO	1	0	0	0	0	0	**01**
2.	AHO	1	0	0	0	0	0	**01**
3.	AHEO	0	0	0	0	0	0	**00**
4.	A.PHY.O	0	0	0	0	0	0	**00**
5.	ANO	0	1	1	1	0	1	**04**
6.	PS-I	1	0	0	0	0	1	**02**
	Total of Gp. B	**3**	**1**	**1**	**1**	**0**	**2**	**08**
	Group C							
1.	Pharmacists	1+1	19	35	23	18	24	**121**
2.	Health Insp.	1+1WC (Gen)	1	20	18	29	16	**86**
3.	Radiographers	-	5	05	01	2	01	**14**
4.	Lab. Staff	-	14	12	03	3	04	**36**
5.	Ministerial Staff	11	4	10	08	8	12	**53**
6.	Nursing Staff	--	60	65	39	16	42	**222**

7.	Midwives	-	0	00	0	0	00	**00**
8.	Drivers	-	05	01	04	02	00	**12**
9.	Dressers/OTA	-	12	25	18	11	14	**80**
10.	Cooks	-	04	00	02	00	02	**08**
11.	ECG technicians	-	04	01	00	00	00	**05**
12.	Physiotherapists	-	02	01	01	00	01	**05**
13.	Dialysis technicians	-	02	00	00	00	00	**02**
14.	Dieticians	-	01	00	00	00	00	**01**
15.	Motor Driver	-	00	00	00	00	-	**00**
16.	Personal Inspector	-	01	00	00	00	-	**01**
17.	Sr.S.O. (A/c)	-	01	00	00	00	-	**01**
18.	Refractionist	-	01	00	00	00	-	**01**
19.	Occupational Therapist	-	01	00	00	00	-	**01**
20.	Dental Hygienist	-	01	00	00	00	-	**01**
	Total of Gp.C	**15**	**138**	**175**	**117**	**89**	**116**	**650**
	*** 01 post of AHO temporarily transferred to WR/CCG (Operated at Bombay Div.).**							

3.2. Family Welfare Department:-

S. No.	Group 'C' Category	HQ	All-Div	BKN- Div	JP-Div	JU- Div	Total
1.	Sr.DEE	01	00	00	00	01	**02**
2.	DEE	00	01	01	01	00	**03**
3.	Compilation Clerk	01	01	01	01	01	**05**
4.	FWO	0	01	01	01	01	**04**
	Total	**02**	**03**	**03**	**03**	**03**	**14**

3.3 Group D Staff

S. No.	Group 'D' Category	HQ	CH-JP	All-Div	BKN-Div	JP-Div	JU-Div	Total
1	X-ray Asstt.	-	03	00	01	2	00	**06**
2	Lab Attendants	-	02	00	01	1	0	**04**
3	Packers	-	03	00	00	1	0	**04**
4	St. Bearer	-	06	00	03	0	0	**09**
5	Cook Helper	-	01	00	00	0	0	**01**
6	Hospital Safaiwala	-	7	00	06	06	02	**21**
7	Hospital Safaiwali	-	00	00	00	0	00	**00**
8	Hospital Attendants	-	47	150	74	34	66	**371**
9	Record sorter	-	00	00	01	0	0	**01**
10	Peons/D.Peon.	-	00	00	00	0	2	**02**
11	Sanitary Khallasi	-	00	00	00	0	0	**00**
12	Watchman	-	00	00	00	0	1	**01**

13	Laskar / Bhisty	-	00	00	00	0	0	**00**
14	Amb. Kh /Cl. S.Wala	-	00	00	00	0	1	**01**
15	SSC Jamadar	-	00	00	00	0	0	**00**
16	Sanitary Safaiwalas	-	00	00	22	45	23	**90**
17	Malis	-	00	00	00	0	00	**00**
18	FW Attendants	-	00	00	00	0	00	**00**
19	Anti Malaria Mate	-	00	00	00	0	1	**01**
20	Anti Malaria Kh.	-	00	00	16	12	1	**29**
21	Office Peon	05	00	05	01	0	0	**11**
22	Hamal	-	00	00	00	0	0	**00**
23	Ayah	-	11	00	00	0	0	**11**
24	Truck Khallasi	-	00	00	00	0	0	**00**
25	Banglow Peon	04	02	00	01	0	00	**07**
26	Khallasi	-	0	00	00	0	0	**00**
Total		**09**	**82**	**155**	**117**	**100**	**95**	**558**

4. Infrastructure

4.1 Hospitals & Health Units over NWR

DIV./Units	HOSPITAL (Beds)				Health Units	Lock up Dispensary
	Central & Divisional		Sub Divisional			
	Name of the hospital	No. of Beds	Name of the hospital	No. of Beds	-	-
HEAD QTR	CENTRAL HOSP	201	-	-	-	-
JAIPUR	JAIPUR DIV	30	2 (BKI & RE)	10+20 = **30**	6	-
AJMER	DIVISIONAL HOSPITAL	166	02—Sub Divisional Hospital ,ABR Rana pratap Nagar	12+9= **21**	8+2 (F.A.post)	04
BIKANER	DIVISIONAL HOSPITAL	84	-	-	9	01
JODHPUR	DIVISIONAL HOSPITAL	102	00	00	8	00
		553	**04**	**51**	**31+2 FA. Post**	**05**

4.2 Total no. of Hospital & Health Units.

	HQ	JP	AII	BKN	JU	Total
Central Hospital	01	-	-	-	-	**01**
Divisional Hospital	-	-	01	01	01	03
Sub Divisional Hospital	-	02	02	-	-	**04**
Health units	-	06	8	09	08	**31**
Lock up Dispensaries	-	01	04	-	-	**05**
First Aid Posts	-	-	2	-	-	**02**
Total no. of Beds in Hospitals	201	30	187	84	102	**604**

5 . Curative services:-

S. No.	Particulars	2023-24	2022-23
1.	No. of hospital beds per 1000 employees (incl. casual labour)	12.61	12.98
2.	**No. of in-patient Treated**		
	I. Males	11395	11197
	II. Females	10702	9112
	III. Children	8889	1773
	TOTAL	**30986**	22155
3.	**Bed occupancy ratio**	49.35	48.48
4.	**No. of outdoor patient**		
	I. Males	462402	490765
	II. Females	389985	305814
	III. Children	37195	45856
	TOTAL	**1269021**	1241385
5.	**No. of Major operations performed**	1699	1505
6.	**No. of Cataract Surgeries With IOL**	1131	1098
7.	**Diagnosis**		
	I. Investigations	1316673	1286059
	II. No. of CT Scans& MRI	12080	10204

6. **Oral Health Services**:-

S. No.	Particulars	2023-24	2022-23
1.	Total no. of new patient treated.	14030	15553
2.	Total no. of old patient treated.	14414	12298
3.	Total no. of permanent filling.	2150	2607
4.	Total no. of root canals done.	1686	1235
5.	Total no. of scaling done.	1702	1419
6.	Total no. of dental operations done.	155	57
7.	Total no. of tooth extractions done.	1038	982

7. **Man Days Lost** :-

Sr. No.	Particulars	2023-24	2022-23
1	**Total no. of RMC Issued**	**14556**	**16599**
2	**Total no. of Man days Loss on RMC**	**168424**	**202308**
3	**Total no. of Man days Loss on IOD**	**15943**	**14856**
4	**Total no. of Certificate Issued on IOD**	**543**	**511**
5	**Average days Per Certificate**	**12.21**	**12.69**

8. **Drug Analysis:**

Division	Drug Samples Taken		Found Fit		Found Unfit	
	2023-24	2022-23	2023-24	2022-23	2023-24	2022-23
CH/JP	21	17	21	17	0	0
DH/AII	11	13	11	13	0	0

DH/BKN	20	22	20	22	0	0
JP-Div.	5	0	5	0	0	0
DH/JU	12	8	12	8	0	0
TOtal	**69**	**60**	**69**	**60**	**0**	**0**

9. Drug Analysis Results:- No Sample found sub-standard.–

The details are as follows-

S. No.	Name of Drug / Product	Name of Manufacturer	Name of lab, where sample sent for Analysis	Cause of Sub Std.
1.	**Nil**			

10.0 **Public Health:-** Special arrangements in sanitation are done during fair and festivals like Pushker Mela, Ramdeora Fair etc. in which sanitation arrangements were done by medical department. Multi-Purpose Drives were conducted throughout the year in which health check-up/Wellness Check of Employees were done & medicines were also distributed among the staff.

10.1 **Family Welfare & other National Programmes:**

Medical organization provides family welfare services to railway population and the community**.**

Services	2023-24	2022-23
Sterilizations	61	110
IUD's	50	62
CC Users	14495	6957
BCG	379	342
DPT	353	384
Measles	322	407

Universal Immunizations Programme for children and expectant mothers is an ongoing activity. Likewise other National Programme, e.g., RNTCP, National malaria Control Programme, National AIDS control Programme etc. are also implemented.

10.2 Immunization:

S. No.	Division	BCG	DPT 3rd Dose	OPV 3rd Dose	Measles	TT(PW)
1.	AJMER	35	77	43	75	261
2.	BIKANER	29	27	37	44	53
3.	JAIPUR	269	99	99	138	36
4.	JODHPUR	45	33	33	65	60
TOTAL		**378**	**236**	**206**	**322**	**410**

10.3 Pulse Polio Immunization Programme:

S. No.	Div	Phase-I		Phase-II		Phase-III		Total	
		Rly	Non Rly	Rly	Non Rly	Rly	Non Rly	Rly	Non Rly
1.	All	465	1235	-	-	-	-	-	-
2.	BKN	541	1681	317	1025	0	0	**858**	**2706**
3.	JP	209	1820	-	-	-	-	-	**2029**
4.	JU	518	894	480	1254	-	-	**1412**	**1734**
TOTAL		**1733**	**5630**	**797**	**2279**	**0**	**0**	**2270**	**6469**

10.4 Division wise Family Welfare Activities:-

S. No.	Division	Sterilization	IUD Insertion	CC Users	Oral Pills
1.	Ajmer	08	04	240	10
2.	Bikaner	04	02	95	32
3.	Jaipur	28	39	**7680**	370
4.	Jodhpur	21	05	**6480**	270
		61	**50**	**14495**	**682**

10.5 Sanitation: Medical dept. of North Western Railway is responsible for sanitation of major railway colonies. The way side station / colonies are under control of Commercial Deptt. / Engineering Deptt.

SANITARY STAFF– (GR.C & GR.D).

NWR	Total	Category	SC	WC	Vacancy	Total Vacancy
Total		Gr. C	18	18	0	05
		Gr. D	22	17	05	

Outsourcing is done in the major colonies in NWR.

11.0 HIV/AIDS Prevention & Control Programme:

S. No.	Division	Tests done	Pool Size
1.	CH-Jaipur	6844	60
2.	AJMER	2961	30
3.	BIKANER	634	00
4.	JAIPUR	-	-
5.	JODHPUR	886	00
Total		**11325**	**90**

11.1 No. of deaths due to AIDS since inception:

Division	No. of Death due to AIDS since inception
CH-JP	16
All	-
BKN	00
JP	-
JU	-
Total	**16**

11.2 No. of HIV / AIDS patients on HAART:-

Division	No. of HIV / AIDS patients on HAART
CH-JP	00
All	00
BKN	00
JP	00
JU	00
Total	**00**

11.3 Availability of blood banks:- NO Blood Bank available.

Blood if required is being collected from other local Authorized blood banks.

11.4 Facilities available in all divisions (HIV testing):- YES

12.0 Drinking water quality:-

12.1 Division wise water sample tested for Bacteriological Quality:-

S. No.	DIVISION	Water Sample Collected	No. of found fit	% age of fitness
1.	CH-JP	24	23	95.83
2.	AJMER	743	730	98.64
3.	BIKANER	858	834	91.20
4.	JAIPUR	832	832	100
5.	JODHPUR	557	521	93.53
Total		**3014**	**2940**	**97.55**

12.2 Division wise water sample tested for Residual Chlorine Test:-

S. No.	DIVISION	Water Sample Collected	No. of found fit	% age of fitness
1.	CH-JP	942	894	94.90
2.	AJMER	24925	24793	99.47
3.	BIKANER	9621	9017	93.72
4.	JAIPUR	13561	13362	98.53
5.	JODHPUR	7443	3980	53.47
Total		**56492**	**52046**	**92.12**

12.3 Reports on Packaged Drinking Water:-

S. No.	DIVISION	FSS-Act*		Quality Control	
		Sample collected	Satisfactory	Sample collected	Satisfactory
1.	AJMER	03	03	07	07
2.	BIKANER	00	00	46	45
3.	JAIPUR	03	03	32	29

4.	JODHPUR	01	01	42	42
TOTAL		**07**	**07**	**127**	**123**

13. Food quality QC & FSSA:-

13.1 Food samples collected under FSSA & Quality Control:

S. No.	DIV	FSSA			Quality Control		
		Collected	Satisfactory	% Fit	Collected	Satisfactory	% Fit
1.	All	52	44	84.61	155	155	100
2.	BKN	43	40	93.02	328	327	99.70
3.	JP	48	42	87.50	221	212	95.92
4.	JU	19	18	94.73	170	162	95.29
Total		**162**	**144**	**88.88**	**874**	**856**	**97.94**

14.0 Surveillance of Communicable Diseases:

14.1 Reports on Malaria Cases:-

S. No.	Particulars	2023-24	2022-23
1.	No. of fever cases.	55187	42807
2.	No. of blood smears.	6434	5156
3.	No. of report +ve for malaria.	06	08
4.	No. of PF Cases.	01	01
5.	No. of cases given radical treatment.	01	02

14.2 Communicable Diseases:

A Statement showing the no. of attacks & deaths due to various diseases are as follows:-

S. No.	Disease	2023-24		2022-23	
		Attacks	Deaths	Attacks	Deaths
1.	Cholera	-	-	-	-
2.	Plague	-	-	-	-
3.	Malaria	-	-	-	-
4.	T.B.	36	-	35	-
5.	Enteric fever	199	-	58	-
6.	Diphtheria	-	-	-	-
7.	Influenza	-	-	-	-
8.	Measles	-	-	-	-
9.	Mumps	-	-	-	-
10.	Chicken pox	-	-	-	-
11.	Whooping cough	-	-	-	-
	TOTAL	**235**	**-**	**93**	**-**

15. <u>Health Education</u>:--

S. No.	Particulars	2023-24	2022-23
1.	Lectures	161	127
2.	Group talk	214	273
3.	Film demonstration	06	05
4.	Exhibition	96	147
5.	Baby Shows	02	01
6.	Multipurpose Health drives	412	184

7.	Orientation training Programme	09	195
8.	Other Programme (CME/Seminar)	67	09
9.	Health Talks	219	180

16.0 Training

16.1 Gazetted staff :

S. NO.	Name of Doctor and Designation	Subject of Training and duration (from-to)	Place of Training
CENTRAL HOSPITAL, JAIPUR			
1	Dr.Indu Singh, Sr.DMO/OBC/CH/JP	Advance Gynaecology Laparoscopy Endoscopy Training Program (01.03.2023 to 29.05.2023)	Mahatama Gandhi Hospital ,Jaipur
2	Dr. Mukesh Kumar Mandawriya, ADMO/CH/JP	6th Annual CONFERENCE OF Thorasic Endoscopy Society (TESCON 2022) (07.04.2023 to 09.04.2023)	NIT, Jalandhar Punjab
3	Dr.L.S.Nainwal, ACHD/Ophth/CH/JP	03 days comprehensive workshop on "Leading change" for IRHS Officers SG/NF-SAG/SAG Level.(22-24 May,2023)	NAIR /BRC
4	Dr.Juhi Asopa, DMO/OBG/CH/JP	Refresher Course HM-06/23 for IRHS Officers from JS to JAG level . (26-30 june 2023)	NAIR /BRC
5	Dr.Juhi Asopa, DMO/OBG/CH/JP	Training in Ultrasonography (1-14, Aug,2023)	Ansh Advance Foetal Care Centre,Jaipur
6	Dr. R.S.Matoria, Sr.DMO/Psy/CH/JP	Online Training on "Big data, Data Analytics and Artificial Intelligence " (IT 07.23)(25.09.23 to 29.09.23	NAIR /BRC
7	Dr. Shavika Gupta DMO/OBG/CH/JP	FOGSI National Conference on Infections in OBGYN-CCC-2023 (29.09.23 to 01.10.23)	Rajasthan International Centre (RIC) Jaipur
8	Dr. Shivank Mathur, Sr,	46th Annual Conference of the Association of Colon and Rectal Surgeons of India (29th	Hotal Radison Blue,Indore

	DMO/Surg/CH/JP	Sept to 01st Oct, 2023)	
9	Smt. Silochana Soinkriya, ANO/CH/JP	Group B Foundation program 11/23 04.12.2023 to 22.12.2023 (03 weeks)	NAIR /BRC
10	Dr. R.P.Choudhary, ACHD/Orth/CH/JP	68th Annual Conference of The Indian Orthopaedic Assiciation. (14.12.23 to 17.12.23)	Ekana Sports Complex LKO
11	Dr. Sahvika Gupta, DMO/OBG/CH/JP	Indian Railway Association of Gynaecology & Obstetrics Conference by ICF Hospital, Chennai (From 04.05, Jan 2024)	CH/SR
AJMER DIVISION			
1.	NIL		

BKN –DIVISION

2.	Dr. G.K.Das, ACMS Radio/DH/BKN	Training on Occupational Health 19-11-23 to 21-11-2023	NAIR/BRC
3.	Dr. G.K.Das, ACMS Radio/DH/BKN	Radiographer' s Conference as Guest Speaker on 24-11-23 to 26-11-2023	Central Hospital Garden Reach Hospital , Kolkata (SER)
4.	Dr. Suresh Chand Meena / Sr. DMO/JP	Hospital Management from 26.06.23 to 30.06.23	NAIR, Vadodara

JODHPUR DIVISION

1 .	Psychiatric in General Practice	Dr.Pradyumna Kumar Sahoo/ADMO	CH/NWR/JP
5.	Mandatory Induction Program (ALP Med 01/23)	Dr. Vijay Choudhary /Sr. DMO Dr.Gulab Singh/ SR.DMO	NAIR,BRC
6.	Refresher Course (HM-06/23)	Dr.Ayush Singh Gehlot/ADMO	NAIR,BRC
7.	Special Refresher Course (HM-11/23)	Dr. A. Vasudevan /CMS	NAIR,BRC

8.	Webinar on "Green Certification of Railway Hodpitals"	Dr. Gulab Singh /Sr.DMO	ONLINE
9.	Big Data, Analyties and Artificial Intelligence	Dr.Ayush Singh Gehlot/ADMO	ONLINE
10.	Leading Change	Dr. Neha Tiwari/Sr.DMO	NAIR,BRC
11.	Refresher Course HM-06/23	Dr.Ayush Singh Gehlot/ADMO	NAIR,BRC
12.	Basic Course on Occupational Health HM-20/23	DR.Rama Ram Kumawat/DMO	NAIR,BRC
13.	Continuing Dental Education Program	Dr.Saita Yadav /DDS	Dr.Babasaheb Ambedker Memorial Hospital, Byculla, Mumbai, CR

16.2 Training in RCH Programme:- Nil

16.3 Laparoscopic Sterilization Programme:- NIL

Total Medical officer trained = **07**

16.4 Paramedical Training Programme:-

S. No.	Division	Total
1.	CH/JP	150
2.	Ajmer	167
3.	Bikaner	161
4.	Jaipur	-
5.	Jodhpur	72
		550

17. **Non Railway Earning**:

Sr. No.	Division	Non Railway Earnings (In Rs.)
1	CH-JP	8,48,826/-
2	AJMER	2,77,270/-
3	BIKANER	2,61,777/-
4	JAIPUR	1,09,853/-
5	JODHPUR	62,350/-
	TOTAL	15,60,076/-

18. **Medical Equipment procured under M&P Programme**:-

CH-JP.

M&P SANCTIONED ITEMS FOR THE YEAR 2023-24 UNDER GM POWER – CH-JP				
S.No	**Item Description**	**Year**	**Status**	**If not completed reasons**
1	CRYOTHERAPY UNIT	2023-24	NOT COMPLETED	Indent submitted on date 22.05.2024. Tender Opening Date 02/09/24 discharged , re tender awaited
2	CORDLESS ULTRASONIC DISSECTION DEVICE WITH ALL STANDARD ACESSORIES	2023-24	NOT COMPLETED	Sent to Stores for procurement on 18/09/24
3	FULLY MOTORISED ICU BEDS	2023-24	NOT COMPLETED	Indent submitted. TOD 11.3.24 bid opened.case discharged, under RT.. TOD: 12/09/24., technical bid opened

4	OPTHALMIC OPERATING MICROSCOPES	2023-24	NOT COMPLETED	indent submitted to procurement on dated - 01.10.2024
5	USG Machine with echo and pain probe for OT with all stand accessories	2023-24	Not Completed	indent submitted on dated - 01/10/2024
6	Diode Laser Machine{For Proctology & Vascular Surgery (Varicose Veins) with all standard Accessories	2023-24	NOT COMPLETED	indent awaited to md/ch/jp for final submission
7	PHYSIO THERAPY UNIT AND DENTAL UNIT IN RAIL NIKUNJ	2023-24	COMPLETED	
8.	Vitrectomy Machine with Phaco Emulsification having straight cutter.	05.01.24	45,00,000/--	

AJMER- DIVISION

	M&P SANCTIONED ITEMS FOR THE YEAR 2023-24-All			
S. No	**Item Description**	**Year**	**Status**	**If not Completed reasons**
1	LMO Tank 6000 KL	2023-24	Under processs	Indent no. NWR-051500-24-200247 dt. 19.04.2024 with DMM
2	Digital Flat Panel C-Arm 6 KW with accessories	2023-24	Under processs	Indent no. NWR-051500-24-00194 dt. 28.03.2024 with Sr. DMM
3	Hysteroscopy set	2023-24	Under processs	Indent no. NWR-051500-24-00195 dt. 28.03.2024 with Sr. DMM
4	Heavy Duty battery operated power drill with accessories for orthopaedic operations	2023-24	Under processs	Indent no. NWR-051500-24-00196 dt. 29.03.2024 with Sr. DMM

5	Anaesthesia work station for OT	2023-24	Under processs	Indent no. NWR-051500-24-00193 dt. 28.03.2024 with Sr. DMM
6	Fully Automatic Bio Chemistry Analyser	2023-24	Under process	Indent no. NWR-051500-24-00172 dt. 11.03.2024 with Sr. DMM
7	Modular Multipara monitors for OT	2023-24	Under process	Indent no. NWR-051500-24-00193 dt. 28.03.2024 with Sr. DMM
8	Single port laparoscopic tubal ligation system	2023-24	Under process	Indent no. NWR-051500-24-00176 dt. 13.03.2024 with Sr. DMM
9	CO2 Insufflator	2023-24	Under process	Indent no. NWR-051500-24-00175 dt. 12.03.2024 with Sr. DMM
10.	PFN Alfa 2 instrument set with titanium nail	16.11.2023	-	Rs. 592480

BIKANER-DIVISION

M&P SANCTIONED ITEMS FOR THE YEAR 2023-24 – BKN				
S. No	**Item Description**	**Year**	**Status**	**If not completed reasons**
1	Dental Unit	2023-24	Completed	
2	Cautery Machine	2023-24	Completed	
3	Anesthesia Work Station	2023-24	Completed	

JODHPUR DIVISION

M&P SANCTIONED ITEMS FOR THE YEAR 2023-24 –JU				
S. No	**Item Description**	**Year**	**Status**	**If not completed reasons**
1	High End USG Machine	2023-24	Not Completed	Tender uploaded by Sr. DMM/JU on 19.06.2024 and it will be opened on 11.07.2024
2	HD Camera for Laparoscopy Surgeries with HD Monitor	2023-24	Not Completed	Tender uploaded by Sr. DMM/JU on 31.05.2024 and after extended period of opened on 04.07.2024 and pending for Technical Suitability.

19. St. John's Ambulance Association:

S. No.	**Details**	**2023-24**	**2022-23**
1.	No. of classes in first Aid /Nursing	60	52
2.	No. of candidates required instruction	192	205
3.	No. of appeared for Examination	32	15
4.	No. of certificates ,Vouchers, etc.	32	15
5.	No. of certificates revalidated	32	15

19.1 Division wise position of St. John's Ambulance Brigade:

S. No.	**Division**	**Ambulance Div.**	**Nursing Div.**	**Cadets**
1.	Ajmer	01	00	-
2.	Bikaner	02	00	-
3.	Jaipur	00	00	-
4.	Jodhpur	04	01	110
		7	**01**	**110**

20. Accident Relief:

S. No.	Name of Division	SPART	ARME Scale-I	ARME Scale-II
1.	Ajmer	01	02	08
2.	Bikaner	04	00	11
3.	Jaipur	02	00	02
4.	Jodhpur	03	01	14
		10	**03**	**35**

20.1 <u>Accident Report</u>:

S. No.	Div.	Date	Brief Particulars	K*	G*	S*	O*
1.	AII	18.03.2024	Side collision of Train no. 12548 SBIB-AGC Exp. With Goods Train	NIL	NIL	NIL	NIL
2.	BKN	30.12.2023	Accident of pickup (RJ07GD3683) with train No. 14897 at Biga and PSV	0	0	0	0
3.	BKN	15.01.2024	Accident of train No.9224 with car at Deshnok	0	0	0	0
4.	JU	15.01.2024	Accident of Train no. 19224 with Scorpio at UMS yard	0	0	0	0

(Note: K*- Killed, G*- Grievous, S*- Simple, & O*- other)

Chapter-12

PERSONNEL DEPARTMENT:-

1. **Cadre and Men on Roll on NW Railway (Excluding Construction):-As on 31.3.2024**

Category	Sanctioned Strength	Men on Roll
Group 'A&B'(Excluding Construction)	725	640
Group 'C'& 'D' (Excluding Construction)	59189	48939
Total	**59914**	**49579**

2. **Gazetted Officers over NWR (Excluding Construction) :-As on 31.03.2024**

Department	HAG/SAG	SG/JAG	SS	JS/GRB	TOTAL
Administration	17	10	7	24	**58**
Accounts	8	13	9	14	**44**
Civil Engineering	10	31	26	50	**117**
Commercial	3	9	6	10	**28**
Electrical	7	16	11	13	**47**
Mechanical	10	21	8	27	**66**
Medical	7	41	24	26	**98**
Personnel	2	11	5	19	**37**
RPF	1	2	3	10	**16**
S &T	8	14	10	15	**47**
Stores	5	11	4	10	**30**
Transportation	5	12	7	14	**38**
Safety	1	8	0	5	**14**
Total	**84**	**199**	**120**	**237**	**640**

3. **Non-Gazetted staff over**

NWR(Excluding Construction):-As on 31.03.2024

Department	Group C (other than Level 1)	Level 1	Total
Administration	821	230	**1051**
Accounts	720	83	**803**
Civil Engineering	6102	7197	**13299**
Commercial	2970	164	**3134**
Electrical	3022	1157	**4179**
Mechanical	11069	1607	**12676**
Medical	545	499	**1044**
Personnel	770	88	**858**
RPF	2069	8	**2077**
S &T	1436	720	**2156**
Stores	375	248	**623**
Transportation	5358	1681	**7039**
Total	**35257**	**13682**	**48939**

4. **Staff trained during the year 2023-24:-**

Name of the Training Centre	Initial Course	Promotional Course	Refresher Course	Other Specialised Course	Total
Zonal Railway Training Institute Udaipur	4996	1212	6691	1664	**14563**
Supervisors Training Centre Ajmer	784	139	434	22	**1379**
DTTC/ABR	69	186	1207	38	**1500**
DTTC/BGKT	824	0	1082	1357	**3263**

Other Training Centres	4654	344	3679	5597	**14274**
Total	**11327**	**1881**	**13093**	**8678**	**34979**

5. PNM meetings held over NWR during calendar year 2023:-

No. of items finalized in PNM meetings are as under:

Division/ Unit	PNM with NWREU					PNM with UPRMS				
	No. of Meetings held	Opening Balance	Items Accrued	Items Finalised	Closing Balance	No. of Meetings held	Opening Balance	Items Accrued	Items Finalised	Closing Balance
JP	06	85	180	150	115	06	131	180	202	109
AII	06	139	181	173	147	06	97	178	162	113
JU	06	84	110	126	68	06	123	173	175	121
BKN	06	50	170	166	54	05	61	150	149	62
AII/WS	06	177	165	120	222	06	191	163	165	189
JU/WS	06	49	72	77	44	06	40	55	81	14
BKN/WS	05	36	119	101	54	05	24	90	64	50
AII/ST	06	76	36	41	71	06	39	33	28	44
HQ	04	104	131	156	79	04	63	113	134	42
Total	51	800	1164	1110	854	50	769	1135	1160	744

6. Redeployment of Medically decategorised/Surplus Staff:-

During 2023-24, total 139 medicallydecategorised staff have been absorbed in alternative posts.

Opening Balance as on 1.4.2023	Accrued during 1.4.2023to 31.03.2024	Finalised during 1.4.2023to 31.03.2024	Closing Balance as on 31.03.2024
4	136	139	1

7. Compassionate ground appointment cases:-

During 2023-24,tota225Compassionate Ground cases have been finalized.

Opening Balance as on 1.4.2023	Accrued during 1.4.2023 to 31.03.2024	Finalised during 1.4.2023 to 31.03.2024	Closing Balance as on 31.03.2024
49	202	225	26

8. Settlement Cases(NR & ONR):-

	Opening Balance as on 1.4.2023	Accrued during 1.4.2023 to 31.03.2024	Finalised during 1.4.2023 to 31.03.2024	Closing Balance as on 31.03.2024
NR	0	1285	1285	0
ONR	38	707	708	37

During 2023-24,total1993settlement cases have been finalized.

9. GrievancesRedressal:-

During 2023-24,Total3713grievanceshave been finalized.

Opening Balance as on 1.4.2023	Accrued during 1.4.2023 to 31.03.2024	Finalised during 1.4.2023 to 31.03.2024	Closing Balance as on 31.03.2024
20	3715	3713	22

Highlights of Personnel Department 2023-24

1. A total of 7000 Candidates received by RRB and RRC have been allotted units.
2. A total of 6518 candidates were recruited by NWR in RozgarMela.
3. For the first time in NWR, Compassionate Ground Appointment Examinations have been processed/ taken through the Centralized Computer Based Test. Results are published on an average of 2-3 days after the Examination.
4. For the first time in NWR, the selection process has been shifted to Centralized Computer Based Test and It is planned to conduct all Selections/Written Suitability/LDCE through Centralized Computer Based Test Only.
5. NWR has been entirely shifted to HRMS Grievance Module.
6. A total of 287 posts surrendered during the year 2023-24.
7. A total of 577 posts has been Redistributed during the year 2023-24.
8. Accident Free Awards are given to Retiring Employees on the day of the Retirement only which was not done earlier.
9. Upgradation of Employees from Level 07 to Level 08 has been completed. Pension Adalats were organized on 5th May, 2023 and 15th December, 2023 in all the Divisions of NWR. In all the Divisions, Workshops and Headquarters office, a total of 524 grievances were finalized out of 534.
10. A total of 76 staff has been promoted to Group" B" from Group "C" financial year 2023-24.
11. Total 5165 staff(NG) has been promoted to the next higher grade for the financial year 2023-24.

Report on Welfare activities over NWR during the year2023-2024

Staff Benefit Fund

In order to give a fillip to Staff Benefit Fund activities on this Railway, a Committee has been constituted as per the nodal provisions named as Central Staff Benefit Fund Committee. The Committee comprises of members as under:-

Ex-officio Chairman – PCPO

Secretary – Dy.CPO (Welfare)

Ex-officio Vic-President – CHD (nominee of Medical Department)

Nominated member – Dy CE (nominee of Engineering Department)

Nominated members – 03 each from both the Recognized Unions and 01 from SC/ST Association and 01 from OBC Association.

Note: Similarly, committees have been constituted at Divisional/Workshop to look after the regulation of funds allotted under SBF.

Every year funds are allotted by Railway Board on per capita basis to all Zonal Railways which are further distributed by CSBF Committee to all Divisions/Units as per laid down norms of Railway Board. The funds, in general, are allotted for the following heads:-

1. to3. **<u>Education</u> :-** For promoting Technical/Professional education among wards of employees working in Level-5 to Level-9 @ Rs.18000/-per year under which –

- Assistance to Railway employees by awarding scholarship to children/wards of Railway employees for degree in B.E./B.Tech./M.E/M.Tech., Medical-MBBS/BDS/MDS(Master of Dental Surgery)/BAMS/BHMS, B/M.Pharma, Pharma-D(Doctor of Pharmacy), BSC(Nursing), BVSAH. BSC(Agri), BCA, MCA, BBA, MBA, PGDM, Hotel Management/Bachelor of Hospitality & Tourism Management, ICWA, CA/CS/CMA, LLB, Bachelor of Yoga & Naturopathy, Bachelor in Arts in Security Management/Radiation Technology, BPT, B/M.Design/ (Architecture) /Environment Planning, Fashion Technology, BJMS, MFA (Phtography), MPT (Physiogherapy), BSC (Mechanical Engineering), MSC Maths/Microbiology @ Rs. 18000/- per year. Accordingly, during the year 2023-2024, total amount of Rs. 18954000/- was sanctioned on this head (1053 scholarship)

- Scholarship for higher education for Girl/Male children of employee working in Level-1 to Level-4 @ 18000 Rs. per year for Technical/Professional Degree/Diploma viz. B.E./B.Tech./M.E/M.Tech., Medical-MBBS/BDS/MDS(Master of Dental Surgery)/BAMS/BHMS, B/M.Pharma, Pharma-D(Doctor of Pharmacy), BSC(Nursing), BVSAH. BSC(Agri), BCA, MCA, BBA, MBA, PGDM, Hotel Management/Bachelor of Hospitality & Tourism Management, ICWA, CA/CS/CMA, LLB, Bachelor of Yoga & Naturopathy, Bachelor in Arts in Security Management/Radiation Technology, BPT, B/M.Design/ (Architecture) /Environment Planning, Fashion Technology, BJMS, MFA (Phtography), MPT (Physiogherapy), BSC (Mechanical Engineering), MSC

Maths/Microbiology. Accordingly, an amount of Rs. 2088000/- (116 scholarship) was sanctioned on this head.

4. **Recreation and Amusement:**

An amount of Rs. 2946775/- was spent under the head of Recreation and Amusement on organizing employee and children's camp.

Camps	S. No.	Place where camp held	Date of camp (From-To)	No. of Campers including officials
Employees Camp	1	Goa (HQ)	03.10.23 to 06.10.23	33
	2	Kashmir (JU)	24.10.23 to 30.10.23	20
Divyang Camp	3	Nepal (AII WS)	08.02.23 to 17.02.23	40
	4	Jaisalmer, Tanot Mata, Ramdevra (JU WS)	07.03.24 to 08.03.24	21
Children Camp	5	Nanital (HQ)	06.06.23 to 10.06.23	44
	6	Kumbhalgarh, Chittorgarh (JU WS)	27.01.24 to 28.01.24	29
Women Camp	7	Ranakpur(AII WS)	09.09.23	30
	8	Kerala, Munnar, Thekkady, Alleppey (HQ)	23.02.24 to 28.02.24	32

5. **Relief in distress and sickness etc. for staff in grade pay up to 4600 (Level-7):**

In addition to medical facilities set up by Railway administration for employees, the following welfare schemes are also carried out by CSBF on this Railway.

- Funeral assistance to the widows/dependent of deceased non gazzetted employees @ Rs. 10000/-(lump-sum).
- Financial assistance – For Railway Employees on LWP and those who are under sick list of authorized medical attendant – Assistance @ Rs 10000/- per month irrespective of their

basic pay. One time payment of Rs. 30000/- is sanctioned to the Patient under the treatment of Cancer and Kidney Transplant.

- Reimbursement of the cost of spectacles to Railway Employees – Rs.1500/- on recommendation of authorized medical attendant (under PME).
- Reimbursement as part cost of denture All non gazetted staff for purchase of artificial denture sets on the recommendation of Railway Doctor are provided with financial assistance of Rs. 8000/- for full denture set and Rs. 4000/- for half denture, once in service period.
- Financial Assistance of Rs.10000/- for braces for unmarried children of Railway Employee.
- An imprest with Medical Director of Central Hospital - for assistance to carry dead body by family of deceased employees in case of death in Railway hospital @ Rs.3000/- in each case. Imprest amounting to Rs. 30,000/- is provided.
- In addition to the above, in the case of amputation of the body of the employee, assistance is also given in cases as follows:-

i)	Rs. 60,000/-	Artificial limb
ii)	Rs. 10,000/-	One foot/One Palm
iii)	Rs. 15,000/-	Below knee of one leg/Below elbow of one hand.
iv)	Rs.20,000/-	Both feet/both Palm
v)	Rs.25,000/-	Above Knee of one leg/Above elbow of one hand.
vi)	Rs.30,000/-	Below Knee of both legs/Below elbow of both hands.
vii)	Rs.50,000/-	Above Knee of both legs/Above elbow of both hands.

In view of above, overall expenditure incurred in the head of relief in distress is Rs. 455000/-

6. **Misc.:**

- Supply of news paper for indoor patient in railway hospital, supply of refrigerator and oven for patients and their attendants, cable connection for existing Television etc. have been arranged by CSBF.
- On the occasion of Republic Day & Independence Day, fruits and biscuits were distributed to indoor patients Hospitalized in Central/Divisional Hospital of this Railway.
- Gift Packets were also distributed to the TB patients who were hospitalised in Railway Hospital on 15th Aug. & 26th January.
- Staff Cantten is running in NWR HQ for contract basis by NWR HQ Sub Committee (SBF).
- Organize International Yoga Day on 21st June 2023 by SBF.

In view of above, an amount of Rs. 905550/- sanctioned in the head of Misc.

7. **Women empowerment:**

- Financial incentive for wards of women railway employees – ward attaining 1st, 2nd& 3rd position in 10th& 12th classes have been paid @ Rs. 3000/-, 2000/- and 1500/- respectively.
- Financial assistance to ward of deceased employees in case appointment on CG cannot be given and for their wards studying, up to the standard of 12th, are paid Rs. 1500 /- per child per month, maximum two children.
- Accordingly, an amount of Rs. 2620388/- has been spent for the activities of women empowerment.

8. **Indigenous system of medical science with Homeopathy and Ayurveda:**

- On this Railway, 04 Homeopathic dispensaries at Jaipur, Bikaner, Ajmer and Jodhpur and one Ayurvedic dispensary at Jodhpur under the aegis of CSBF are under operation.
- An amount of Rs2295000/- was paid as honorarium to doctor and a sum of Rs 720000/- was spent as Cost of Medicine for homeopathic dispensaries.

9. **Railway Institutes, Clubs & Community Halls:**

- There are Thirteen Community halls for the use of staff on this Railway. All are functioning. Five Officers clubs, one each at Divisional Headquarters and one at Abu Road and 11 Active Railway Institutes for recreation of staff /officers and their families. It includes indoor sports facilities.

Division	No. of community halls	Location of community hall
Jaipur	5	Jaipur, Sikar, Phulera, Bandikui, Jagatpura -Jaipur
Ajmer	3	Abu Road, Ajmer, Udaipur
Jodhpur	2	Stores Jodhpur & near DRM Office , Jodhpur
Bikaner	3	Hanumangarh, Lalgarh, Sirsa
Total	**13**	

The list of active Institutes is as under:-

SN	Name of Division/WShop	Name & Location	No. of members
1	Jaipur Division	Rly Inst. Jaipur	60
2	Jaipur Division	Rly Inst. Phulera	380
3	Jaipur Division	Rly Inst. Bandikui	60
4	Jodhpur Division	Rly Inst. Jodhpur	470
5	Ajmer Workshop	Senior Rly Inst. Ajmer	2810
6	Ajmer Division	Bisset Rly Inst. Ajmer	2010
7	Ajmer Division	Junior Rly Inst. Aburoad	360
8	Ajmer Division	Senior Rly Inst. Aburoad	344
9	Ajmer Division	Rly Inst. Dungarpur	17
10	Ajmer Division	Rly Inst.RPZ	742
11	Bikaner Division	Rly Inst. Bikaner	523

Rs. 1800000/- has been sanctioned for the expansion of facilities in the said Community Building Institute and Club.

10. **Holiday Homes:**

On this railway, well furnished holiday homes are available at seven locations. The details are as under:-

Division	Location	No. of suites
Ajmer	Ajmer	04
Ajmer	Udaipur	16
Ajmer	Abu Road	03
Jaipur	Jaipur	08
Jodhpur	Jodhpur	04
Jodhpur	Jaisalmer	02

Bikaner	Bikaner	02
		39

11. **Trekking & Mountaineering:**
The North Western Railway is associate member of NRTMA and the employees of this Railway are participating in various programme of NRTMA.

12. **Status of Railway School during 2022-23**
On this Railway One Senior Secondary School is in operation. The location of the school is as under:-

RAILWAY SCHOOLS RUN BY NWR												
S. No.	**Name and Location of Railway Schools**	**Type of School / Boys/ Girls/ Mixed**	**State**	**Classes**	**Medium of Instruc-tion**	**No. of students studying in school**				**Sanctioned strength as on 31-03-2024**		**Affilia-ted to Central /State Educa-tion Board**
						Railway wards	**wards**	**SC wards**	**ST wards**	**Teaching**	**non teaching**	
1	Railway Senior Secondary School, Bandikui	Mixed	Rajasthan	VI to XII	Hindi and English	25	128	41	23	Prin.-1 (Gaz.) + 18 Non vacant-2 Total =20	6(+ 1vac) Total =7	CBSE
				Total		25	128	41	23			

The school in Aburoad has been completely closed from the session 2023-24. In the present one Railway Senior Secondary School, Bandikui is in operation. Apart from these, two KendriyaVidyalayas are being operated in Jaipur division at Phulera station and Bandikui station on railway land.

13. Co-operative Societies :

Following Co-operative and banking societies are functioning on NWR:

SN	Name of the society	No. of societies	No. of members
1	Co-operative Banking Society	5	30240
2	Consumer Cooperative Society	5	3403
3	Housing Cooperative Society	2	1051
4	Co-operative Labour Society	1	50

14. Cultural Activities:-

1. **Inauguration of Vande Bharat Train:-** The inauguration of Vande Bharat Train was held on 12.04.2023. Cultural programs were presented by artists from Headquaarter office during this inaugural ceremony.
2. **Job Fair:-** Job Fair was held on 13.04.2023, in Ganpati Nagar, Cricket Ground, Jaipur. A cultural program SaraswatiVandana was presented by the artists of the Headquarter office during the event.
3. **World Environment Day- Street Play:-**On the occasion of World Environment Day on 05.06.2023, a street play was organized in the courtyard of the Headquarter office. In this street play, artists from the Headquarter office participated.
4. **Railway Officers Club Jagatpura program:-** A cultural program was organized in Officer's Club Jagatpura on 13.08.2023. Various cultural programs were pressented by artists/employees of the Headquarter office.
5. **Independence Day Celebrations:-** Independence Day 2023 was celebrated in the Headquarter office premises. In this event, the national flag was hoisted by the General Manager and after

the parade, various cultural programs were presented by artists/employees of the Headquarter office.

6. **Anugunj 14th Inter-Divisional Cultural Competition:-**A 14th Inter-Divisional Cultural Competition was organized in Ajmer from 21st September 2023 to 23rd September 2023 for railway employees and their families. Participants included teams from Ajmer Division, Bikaner Division, Jaipur Division, Jodhpur Division, Ajmer Workshop, and the Headquarter office. Around 150 women/men/children participated in this competition.
7. **The Inter Railway Cultural Competition (Music):-** 2023 of South Western Railway, Hubli was organized in Hubli from 18.12.2023 to 19.12.2023. The team from Head office of this railway represented the North Western Railway in this competition.
8. **68th Outstanding Railway Service Award:-** The celebration of the 68th Outstanding Railway Service Award 2023 at the Officer's Club, Jagatpura, Jaipur was organized on 22nd December 2023. Various cultural programs were presented by artists/employees of NWR HQ office in this event.
9. **Republic Day Celebrations:-** The Republic Day Celebration-2024 was held at Ganpati Nagar, Jaipur on the headquarters level. In this event, the National Flag was hoisted by the CPO/ Admin and various cultural programs were presented by artists/employees after the parade by RPF.
10. **National Wrestling Competition:-**From 02.02.2024 to 05.02.2024, the Senior National Wrestling Competition was organized in Ganpati Nagar, Jaipur. In this competition, various cultural programs were presented by artists/employees of the head office.
11. **Stairway to Success Event:-** On 10.02.2024, an event titled 'Stairway to Success' was organized by Officer's Club, Jagatpura, featuring the workshop by Mr. Anand Kumar (Padmashree and Super 30 fame). Various cultural programs were presented by artists from the head office in this event.
12. **Sanganer Railway Station:-**On 26.02.2024, the foundation stone laying ceremony of railway projects worth 41 thousand crores was conducted at Sanganer Railway Station, Jaipur. Various cultural programs were presented by artists from the head office in this event.
13. **Women's Day:-** On the occasion of International Women's Day on 08.03.2024, a street play was organized in the premises of the Headquarter office.
14. **The All India Hindi RajbhashaNatak Utsav-2023:-** The All India Hindi RajbhashaNatak Utsav-2023, organized by North Western Railway, was held at Regional Railway Training Institute, Udaipur from 12.03.2024 to 15.03.2024. Various cultural programs were presented by the artists/employees of the Headquarter office at the closing ceremony of this competition.
15. **The Inter Railway Cultural Competition (Drama)-2023:-** The Inter Railway Cultural Competition (Drama)-2023, organized by South Eastern Railway, Kolkata, was held in Kharagpur from 18.03.2024 to 20.03.2024. The team from Ajmer Division represented North Western Railway in this competition and received the Consolation Prize.
16. **The Inter Railway Cultural competition (Dance)- 2023:-** The Inter Railway Cultural competition (Dance)- 2023, organized ny RCF, Kapurthala was held in Kapurthala from 20.03.2024 to

21.03.2024. The teams from Jaipur Division, Ajmer Division and Workshop represented North Western Railway in this competition.

17. **3rd Annual Sports Cultural Meet-** 3rd Annual Sports Cultural Meet Was organized from 29.03.2024 to 30.03.2024 in NWR Officers club, Jaipur. During this event cultural performance was given by the officers from Jodhpur, Bikaner, Ajmer and Headquarter Office.

15. Scout-Guide Activities 2023-24

Activities Organized and Participated in by Scouts and Guides during 2023-24

1. **Participation of North Western Railway in the State-Level Rally Organized by Northern Railway in New Delhi**

   From May 24 to 28, 2023, the Northern Railway Bharat Scouts and Guides organized a state-level rally in New Delhi. North Western Railway was also invited, and a 16-member team from the Bikaner division represented it, performing excellently in the rally.

2. **State Council Meeting Organized by North Western Railway State Bharat Scouts and Guides - 2023**

   On May 29, 2023, a State Council Meeting was organized with officials from all four divisions and the state. In this meeting, plans for upcoming programs for the year 2023-24 were prepared. Representatives from all four divisions and officials from the state headquarters participated. Detailed discussions were held on various important issues such as the placement of council members, selection of various officials, and increasing the census. State officials provided suggestions and instructions to ensure smooth running of Scout activities, which the divisions assured they would follow.

3. **State-Level Disaster Preparedness and Management Training Camp - Jodhpur**

   Under the directives of the North Western Railway state, a state-level disaster preparedness and management training camp was organized at the Jodhpur division from June 24 to 28, 2023. Scouts, Guides, Rovers, Rangers, and unit leaders from all four divisions (Ajmer, Bikaner, Jaipur, and Jodhpur) of North Western Railway and the state of Rajasthan participated. During the training camp, trained and qualified instructors provided important information on topics like rescue, relief, first aid, and disaster management during natural disasters and emergencies. Practical training was arranged for the participants each day, and various representatives were invited to provide information through workshops. All officials of the division participated in the closing ceremony of the training camp and encouraged the trainees.

4. **Yoga Day, June 21, 2023**

   Yoga Day was organized by the North Western Railway State Bharat Scouts and Guides in all four divisions. Scouts, Guides, Rovers, Rangers, and leaders from Ajmer, Bikaner, and Jodhpur actively participated in this event. On the occasion of International Yoga Day on June 21, a morning procession was organized to raise awareness about yoga among the general public.

5. **Independence Day Program, North Western Railway Headquarters**

   On August 15, 2023, during the Independence Day program organized by the headquarters, Jaipur, along with all four divisions, various services were provided by the North Western Railway Bharat Scouts and Guides, and they participated in cultural programs. Scouts and Guides of the North

Western Railway State Bharat Scouts and Guides actively participated in the parade organized on this occasion and performed excellently.

6. **Republic Day Program, Ganpati Nagar Railway Colony, Jaipur**

During the Republic Day program organized by the Headquarters, Jaipur along with the four divisions for the year 2023-24, the North Western Railway Bharat Scouts and Guides provided assistance and services. They also participated in cultural programs on January 26, 2024. Scouts and Guides members took part in the parade alongside the RPF contingent. Observing the Scouts and Guides' performance, the Honorable General Manager announced a cash award for their team.

7. **North Western Railway State Bharat Scouts and Guides State Council Meeting, Headquarters - Jaipur, November 9, 2023**

On November 9, 2023, a State Council meeting was held at the Headquarters, Jaipur with officials from all four divisions and the state. In this meeting, a work plan was prepared for the activities of the year 2023-24, and significant decisions were made regarding the audit charge and meal expenses of the state. During the meeting, state officials provided suggestions and instructions to all divisions to ensure smooth running of Scout activities, which the divisions assured they would follow.

8. **Participation of North Western Railway in the State-Level Rally Organized by Western Railway at Sabarmati**

From December 15 to 19, 2023, the Western Railway Bharat Scouts and Guides organized a state-level rally at Sabarmati, Ahmedabad. North Western Railway was invited, and a team from the Ajmer division represented it, performing excellently in the rally. The State Chief Commissioner of Western Railway awarded certificates and prizes to the North Western Railway for their active participation.

9. **68th Distinguished Railway Service Award Ceremony, Railway Officers Club, Jagatpura, Jaipur**

On December 22, 2023, during the 68th Distinguished Railway Service Award Ceremony organized by the Headquarters, Jaipur, the North Western Railway Bharat Scouts and Guides provided various services and assistance. Observing their cooperation, the Honorable General Manager announced a cash award for their team.

10. **20th All India Railway Jamboree, January 4-9, 2024 - Tiruchirappalli, Southern Railway**

Approximately 145 Scouts, Guides, Rovers, Rangers, and leaders from the North Western Railway participated in the 20th All India Railway Jamboree held at the Railway Grounds, Tiruchirappalli, Southern Railway from January 4-9, 2024. Representatives from all zones of Indian Railways participated in various programs and competitions during the jamboree. The Scouts and Guides from North Western Railway performed admirably and presented different cultures, tableaux, and

exhibitions from Jaipur, Ajmer, Bikaner, and Jodhpur, which were highly appreciated by other states and participants.

11. **North Western Railway State Bharat Scouts and Guides State Council Meeting, Headquarters - Jaipur, February 28, 2024**

On February 28, 2024, a State Council meeting of the North Western Railway was held at the Headquarters, Jaipur. In this meeting, dates were requested from the divisions for organizing the remaining activities of the year 2023-24 in the coming year, and instructions were issued for conducting activities on the decided dates. During the meeting, the Honorable Chairman, the State Chief Commissioner, and all officials provided instructions to the divisions to ensure the smooth running of Scout activities, which the divisions assured they would follow.

16. Sports activities:-

Performance of Players and Teams of North Western Railway

For Sports Achievements during the financial year 2023-24

No.	Event	Name of SportspersonRepresented India/Indian Railway	Game/Event	Championship Details		Medal/ Performance
				Venue	Dates	
1	Asian Games	Kiran	76 KG	Hangzhou China	23 Sept – 08 Oct 23	Bronze
		Sunil Kumar	87 KG /GR			Bronze
		Rubina	High Jump			Participate
2	SAF Games	--	--	--	--	--
3	USIC Cycling Championship	ManojJaat	Team Time Trail	Knebal Denmark	7-11 Sept 23	Participate
		ManojJaat	Ind. Time Trial			Participate
4	2023 Sr. World Wrestling Championship	MsSarita	(WW-59 Kg)	Belgrade (Serbia)	16-24 Sept 2023	Participate
		Sh. Sajan	(GR/ 77 Kg)			Participate
		Ms. Neelam				Participate
5	U-23 World Wrestling Championship	Ms. Neelam	(WW 50 Kg)	Tirana (Albania)	23- 29 Oct 2023.	Participate
6	2023 Wrestling	Ms. Sarita	(WW-59 Kg)	Astana	9 - 14 April	Participate

	Championship	Ms. Nisha	(WW-68 Kg)	(Kazakhstan)	2023	Participate
		Sh. Sajjan	(GR/ 77 Kg)			Participate
7	3rd Raking Series International Wrestling Tournament	MrSajjan	(GR/ 77 Kg)	Bishkek (Kyrgyzstan)	1- 5 June 2023.	Participate
		Ms. Sarita	(WW-59 Kg)			Participate
		Ms .Nisha	(WW-68 Kg)			Participate
8	2024 Senior Asian Wrestling Championship	ShSajaan (GR)	(GR/ 77 Kg)			Participate
		Sh. Sunil (GR)	(GR- 87 Kg)			Participate
		Ms. Anju	(WW 50 Kg)	Bishkek (Kyrgyzstan)	11- 16 April 2024	Participate
		MsSarita	(WW-59 Kg)			Participate
		MsNisha	(WW-68 Kg)			Participate
9	Asian Track Cycling Championship	Ms. Monika Jat	Time Trial	Malaysia	14 - 19 June 2023	Participate
10	43rd Asian Track Cycling Championship	Ms. Swasti Singh	Time Trial	New Delhi	21- 26 Feb 2024	Participate
11	National Wrestling Championship	Kuldeep Malik	72 KG /GR	Jaipur	02 -05 Feb 24	Gold
		Sunil Kumar	87 KG/ GR			Gold
		Anju	57 KG			Gold
		Nisha	68 KG			Gold
		Sarita	59 KG			Silver
		Neelam	50 KG			Silver
12	National Boxing Championship	Sonia	57 KG	Noida	20-27 Dec 23	Gold
		Nupur	81 + KG			Gold
13	National Track Cycling Championship	Monika Jaat	4KM Team Persuit	Ranchi	30 Nov to 04 Dec 23	Gold
		Swasti Singh	4 KM Team Persuit			Gold
		Swasti Singh	10 Km Scratch			Bronze
14	National Road Cycling Championship	Monika Jaat	In Time Trial	Karnataka	09 -12 Jan 24	Gold
		Monika Jaat	Team Persuit			Gold
		Monika Jaat	Team Relay			Gold

		Swasti Singh	Team Persuit			Gold
		Swasti Singh	Road Race			Gold
		Swasti Singh	Criturm			Gold
		ManojJaat				Participate
		Rajveer Singh				Participate
16	Open National Athletics Championship	Yamandeep	Decathlon	Bangaluru Kaarnataka	11-15 Oct 23	Gold
		Tannu	Hepthalon			Silver
		SandeepKumari	Discuss Throw			Bronze
17	National Weightlifting Championship	DipaliGurshale	45 KG	Itanagar	28 Dec 23 to 08 Jan 24	Gold
18	Handball Sr. National Championship	Pavitra	Handball	Hathras (UP)	07-03 March 24	Gold
19	National Powerlifting Championship	RekhaAcharya	69 KG	Kashipur Utrakhand	8-13 Aug 2023	Silver
		Bharat Bhushan	74 KG			Silver
		Arivalagam C	93 KG			Silver

Chapter-13

Safety Department

XIII. ACCIDENTS-

13.2 (b) No. of accidents classified under principal heads including workshop during the year 2023-24 in comparison to 2022-23 were as under:

Sr. No.	Particulars	2023-24	2022-23
1. (i)	Collision involving Passenger trains	1	Nil
1. (ii)	Collision involving other than passenger trains	0	Nil
2.(i)	Derailments involving Passenger trains	1	2
2.(ii)	Derailment involving other than Passenger trains	Nil	Nil
3.	Train wrecking	Nil	Nil
4.	Train running in to road traffic or road traffic running in to trains at level crossings	Nil	Nil
5.	Fire on trains	Nil	Nil
6.	Misc.	Nil	Nil

13.2 (d) No. of persons killed and injured in train accidents:-

Year	No. of passengers carried* (in thousands)	No. of persons killed			Killed per thousand of passengers carried*	No. of persons injured		
		Pass.	Rly.Staff	Others		Pass.	Rly.Staff	Others
2023-24		0	0	0		0	0	0
2022-23		0	0	0		71	0	0

* Figures may be taken from Commercial Department.

13.3.1 The figures of various types of accident and accidents attributed to failure of elements for 2023-24 in comparison to 2022-23 are given below:-

Consequential			
Sr. No.	**Category**	**2023-24**	**2022-23**
1.	Collisions	1	Nil
2.	Derailments		
	(i) Mid-section	1	2
	(ii) At stations	Nil	Nil
3.	Trains running into road traffic at LC	Nil	Nil
4.	Fire in trains	Nil	Nil
5.	Misc.	Nil	Nil
	Total	**2**	**2**

Indicative			
Sr. No.	**Category**	**2023-24**	**2022-23**
1.	Averted collisions	Nil	Nil
2.	Train Passing signal at danger	4	2
3.	Breach of block rules	Nil	Nil
	Total	**4**	**2**

13.3 Safety Camps:

Attendance of the important categories of train passing staff in safety camps during year 2023-24 and 2022-23.

Sr. No.		2023-24	2022-23
1.	SM/ASM	479	576
2.	Guards	378	311
3.	Drivers	629	522
4.	Diesel Asstt.	524	777

13.4 Inspections-

Sr. No.	No. of inspections	2023-24	2022-23
1.	Total No. of Foot Plate inspections	1462	1340
2.	No. of Brake Van inspections	783	852
3.	No. of inspections at stations	1960	1823
4.	No. of Level Crossing inspections	1321	1516
5.	No. of lobby inspections	387	448
6.	No. of running room inspections	378	382
7.	No. of ambush checks	1839	2004
8.	Total No. of surprise night inspections	2371	2448
9.	No. of night foot plate inspections	564	545

13.5 Special Safety Drives-

A. The following important Safety Circulars were issued during 2023-24

Safety Circular No.	Subject	Date of issue
04/2023	Keeping vehicles safe at stations	20.04.2023
05/2023	Damaged or defective vehicle	08.05.2023
06/2023	Precautions to be taken during rainy season.	12.06.2023
07/2023	Patrolling the lines	10.07.2023
08/2023	Entry of train on signal less line.	23.08.2023
09/2023	Checking of trains before departure	07.09.2023
10/2023	Checking of train by loco pilot	10.10.2023
11/2023	Bursting crackers in mist, fog or stormy weather when visibility is not clear	14.11.2023
12/2023	Control of shuttling.	07.12.2023
01/2024	Brake Van	16.01.2024
02/2024	Authority for shunting or blockage in block section	12.02.2024
03/2024	Keeping vehicles safe at the station.	14.03.2024

B. The following Safety Drives were held during 2023-24

Safety Drive No.	Subject	Rly. Board's reference letter No./ CSO/NWR's letter No.	Date of issue	Period
05/2023	Week long Safety Drive for the month of April 23	NWR/HQ/Safety/SD/5/23 RB Letter No. 2023/Safety-I/3/3 dated: 05.04.2023	06.04.2023	7 days
06/2023	Week long Safety Drive for the month of May 23	NWR/HQ/Safety/SD/6/23 RB Letter No. 2023/Safety-I/3/3 dated: 07.05.2023	08.05.2023	7 days
07/2023	Safety Drive strict observation of rules in shunting.	NWR/HQ/Safety/SD/7/23	15.05.2023	15 days
08/2023	Foot plating by CLI with nominated crew for complete beat.	NWR/HQ/Safety/SD/8/23 RB Letter No. 2023/Safety/Electrical /3 dated: 22.05.2023	23.05.2023	30 days
09/2023	Week long special safety drive on Container Trains.	NWR/HQ/Safety/SD/9/23 RB Letter No. 2023/Safety(DM) /12/1 dated: 30.05.2023	31.05.2023	7 days
10/2023	Week long safety drive.	NWR/HQ/Safety/SD/10/23 RB Letter No. 2023/Safety(Inquiries) /22/5 dated: 05.06.2023	05.06.2023	7 days

11/2023	Week long safety drive for the month of June 23	NWR/HQ/Safety/SD/11/23 RB Letter No. 2023/Safety-I/3/3 dated: 29.05.2023	07.06.2023	7 days
12/2023	Intensive 15 day's safety drive.	NWR/HQ/Safety/SD/12/23 RB Letter No. 2023/Safety-I/3/3 dated: 07.06.2023	08.06.2023	15 days
13/2023	Week long safety drive for the month of July- 23	NWR/HQ/Safety/SD/13/23 RB Letter No. 2023/Safety-I/3/3 dated: 28.06.2023	30.06.2023	7 days
14/2023	Safety Drive on Monsoon Precaution.	NWR/HQ/Safety/SD/14/23	18.07.2023	15 days
15/2023	Week Long Safety Drive for the month of Aug-23	NWR/HQ/Safety/SD/15/23 RB Letter No. 2023/Safety-I/3/8 dated: 01.08.2023	02.08.2023	7 days
16/2023	Safety Drive regarding Fire Incidences	NWR/HQ/Safety/SD/16/23 RB Letter No. 2023/Safety-1/3/3 dated : 26.08.23	27.08.2023	15 days
17/2023	Week Long Safety Drive for the month of Sep-23	NWR/HQ/Safety/SD/17/23 RB Letter No. 2023/Safety-1/3/9 dated : 07.09.23	08.09.2023	7 days
18/2023	Week Long Safety Drive for the	NWR/HQ/Safety/SD/18/23	04.10.2023	7 days

	month of Oct -23	RB Letter No. 2023/Safety-1/3/10 dated : 27.09.23		
19/2023	Winter Preparedness drive.	NWR/HQ/Safety/SD/19/23 RB Letter No. 2005/Elect(TRS)/440/23 dated 10-10-23	11.10.2023	15 days
20/2023	Intensive Safety Drive	NWR/HQ/Safety/SD/20/23 RB Letter No. 2023/Safety(Imp)/3/10/1 dated : 30.10.23	31.10.2023	15 days
21/2023	Week Long Safety Drive for the month of Nov -23	NWR/HQ/Safety/SD/21/23 RB Letter No. 2023/Safety-1/3/11 dated : 06.10.23	06.11.2023	7 days
22/2023	Week Long Safety Drive for the month of Dec -23	NWR/HQ/Safety/SD/22/23 RB Letter No. 2023/Safety-1/3/12 dated : 06.12.23	07.12.2023	7 days
01/2024	Week Long Safety Drive for the month of Jan'2024	NWR/HQ/Safety/SD/01/24 RB Letter No. 2024/Safety-I/3/1 dated: 02.01.2024	02.01.2024	07 days
02/2024	Intensive Safety Drive.	NWR/HQ/Safety/SD/02/24 RB Letter No. 2023/Safety (Imp)/3/10/2 dated: 11.01.2024	12.01.2024	15 days
03/2024	Week Long Safety Drive for the month of Feb'2024	NWR/HQ/Safety/SD/03/24 RB Letter No. 2024/Safety-1/3/2 dated 07.02.2024	08.02.2024	07 days
04/2024	Safety Drive Regarding Prevention of SPAD cases	NWR/HQ/Safety/SD/04/24	19.02.2024	15 days.
05/2024	Week Long Safety Drive for the month of March'2024	NWR/HQ/Safety/SD/05/24 RB Letter No. 2024/Safety-1/3/3 dated 20.02.2024	29.02.2024	07 days

06/2024	Safety drive for securing of stabled loads.	NWR/HQ/Safety/SD/06/24	14.03.2024	15 days
07/2024	Week long safety drive from 18.03.24 to 24.03.24 Identification of Signal with poor visibility.	NWR/HQ/Safety/SD/07/24 RB Letter No. 2024/Safety-1/3/3 dated 08.03.2024	15.03.2024	07 days
08/2024	Safety Drive Regarding Prevention of SPAD cases.	NWR/HQ/Safety/SD/08/24	22.03.2024	05 days

13. □□□□□□□□□□□

13.2 **(□)** □□□□ **2022-23** □□ □□□□□ □□□ **2023-24** □□□ □□□□ □□□□□□□□□□ □□□□□ □□□□□□□□□ □□ □□□□□ □□ □□ □□□□□□ □□

□□ □□□□□ □□□□□□□□ □□□ □□□□□□□□ □□ □□ □□□ –

□□□□ □□□□ □□	□□□□□	2023-24	2022-23
1.	□. □□□□□□ □□□□ □□ □□□□□ □. □□□□□□ □□□□ □□□□ □□ □□□□□	1 □□□ □□□□	□□□ □□□□ □□□ □□□□
2.	□. □□□□□□ □□□□ □□ □□□□□ □. □□□□□□ □□□□ □□□□ □□ □□□□□	1 □□□ □□□□	2 □□□ □□□□
3.	□□□□ □□□□□□□□□□□ □□□□	□□□ □□□□	□□□ □□□□
4.	□□□□□□ □□ □□□□ □□ □□□ □□□□□□ □□ □□□□□□	□□□ □□□□	□□□ □□□□
5.	□□□□□□□ □□□ □□	□□□ □□□□	□□□ □□□□
6.	□□□□□	□□□ □□□□	□□□ □□□□

13.2 (□) □□□□□ □□□□□□□□□□□□ □□□□ □□□□ □ □□□□□ □□□□□□□□□□□□ □□ □□□□□□□ –

□□□□	□□□□ □□□□□ □□ □□□□□□□ □□□□ □□ □□□□□□□ *(□□□□□□□ □□□□)	□□□ □□□□□□□□□□□ □□ □□□□□□□			□□□□□□□□□□ □□□□□ □□□□ □□□□□□□ □□ □□□□□□□ □□□□ □□ □□□□□□□ *□□	□□□□□ □□□□□□□□□□□□ □□ □□□□□□□			□□□□□□□□□□ □□□□□ □□□□ □□□□□ □□ □□□□□□□□□□ □□ □□□□□□□ □□ □□□□□□□ *
		□□ □□ □□	□□□□□□ □□□□□ □□□□□	□□□□ □		□□ □□ □□	□□□□□□ □□□□□ □□□□□	□□□□□	
2023-24		0	0	0		0	0	0	
2022-23		0	0	0		71	0	0	

- □□□□□□ □□□□□□□□ □□□□□□ □□ □□□□ □□ □□□□□ □□□□ 1

13.3.1 □□□□□ 2022-23 □□ □□□□□□ □□□□ 2023-24 □□□□ □□□□□ □□□□□□□□ □□□□□□□ □□ □□□□□□□□□□□□ □□□□□ □□ □□□□ □□□□ –

□□□□□ □□□□□□□	□□□□□	2023-24	2022-23
□□□□□□□□ □□□□□□□□□□□□			
1.	□□□□□□□□□	1	□□□ □□□□□
2.	□□□□□□ □. □□□□ □□ □□□□□ □. □□□□□□□ □□	1 □□□ □□□□□	2 □□□ □□□□□
3.	□□□□□□□ □□ □□□□□ □□ □□□□ □□□□□□□□ □□ □□□□□□□	□□□ □□□□□	□□□ □□□□□
4.	□□□□□□□□□ □□□□ □□	□□□ □□□□□	□□□ □□□□□
5.	□□□□□□	□□□ □□□□□	□□□ □□□□□
□□□		2	2

□□□□□□□□□□□□ □□□□□□□□□□□ -

□□□□□ □□□□□□□	□□□□□	2023-24	2022-23
1.	□□□□□□□□ □□□□□□□□	□□□ □□□□	□□□ □□□□
2.	□□□□ □□ □□□□ □□ □□□□□ □□ □□ □□□□	4	2
3.	□□□□□ □□□□□□ □□ □□□□□□□	□□□ □□□□	□□□ □□□□
□□□		4	2

13.3 □□□□□□□□ □□□□□ –

□□□□ □□□□□ □□ □□□□□□□□ □□□□□□□□□□ □□□□□□□ □□ □□□□□□□□□□ □□ □□□□ 2023-24 □□□ 2022-23 □□□ □□□□□□□ □□□□□ □□□ □□□□□□□□ -

		2023-24	2022-23
1.	□□□□. □□./□.□□□□. □□.	479	576
2-	□□□□□	378	311
3-	□□□	629	522
4-	□□□□ □□□□□	524	777

13.4 □□□□□□□□□ -

□□□□ □□□□□□	□□□□□□□□□ □□ □□□□□□□	2023-24	2022-23
1.	□□□ □□□□□□□ □□□□□□□□□	1462	1340
2-	□□□□□□□□□ □□□□□□□□□	783	852
3.	□□□□□□□ □□□□□□□□□	1960	1823
4.	□□□□□□□□ □□ □□□□□□□□□	1321	1516
5.	□□□□□ □□□□□□□□□	387	448
6.	□□□□□□ □□□ □□□□□□□□□	378	382
7.	□□□□□□□ □□□	1839	2004
8.	□□□□□□□□ □□□□□□ □□□□□□□□□	2371	2448
9.	□□□□□□□ □□□□□□□ □□□□□□□□□	564	545

13.4 □□□□□ □□□□□□□ □□□□□□ –

(□) □□□□ 2023-24 □□ □□□□□ □□□□□□□□□□ □□□□□□□□□□ □□□□□□□□ □□□□□□□□ □□□□ □□□□ □□ □□-

□□□□□□□□ □□□□□□□ □□□□□□	□□□□	□□□□ □□□□ □□ □□□□□□□
04/2023	□□□□□□□□□ □□ □□□□□ □□ □□□□□□□□ □□□□□	20.04.2023
05/2023	□□□□□□□ □□ □□□□□□□□ □□□□□	08.05.2023
06/2023	□□□□□□ □□□ □□□ □□□□ □□□□ □□□□ □□□□□□□□□□□	12.06.2023

07/2023	□□□□□□□ □□ □□□□□ (□□□□□□□□□□□□) □□□□□□□	10.07.2023
08/2023	□□□□□□ □□□□□ □□□□□ □□ □□□□□ □□ □□□□□□□ □	23.08.2023
09/2023	□□□□□□□□□□ □□□□□ □□ □□ □□□ □ □□ □□ □□□□ □□ □□□□□□	07.09.2023
10/2023	□□□□□ □□□□□□ □□□□□□□ □□□□□ □□□ □□□□□□	10.10.2023
11/2023	□□□□□, □□□□□□ □□ □□□□□□□ □□□□□ □□□□ , □□ □□□□□□□ □□□□□□ □□□□□ □□□□□ □□ □□□□□□ □□□□□□	14.11.2023
12/2023	□□□□□□□ □□ □□□□□□□□□□	07.12.2023
04/2023	□□□□□□□□ □□ □□□□□□ □□ □□□□□□□□□□ □□□□□□	20.04.2023
01/2024	□□□□□□□□□□	16.01.2024
02/2024	□□□□□□ □□□□□□□ □□□□ □□□□□□□ □□ □□□□□□ □□ □□□□ □□□□□□□□□□	12.02.2024

(□) □□□□□ **2022-23** □□□□ □□□□□□□□□□ □□□□□□□□ □□□□□□□ □□□□□ □□ □

□□□□□□ □□ □□□□□□ □ □□□□□ □□	□□□□□	□□□□□□ □□□□□ □□ □□□□□□□□□□ □□□□□ □□□□□□□ /□□.□□. □./ □.□.□□. □□ □□□□□ □□□□□□□	□□□□□ □□□□□ □□□□□ □□ □□□□□□□	□□□□
05/2023	□□□□□□□ 23 □□□□ □□ □□□□ □□□□□□□ □□ □□□□□ □□□□□ □□□□□□□□ □□□□□□□	□□□□□/□□□□□□/□□□□□□□□□/□□. □./5/23 □□.□□. □□□□□ □□. 2023/□□□□□□□□-I/3/3 □□□□□□□ 05.04.2023.	06.04.2023	7 □□□□
06/2023	□□ 23 □□□□ □□ □□□□ □□□□□□□ □□ □□□□□ □□□□□ □□□□□□□□ □□□□□□□	□□□□□/□□□□□□/□□□□□□□□□/□□. □./6/23 □□.□□. □□□□□ □□. 2023/□□□□□□□□-I/3/3 □□□□□□□ 07.05.2023.	08.05.2023	7 □□□□
07/2023	□□□□□□□ □□ □□□□□□□ □□ □□□□□□□ □□ □□□□□ □□□□□ □□□□□ □□ □□□□□□□□ □□□□□□□	□□□□□/□□□□□□/□□□□□□□□□/□□. □./7/23	15.05.2023	15 □□□□

08/2023	□□□□□ □□□□ □□ □□□□ □□□ □□ □□ □□ □ □□□□ □□□□□□□□ □□ □□ □□ □□□□□□ □□ □□ □□ □ □	□□□□/□□□□□/□□□□□□□□/□□. □./8/23 □□.□□. □□□□ □□. 2023/□□□□□□□□/□□□□□/3 □□□□□□ 22.05.2023.	23.05.2023	30 □□□
09/2023	□□□□□□ □□□□□ □□ □□□□□□ □□ □□□□ □□□□ □□□□□ □□□□□□□ □□□□□□	□□□□/□□□□□/□□□□□□□□/□□. □./9/23 □□.□□. □□□□ □□. 2023/□□□□□□□□/(□.□□□.)/12/1 □□□□□□ 30.05.2023.	31.05.2023	7 □□□
10/2023	□Ü□□□ □□ □□□□ □□□□ □□□¢□ □µ□□□□	□□□□/□□□□□/□□□□□□□□/□□. □./10/23 □□.□□. □□□□ □□. 2023/□□□□□□□□/(□□□□□)/22/5 □□□□□□ 05.06.2023.	05.06.2023	7 □□□
11/2023	□□□ 23 □□□ □□ □□□ □□□□□□ □□ □□□□ □□□□ □□□□□□□ □□□□□□	□□□□/□□□□□/□□□□□□□□/□□. □./11/23 □□.□□. □□□□ □□. 2023/□□□□□□□-I/3/3 □□□□□□ 29.05.2023.	07.06.2023	7 □□□
12/2023	15 □□ □□□ □□ □ □ □ □ □□ □□ □□ □ □□ □□ □	□□□□/□□□□□/□□□□□□□□/□□. □./12/23 □□.□□. □□□□ □□. 2023/□□□□□□□-I/3/3 □□□□□□ 07.06.2023.	08.06.2023	15 □□□
13/2023	□□□□□ 23 □□□ □□ □□□ □□□□□□ □□ □□□□ □□□□ □□□□□□□ □□□□□□	□□□□/□□□□□/□□□□□□□□/□□. □./13/23 □□.□□. □□□□ □□. 2023/□□□□□□□-I/3/3 □□□□□□ 28.06.2023.	08.06.2023	15 □□□
14/2023	□□□□□□ □□□□□□□□ □□□□□□□□□□ □□ □□□□□□□ □□□□□□	□□□□/□□□□□/□□□□□□□□/□□. □./14/23	18.07.2023	15 □□□

15/2023	□□□□□ 23 □□□ □□ □□□ □□□□□□ □□ □□□□ □□□□ □□□□□□□ □□□□□□	□□□□/□□□□□/□□□□□□□/□□. □./15/23 □□.□□. □□□□ □□. 2023/□□□□□□□-I/3/8	02.08.2023	7 □□ □
		□□□□□□ 01.08.2023		
16/2023	□□ □□□□ □□ □□□□□□ □□ □□□□□ □□ □□□□□□□ □□□□□□	□□□□/□□□□□/□□□□□□□/□□. □./16/23 □□.□□. □□□□ □□. 2023/□□□□□□□-I/3/3 □□□□□□ 26.08.2023.	27.08.2023	15 □□□
17/2023	□□□□□□□ 23 □□□ □□ □□□ □□□□□□ □□ □□□□ □□□□ □□□□□□□ □□□□□□	□□□□/□□□□□/□□□□□□□/□□. □./17/23 □□.□□. □□□□ □□. 2023/□□□□□□□-I/3/9 □□□□□□ 07.09.23	08.09.2023	7 □□□
18/2023	□□□□□□□ 23 □□□ □□ □□□ □□□□□□ □□ □□□□ □□□□ □□□□□□□ □□□□□□	□□□□/□□□□□/□□□□□□□/□□. □./18/23 □□.□□. □□□□ □□. 2023/□□□□□□□-I/3/10 □□□□□□ 27.09.23	04.10.2023	7 □□□
19/2023	□□□□□□□□ □□□□□□□□□ □□ □□□□□□□ □□□□□□	□□□□/□□□□□/□□□□□□□/□□. □./19/23 □□.□□. □□□□ □□. 2005/□□□□□(□□ □□ □□)/440/23 □□□□□□ 10.10.23	11.10.2023	15 □□□
20/2023	□□□ □□□□□□□ □□□□□□	□□□□/□□□□□/□□□□□□□/□□. □./20/23 □□.□□. □□□□ □□. 2023/□□□□□□□ (□□ □□ □□)/3/10 □□□□□□ 30.10.23	31.10.2023	15 □□□
21/2023	□□□□□□ 23 □□□ □□ □□□ □□□□□□ □□ □□□□ □□□□ □□□□□□□ □□□□□□	□□□□/□□□□□/□□□□□□□/□□. □./21/23 □□.□□. □□□□ □□. 2023/□□□□□□□-I/3/11 □□□□□□ 06.10.23	06.11.2023	7 □□□

22/2023	□□□□□□□□ 23 □□□□ □□ □□□□ □□□□□□□ □□ □□□□□ □□□□□ □□□□□□□□ □□□□□□□	□□□□/□□□□□□/□□□□□□□□/□□. □./22/23 □□.□□. □□□□ □□. 2023/□□□□□□□□/I/3/12 □□□□□□ 06.12.23	07.12.2023	7 □□□
01/2024	□□□□□□ 24 □□□□ □□ □□□□ □□□□□□□ □□ □□□□□ □□□□□ □□□□□□□□ □□□□□□□	□□□□/□□□□□□/□□□□□□□□/□□. □./01/24 □□.□□. □□□□ □□. 2024/□□□□□□□□/1/3/1 □□□□□□ 02.01.2024	02.01.2024	07 □□□
02/2024	□□□□ □□□□□□□□ □□□□□□□	□□□□/□□□□□□/□□□□□□□□/□□. □./02/24 □□.□□. □□□□ □□. 2023/□□□□□□□□(□□ □□ □□)/3/10/2 □□□□□□□ 11.01.2024	12.01.2024	15 □□□
03/2024	□□□□□ 24 □□□□ □□ □□□□ □□□□□□□ □□ □□□□□ □□□□□ □□□□□□□□ □□□□□□□	□□□□/□□□□□□/□□□□□□□□/□□. □./03/24 □□.□□. □□□□ □□. 2024/□□□□□□□□-I/3/2 □□□□□□ 07.02.2024	08.02.2024	07 □□□
04/2024	□□□□□ □□□ □□□□□□ □□ □□□□□□□□ □□ □□□□ □□□□□ □□ □□□□□□ □□□□□□ □□ □□□□ □□□□□□□□ □□□□□□□	□□□□/□□□□□□/□□□□□□□□/□□. □./04/24	19.02.2024	15 □□□
05/2024	□□□□□□ 24 □□□□ □□ □□□□ □□□□□□□ □□ □□□□□ □□□□□ □□□□□□□□ □□□□□□□	□□□□/□□□□□□/□□□□□□□□/□□. □./05/24 □□.□□. □□□□ □□. 2024/□□□□□□□□-I/3/3 □□□□□□ 20.02.2024	29.02.2024	07 □□□
06/2024	□□□□□□ □□□□ □□ □□□□□□□□□ □□□□□ □□ □□□□ □□□□□□□□ □□□□□□□	□□□□/□□□□□□/□□□□□□□□/□□. □./06/24	14.03.2024	15 □□□
07/2024	18.03.2024 □□ 24.03.2024 □□ सिग्नल की कम दृश्यता की □□□□□□ □□ □□□□□□□ □□ □□□□□ □□□□□ □□ □ □□ □□ □ □□ □□ □	□□□□/□□□□□□/□□□□□□□□/□□. □./07/24 □□.□□. □□□□ □□. 2024/□□□□□□□□-I/3/3	15.03.2024	07 □□□

		□□□□□□ 08.03.2024		
08/2024	□□□□ □□ □□□□□□ □□□ □□□□□□□□ □□ □□□ □□□□ □□ □□□□□ □□□□□ □□ □□□ □□□□□□□ □□□□□ I	□□□□/□□□□□/□□□□□□□/□□. □./08/24	22.03.2024	05 □□□

Chapter-14
Security Department

01. □□ □□ □□□□□□□ □□□ □□□□:-

□□ □□ □□□□□□□ □□□ □□□□- □□□□ 2023-24 □□ □□□□□ □□□□□ □□□□□□□ □□, □□□□□□□ □□ □□□□□□□ □□□□□ □□□□□□□ □□ □□□□□□□□ 1987 □□ □□□□ 158 (□□□ □□□-51) □□□ 153 (□□□□□ □□□-29) □□ □□□ □□□□□□□□□□□□ □□□□□□□□ □□ □□ □□□□□□□ □□ □□□□□□ □□□□ □□□ □□ I

2 . □□□□ 2023-24 □□□ □□ □□□□□□□ □□ □□□□□□□□□ □□□□ □□□:-

□ □ □□ □□ □□□□□ □□ □□□□□□□ □□□□□□ □□ □□□□□□□□□ □□□□□□ □□□□□□□□, □□□□□ □□□ □□□□□□ □□□ □□□□□□, □□□□ □□□ □□□□□□□□□ □□□□□□ □□□□ □□□

□□□□□ □□□□□ □□□□□□□□□□□ □□-

□□□.□□.	□□□□□□□□□	□□□.□□.	□□□□□	□□□□□□□	□□□□□	□□□□□□	□□□.□□.□□.□□□□□□□□	□□□
01	□□□□□□□□□□ □□□□□□□□□	-	-	-	-	-	-	-
02	□□□□□□□□□	8	**04**4	19	27	20	**0**1	119
03	□□□□□□□□□	04	**0**24	27	33	23	**05**	116
04	□□□□	05	381	**1**33	420	**2**83	32	**125**4
05	□□□	17	449	181	480	326	38	148**9**

□□□□□□□ □□□□ 2023-24 □□□ □□□□□ □□ □□□□□□□□□□

3. □□□□□□□ □□□□ 2023-24 □□□ □□□□□□□ □□□ □□□ □□□ □□□□□□□ □□ □□□□ □□ □□□□□□□□

□□□□□□□□	□□□□	□□□□□ □□ □□□□□□		□□□□□□□ □□ □□□□		□□□□□□□□ □□□□□□□		
	2024-25	□□□□	□□□□ □□	□□□□□ □□□	□□□□□□□	□□□□□	□□□ □□□□□	□□□□□
□□□□□□□		**05**	**2**	**1602089**	**1483124**	**12**	-	**-**
□□□ □□□□□□□		120	11**5**	**7193673**	**5939014**	**339**	0**8**	**-**
□□□ □□□		**12**5	**11**7	8795762	7422138	351	08	-

□□□ □□□□□□□ (□□□□ □□□□□) □□□□□□□ 1966 □□ □□□ □□□□ □□ □□□□□□ :-

□□□□	□□□□□□□ □□□□□	□□□□□ □□□□□□□ □□ □□□□□	□□□□□□□□		
			□□□□□	□□□ □□□□□	□□ □□ □
20**23-24**	**125**	**7422138**	**351**	**08**	**-**

04. □□□□□□ □□□□□□□ :-

01. □□□□□□□ □□□□□ □□□□ 139- □□□□ 202**3**-2**4** □□□ □□□□□□ □□□□□ □□□□□, □□□□□□ □□□□ □□ □□□ □□□□, □□□□□□□, □□□□□□□□□

□□ □□□ □□□□ □□□□, □□□□□□□ □□□□□ □□□

□□□□□□□□□ □□□□□□□□□□ □□ □□□□□□□ □□□□□□ □□□□□ □□□□□□□, □□□□□□□ □□ □□□□□□ □□□□□□ □□□□ □□□ □□ □□□□□□□□ □□□-**17130** (□□□□□□□ /□□□□□□ □□□□□ □□□□□ □□ □□□□□□□□) □□□□□□□□ □□□□□□□ □□□ □□ **।** □□□□□ □□□□□□□ □□□□□□□□□□ □□□□□ □□□□ □□□ **।**

02. □□□□□/ □□□□ □□□□ 202**3**-**24** □□ □□□□□ □□□□ □□□□□ □□□□□ □□ □□□ 16 □□□□□ □□□□□□□ □□ □□□□□□□ □□ □□□□□ □□□□□□□□□ □□ □□□□□□□ □□ □□ □□□□□ □□□□□ □□□

□□□□ □□□□□□□□□□□□□ □□□ □□□□ □□□□ **6744** □□□□□ □□□□□□□ □□□ □□□□□ □□□□□ □□□□□ □□□□□□ 87696 □□□□□ □□□□□□□□□ □□ □□□□□ □□ □□□□□□ □□□□□□ □□□□ □□□ □□□□□□

□□□□□ □□ □□□□□□□□ □□□□□□ □□ □□□□□ □□□□□□□□□ □□□ □□□□□ □□ □□□□□ □□□□□□□ □□□ □□□□□□□ □□ □□□ □□□□□ □□□□ **।**

03. □□□□□□ □□□□□□□ □□□□□□□ :- □□□□ □□□□□ □□ □□□ □□□□□□ □□□□□□□□ □□ □□□□□□ □□□□□□□ □□□□□□□ □□ □□□ □□□□□□ □□□□□□□ □□ □□□□□□□ □□□ □□□ □□□□□□ □□□□□□□□ □□ **cctv** □□□□□, **UVSS,** □□□□□ □□□□□□, □□□□□□□□ □□□□□□□□ □□□ □□□□□□□ □□ □□□ □□□□ □□□ □□ **।** □□□□□□□□ □□□□□□ □□ □□□□□ □□ □□□□□□□□ □□□□□□□□□□ □□ □□□□□□□□ □□□□□□ □□ □□□ □□□□ □□ □ □□□□ □□□□□□□ □□□□□□ □□□□□□□□□□ □□ □□□ **।**

04. □□□□□ □□□□□:- □□□□ □□□□□ □□ □□□□□, □□□□□□, □□□□□□□, □□□□□, □□□□□, □□□□□, □□□□□□ □□□ □□□□□□ □□□□□□□□ □□ □□□□□ □□ □□□□□□□□□□ □□□□□□

□□□□□□ □□□□□□ □□, □□□□□□□ □□□ □□ □□□□□□□□ □□□□□□, □□□□□ □□□□□□ □ □□□□□□□□ □□□□□□□ □□□ □□ □□□□ □□□ □□□ □□□□ □□□□ □□ **।**

05. □□□□□□ □□ □□□□□□□□□□ :-

□□□□ 202**3**-**24** □□ □□□□□ □□□□ □□□□□□ □□ □□□□□□□:-

□□□.□□.	□□□□□	□□□□□□
01	□□□ □□□□ □□ □□□□□□	-
02	□□□ □□□□ □□□ □□□□ □□□□□□□□	0**4**
03	□□□ □□□□ □□ □□□□□ □ □□□ □□□□□	-
04	□□□□ □□□□□□□ □□ □□□□□ □□□ □□□□ □□ □□□□	-
05	□□□/□□□ □□□□□ □□□ □□□□□□□ □□□□□□□	-
06	□□□□□ □□□□□□ □□□□ □□□□□ □□ □□□□	-

06. □□□□ 202**3**-2**4** □□ □□□□□ □□□□□ □□ □□□□□ □□□□□□□□□□

□□□.□□.	□□□□□
1.	□□□□□ □□□□□□ □□ □□□□ □□□ □□□□□□□□ □□□□□□□□ :- 3**51** □□□□□ □□□□□□□ □ **08** □□□ □□□□□ □□ □□□ □□□□□□□ □□ □□□□ □□□ □□□□□□□□ □□ □□□□□ **74,22,138/-** □□ □□□□□ □□□ □□□□□□□ □□ □□□□□□□ □□ □□ **।**
2.	□□□ □□□□ □□□ □□□□□□□ □□□ □□ □□□□ □□ □□□□□ □□□□□□ □□□□ □□ □□□□□□□□□□:- 3**064** □□□□□□□□□□ □□ □□□ □□□□ □□□ □□□□□□□ □□□ □□ □□□□ □□ □□□□□ □□□□□□ □□ □□□□□ □□□ □□□□□□□□ □□ **13,99,260/-** □□ □□ □□□□□□□□ □□□□ □□□□ □□□ **।**
3.	□□□□□□□ □□□ □□ □□□□ □□□□□ □□□□ □□□□□□/□□□□□ □□ □□□□□□□□□□ :- **5708** □□□□□□□□□□ □□ □□□□□□□ □□□ □□□□ □□□□□ □□□□□ □□□□□□□ □□□□□ □□□□ □□□□□□/□□□□□□□ □□ □□□□□□□□ □□ **90,02,014/-** □□□□□ □□ □□□□□□□□ □□□□ □□□□ □□□ **।**
4.	□□□ □□□□ □□ □□ □□ □□□□□□ □□□□ □□□□ □□ □□□□□□□□□□:- **709** □□□□□□□□□□ □□ □□□ □□□□□□□ □□ □□ □□ □□□□□□ □□□□ □□ □□□□□ □□□ □□□□□□□□ □□ □□□□ **95,555/-** □□□□□ □□□□□□□□ □□□□ □□□□ □□□ **।**
5.	□□□□□□□ □□□□ □□□□□□ □□ □□□□□□□ □□□□□□□□□□:- □□□□□□□ □□□□□□ □□ □□□□□□□ □□□□□□□□□ □□□□ □□□ **153** □□□□□ □□□□□□□ □□□□ □□ □□□ **180** □□□□□□□□ □□ □□□□□□□□ □□ □□□□□□□ □□□ □□□ □□□□ □□□ **।**
6.	□□□□□□ □□□□□ □□□ □□□□□□ □□□□□□□□□ □□ □□□□□□:- □□□□ **2023-24** □□ □□□□□ □□□□□ □□□□□ □□□□□□ □□□□□□ □□□□□ □□□ □□ □□□□□□ □□ □□□ □□□□□□□□□□ □□ □□□□ □□□□□□ □□□□□ □□□□ □□ □□□□□□□□□□ □□□□□□□□ □□□□□□ □□□□□ □□ **।** **1.** □□□□□□□□□□ □□ □□□□□□ □□□□□ □□□ □□ □□□□□□ □□□□□□ □□ □□ **-5826** **2.** □□□□□□□□□□ □□ □□□□□ □□□□ □□ □□□□□□ □□□□□□ □□ □□□ **-168** **3.** □□□□□ □□□□□□□□□□ □□ □□□□□□□□ □□□□□□ □□□□□□ □□□ **-113** **4.** □□□□□□□ □□□□□ □□□ □□□□□□ □□ □□□□ □□□□□□□□/□□□□□ □□ □□□□□□□ □□□□ □□□ **-602**
7.	□□□ □□□□□□□ □□□□□□□ □□□□□□□□□□□□ :- **Reg.** | **Arrested** | **Prosecuted** | **Convicted** | **Amount** **27433** | **27272** | **25701** | **25475** | **1,02,23,362**
8.	□□□□□ □□□□□□ □□□□□□□□□□ □□ □□□□ □□□ □□□□□ □□ □□□□□□□□□□ □□ □□□□□:- □□□□□ □□□□□□ □□□□□□□□□□ □□ □□□□□□□ □□□□ □□ □□□□□ □□ □□□□□□□- **1514** □□□ □□□□ **2,73,76,688/-** □□□□□ (□□ □□□□, □□□□□□□ □□□, □□□□□□□ □□□□ □□ □□ □□□□□□) □□□□□

9.	□□□□□□ □□□□□ □□ □□□□ □□ □□□□□ □□□□□□ □□□□□:- □□□□□ □□□□□□ □□□□□□ □□□□□ □□ □□□□ □□□ □□□□ □□ □□□□□□□□□ □□ □□□□□□ (□□□□□□ □□ □□□□□□□ □□□□ □□ I) 98 □□□□□ I

Chapter -15

□□□□□□□ □□□□□

1. □□□□□□□ □□□□□□ □□ □□□□□□□□□□ □□□□□□ –

□□□. □□.	□□	□□□□□□□	□□□□□□□	□□□□□
1.	□□□□□ □□□□□□□ □□□□□□□	□□□□□□ □□□□□ □□□□□□□□ □□ □□□□□ □□□ □□□ □□□।		
2.	□□□□□□ □□□□□□□ □□□□□□□	02	01	01
3.	□□□□□□□ □□□□□□□	05	01	04
4.	□□□□□□ □□□□□□□	18	17	01
5.	□□□□□□ □□□□□□□	22	09	14

* □□□ – □□□□□ □□□□ □□ □□□□ □□ □□□□□□□□□ □□ □□ □□□ □□।

2. □□□□□□□ □□□□□ –

□□□ □□ □□□□□□□ □□□□ □□□□□□□□ □□ □□□□□□□□□ □□ □□□□□□ □□ □□□□□□□ □□□□□ □□ □□□□□□□ □□ □□ □□। □□ □□□□□ □□ □□□□ □□□□□, □□□□□ , □□□□□□ □ □□□□□□□ □□□□ □□□ □□□□□ ,□□□□□□ □ □□□□□□□ □□□□□□□, □□□□□□□□□ □□□ □□□□□□□□□ □□□□□□ □□□□□ □□□ □□ □□□□□ □□□□□□□ □□□□□□□ □□□□□□□□, □□□□□ □□□ □□□। □□ □□□□□ □□□□□□□□□ □□□□□ □□ □□□□□ □□□□□□□□ □□□□□□□ □□ □□□□□□□□□ □ □□□□□□□□□ □□□ □□□□□ □□□□ □□□। □□□□□□□ □□□ □□□□ □□□□□□□□ □□□□, □□□□□□ □□□□□ □□□□□□□□ □□□□□□□ □□□□ □□ □□ □□□□□□□□□ □□ □□□-□□□ □□□□□ □□□□□□□ □□□□□□□ □□ □□ □□ □□□□□ □□ □□□ □□□ □□ ।□□□□□□, □□□□□□□□□ □□□ □□□ □□ □□□□□□□ □□□□ □ □□□□□□□□□ □□ □□□□□ □□ □□ □□□□□ □□□□□□ □□□□□□□□□□ □□□□ □□□□ □□। □□ □□□□□ □□ □□□□ 2023-24 □□ □□□□□ □□□□□□ □□□□□□ □□□ □□□□□ □□ □□□□□□-□□□□□□ □□ □□□□□ □□ □□□ □□□□ □□□□□ □□□□ □□। □□□□□□□ □□ □□□□□□□□□ □□□□□□ □□ □□□□□ □□ □□□ □□ □□□□□ □□□□□□ □□□□□ □□ □□□□□□□ □□□□□-□□□□□□ □□ □□□□□□□□□ □□□□□ □□□□□□□□□□□ □□:-

3. □□□□□ □□□□□□□□□□□□/ □□□□□□□□□ □□ □□□□□□-

□□□□□ □□□□ □□ □□□□□□□-□□□□□□ □□ □□□□□ □□□ □□□□□□□□□□□□/ □□□□□□□□□ □□ □□□ □□□□□□ □□□□ □□ □। □□ □□□□□□□ □□ □□□□□ □□□□□□ □□□□□ □□ **51** □□□□□ □□□□□□□□□□/□□□□□□□ □□□ □□□□□ □□□□ □□□□□□ □□□□□ □□□□□□□ □ □□□□-□□□□□□□□□ □□□□□□ □□□। □□□□□□□□□□ □ □□□□□□□□□□□ □□ □□□□□□ □□ □□□ □□□□□□ □□□□□□□ □□ □□□□□□□□ □□□□ □□□□□□□ □□□□□ □□ □□□□□□ □□□□ □□ □□□□□□ □□□ □□ □□□ □□ □□ □□ □□□□ □□□□□ □□□ □□□ □□□ □□□।

4. □□□□□□□□□□ □□ □□□□□□ □□ □□□□□□ □□□□□ □□□□□ □□□ □□□□ –

□□□□□ □□□□□□□□□□□□ □□ □□□ □□□ □□□□□□□□□□ □□ □□□ □□ □□□□□ □□। □□□ □□□□ □□□□ 3348 □□□□□□□□ □□, □□□ □□□□□□□□□□ □□□ □□□□□- □□□□□□□□ □□□□□□□□ □□□ □□□□□□□ □□□ □□□ □□□□ □□ □□□□□□ □□□□□□ □□। □□□□□□□ □□□□□□□□ □□□□□□□□ □□ □□□□□□□□□□□□□ □□□□□ □ □□□□□□□□ □□□ □□□ □□□□ □□□। □□□ □□□□□□□□□□□ □□ □□□□□ □□□□□□□ □□ □□□□□ □□□□ □□□□ □□, □□□□□□□ □□□□□□□□ □□□□□□ □□□□□ □□□□□□□ □□ □□□□□□□□□□ □□□□ □□□□ □□□।

5. □□□□□□□ □□□□□□□□□□□□ □□□□□□□□ □□ □□□□□□ □□ □□□□□□□ □□□□□-

□□□□□□□ □□ □□□□□□ □□□□□□□□□ □□□□ □□□ □□□□□□ □□□ □□□□ □□□□□□□ □□□□□□ □□ □□□□□□ □□ □□ □□□□□ □□ □□□□ 49 □□□□□□□ □□□□□□□□□□□ □□□□□□□□ □□ □□□□□ □□□□□□ □□□ □□ □□□□□□ □□ □□ □□□ □□ □□ □□ □□□□□ □□□ □□□ □□ □□□□□□□□ □□ □□□□□□□□ □□□□□□□□□□ □□ □□□□□□ □□□□□□□□□□□□ □□□□□ □□□□ □□ ।

6. □□□□□□□ □□□□□ □□□□□□ □□□ □□□□□□□ □□□□□□□□□□□ □□□□□ (□□□□□□□□-2) □□ □□□□□ □□□□□□□ □□ □□□□ □□□ □□ □□□□□□ □□□□ □□ □□□ □□।□□□□ □□□□□□ □□□□□ □□ 55 □□□□□□□□ □□□□□ □□।□□ □□□□□□□□□□ □□□ □□□□□□□ □□ □□□□□□-□□□□□□ □□ □□□□ □□□ □□ □□□ □□□□ □□□□ □□□ □□□□□□□ □□□□□□□□□□□ □□□□□ □□ □□□□□□ □□□ □□□□□□□ □□ □□□□ □□।□□□□ □□□□□□□□ □□ □□□□□ □□ □□□□ □□□□□□□ □□□□□ □□□□□□□ “□□□□□” □□ □□□□□□□ □□ □□ □□□□ □□ ।□□□□□ □□□□ □□□□□□□□ □□□□□ □□□□ □□□□ □□□□□ □□□□□□□□□□ □□ □□□□□ □□□□ □□□□□ □□□□□□ □□ □□□□ □□ ।

7. □□□□□□□ □□□□ **1963** □□ □□□□ **3(3)** □□ □□□□□□□□-

□□ □□□□□ □□ □□□□ 3(3) □□ □□ -□□□□□□□ □□□□□□□ □□ □□□ □□।

□□ □□□□□ □□ □□□ 451 □□□□□□ □□□□□□ □□□□ □□□।□□ □□□ □□ □□□□□□□□ □□□ □□□ □□□□□□ □□□ □□□□ □□□ □□।

8. □□□ □□□□□□□□-

□□□□□ □□□□□□ □□□□□ □□ □□□ □□□□□□□□ □□□ □□□□□ □□ □□□□□□ □□□□ 99 □□□□□□□ □□।□□□□□ □□ □□□□□□□ □□ □□□□□□ □□ □□□□□□□ □□□□

□□ □□□□□□ □□□□ □□।

9. □□□□□ □□□ □□□□□□□ □□□□□□ □□ □□□□□-

□□ □□□□□ □□ □□□□□ □□□ □□□□□□□ □□□□□□ □□ □□□□□ □□□□□ □□□ □□ □□□ □□ □□□ □□□।□□□□□ □□□ □□□□□□□ □□□ □□□□□□□□ □□□□□□ □□ □□□□□ □□□□□ □□□ □□□ □□।

10.□□□□□□□ □□ □□□□□□□□□□□□-

□□□□□ □□□□□□□□□□□□ □□ □□ □□□ □□□ □□□□ □□ □□□□□ □□ □□□□ □□□□□□□/□□□□□ □□ □□□□ □□ □□□ □□□□□□□□ □□□□□ □□ □□□□□□ □□ □□□□□□□ □□ □□□ □□ □□□□□ □□।□□□ □□□□□□□□ □□ □□□□□□□□□□□□□ □□□□□ □□□□□□ □□□□□ □□ □□□□□□□ □□□□□□□□ □□□□ □□□□□□ □□।□□ □□□ □□ □□ □□ □□□ □□ □□□□□ □□ □□□□□□□ □□□□□ □□ □□□□ □□ □□ □□□ □□□□□□□□ □□□□ □□ □□□ □□□□□ □□ □□□□ □□□□□ □□□□ □□ □□□□□□□□ □□ □□□ □□□□ □□□□□ □□□□□□□□□□ □□ □□□।

11.□□□□□ □□□□ □□ □□□□□□

□□□ □□□□□□□□□□□ □□□□ □□□□□□ □□□□□□ □□ □□□□□□□□□□□ □□□□□□ □□ □□□□□□ □□□□□□□ □□□□□ □□□□ □□ □□□□□□ □□ □□□□□ □□□□ □□□□□ □□□□ □□ □□□□□□□□□ □□□□ □□□□□□□ □□□□□□□/□□□□□□□ □□□□□ □□□□ □□।□□ □□□□ □□ □□□□□□□ 14.09.2023 □□ 28.09.2023 □□ □□□□□□□ □□□□□□□ □□□□□ □□□।□□ □□□□□ □□□□□ □□□□□□□□□□□□□ □□□□ □□□□□□□□□□ □□□□□□□ □□□□□ □□।□□□□□□ 26.09.2024 □□ □□□□□□□□□□ □□□□□□ □□□□□□□ □□ □□□□□ □□ □□□□□□□ □□□□ □□□□ 52 □□□□□□□□□□□ □ □□□□□□□□□□□□ □□ □□□□□□□□□ □ □□□□□□□-□□□□□ □□□□□□□ □□ □□□□□□□□□ □□□□□ □□□।

Chapter-16

VIGILANCE ORGANISATION

1. General

The activities of Vigilance Organization cover a wide range in various fields. The organization focuses on preventive aspects of Vigilance so as to result in major system improvements by use of information technology tools that would lead towards increased efficiency, plugging areas of leakage of revenue, minimize other irregularities / malpractices etc.

(a) The main areas of activities of vigilance may be broadly categorized as under:-

(i) Preventive checks with a view to effect System improvements.
(ii) Create awareness amongst rail employees about extant rules & instructions to avoid irregularities.
(iii) Investigations into genuine and owned complaints.
(iv) Punitive recommendations consequent to investigations.
(v) Integrity building along with moral & ethics amongst Railway employees & officers. Introducing best practices for Good Governance,
(vi) Vigilance Clearances.

(b) The activities of vigilance carried out in various areas have the following objectives:-

(i) Ensure observance of rules and procedures
(ii) To protect against leakages in Railway revenue.
(iii) Procedural and structural reforms to restrict and limit opportunities for corrupt practices.
(iv) Speedy action against delinquents to install a message for punitive action for mala-fide irregularities.
(v) Initiatives for integrity improvements.
(vi) To improve rail user's perception.


(c) The three pronged strategy of vigilance to boost Railway Revenue has been undertaken in:

(i) Mass Contact Areas.
(ii) Examination of internal business procedures.
(iii) Computerization & use of Information Technology.

2. Organization

Vigilance organization on the North Western Railway continued to function during 2023-2024 under the Administrative Control of Senior Deputy General Manager, who is also the Chief Vigilance Officer of the Railway. The sanctioned strength of the Vigilance Organization was as follows:-

ORGANIZATION CHART OF VIGILANCE BRANCH

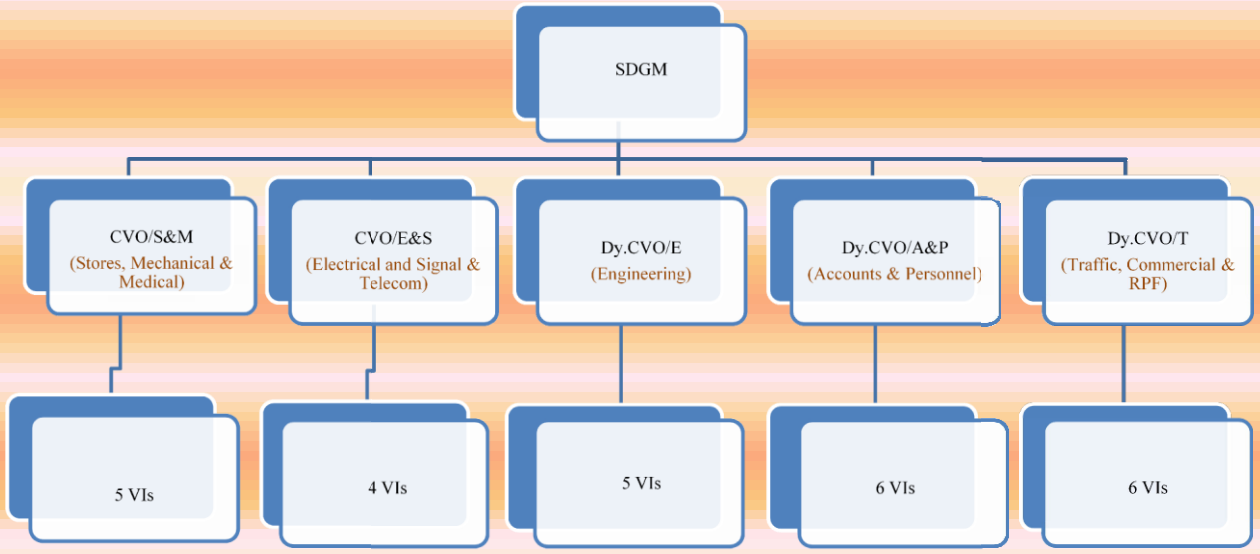

Office Strength of Vigilance Branch:-

Ministerial Cadre- (12)

Inquiry Inspector-(02)

Presenting Officer- (02)

Non-Gazetted Staff:-

1.	Field Staff [(26 VIs) & (6 RPF)[04 Head Constable & 02 Constable)]	32
2	Ministerial Office Staff	12

3. ***Investigation into Complaints:-***

Total number of complaints investigated by the Vigilance branch during the 2023-2024 and the result arising here from in the form of Major / Minor penalty proceedings are as under.

S.No		Total
(a)	Total number of complaints investigated	113
(b)	Total number of Major penalty proceedings arising there from (Number of staff both GO & NGO)	12
©	Total number of Minor penalty proceedings arising there from (Number of staff both GO & NGO)	12

4. ***Preventive Checks***:-

(a)	Number of Preventive checks undertaken	323
(b)	Amount realized raised towards Railway dues	₹ 50.97 (Lakhs)
(c)	Total number of Major penalty proceedings arising there from (Number of staff)	13
(d)	Total number of Minor penalty proceedings arising there from (Number of staff)	91

5. ***Statistical Information (Major and Minor):-***

		GO	NGO	Total
(a)	Number of DAR cases brought forward from the previous year	08	53	61
(b)	Number of fresh cases which arose during the year	05	125	130
(c)	Number of cases finalized	07	139	146
(d)	Number of cases outstanding at the end of the year	06	39	45

6. ***Earnings raised / realized due to irregularities***:- (in lakhs)

(a)	Staff payment	09.93
(b)	Mass contact and traffic under charges	09.84
(c)	Other earnings (Technical)	14.11
	Total earnings	33.88

7. ***Some other important activities during the year (2023-2024):-***

7.1 Vigilance Awareness Week-2023 as per CVC & Railway Board's directions, Vigilance Awareness Week was observed in right earnest and spirit over N.W. Railway from 30th October, 2023 to 5th November, 2023.In this regard, banners and posters were displayed

at prominent locations in NWR. Various activities such as Essay Competitions, Slogan Writing, Nukkad Natak, Poem Recitations, Vigilance Seminar, Vigilance Workshops etc were organize at Head quarter and field units . As directed by CVC, various programme such as debates, elocution, panel discussion, painting, essay writing, Quiz and Slogan writing were organized at schools / colleges of Divisions in NWR, which attracted very good participation of students / Railway employees and their families. The detailed report of the activities conducted was sent to Railway Board after completion of Vigilance Awareness Week. During the week, a seminar along with valedictory session was organized in NWR, HQ Office on the subject " Say no to corruption ; Commit to the Nation" (□□□□□□□□□□ □□ □□□□□ □□□□; □□□□□□□ □□ □□□□□ □□□□□□□ □□□□ ") in which Sh. Hemant Priyadarshy, IPS, Addl. Director General & Additional charge of DG, ACB Rajasthan, was Chief Guest. The function was presided by GM, North Western Railway and attended by the officers of North Western Railway. The winners of the different activities held during the week were given Prize and Certificates.




उत्तर पश्चिम रेलवे
सतर्कता जागरुकता सप्ताह
30 अक्टूबर से 5 नवम्बर, 2023
भ्रष्टाचार का विरोध करें; राष्ट्र के प्रति समर्पित रहें


North Western Railway
Vigilance Branch
workshop on
Cyber Hygiene & Security
As precursor to VAW-2023



7.2 Further, Vigilance Bulletin was unveiled by G.M NWR & Chief Guest. Same was distributed amongst the officers and staff of the Railway.



Chapter-17

General Department

Public Relation Office - Narrative Report 2023-24

(1). PUBLIC RELATIONS

The year 2023-24 was an eventful year over North Western Railway & Public Relations Department did intensive coverage through print & electronic media for timely dissemination of information to rail users & public.

(2). Display Ad from 01 April 2023 to March 2024

1. Foundation stone Amrit Bharat Station Scheme by Hon'ble Prime Minister Shri Narendra Modi through Video Conferencing on 06.08.2023
2. Social Media Hero campaign on inaugural of Udaipur – Jaipur – Udaipur Vande Bharat Express on 22.09.2023
3. Inauguration of Jaipur- Udaipur Vande Bharat Express by Hon'ble Prime Minister Shri Narendra Modi through Video Conferencing on 24.09.2023
4. Foundation stone of Station Re-development work by Hon'ble Prime Minister Shri Narendra Modi through Video Conferencing on 26.02.2024.

(3). Publicity Materials

11

(4). Electronic Media

02 Campaign on Various subjects.

(5). FM Radio

15 campaigns on various subjects.

(6). SMS

NIL

(7). Film Shooting

1. Shooting of Film "Untitled" Hindi Film at LC-14 between Mandore – Marwar Mathaniya Over Jodhpur division on 29.06.2023, 30.06.2023.

2. Shooting of “Silence-2- The Night over Murder” Hindi Film at Durgapura over Jaipur on 12.09.2023

(8). Film/ Short Films

1. **75 Reals/Movies**

(9). Still Photography

NIL

(10). Exhibition

NIL

(11). Major Functions

1. Hon’ble Prime Minister Shri Narendra Modi inaugurated the Ajmer-Delhi Cantt Vande Bharat Express through video conferencing from Delhi on April 12, 2023
2. Hon’ble Prime Minister Shri Narendra Modi flagged off the Jodhpur-Ahmedabad (Sabarmati) Inaugural Special Vande Bharat Express through video conferencing on 07.07.2023
3. Hon’ble Prime Minister Shri Narendra Modi inaugurated the semi high-speed Vande Bharat Express train, which operates between Udaipur and Jaipur through video link from Delhi on 24th September 2023.
4. Hon’ble Prime Minister Shri Narendra Modi laid the Foundation Stone for three significant rail projects in Nathdwara on May 10, 2023
5. Hon’ble Prime Minister Shri Narendra Modi laid the Foundation for Redevelopment of Bikaner Station and the Doubling of Churu-Ratangarh Railway Line in Bikaner on 08.07.2023
6. Prime Minister Shri Narendra Modi laid the Foundation Stone for the Redevelopment of 508 Indian Railway Stations through video conferencing under the Amrit Bharat Station Scheme On August 6, 2023
7. Hon’ble Prime Minister Shri Narendra Modi inaugurated railway doubling projects, he flagged off a heritage train on the Marwar Jn.-Khamli Ghat meter gauge rail line and also a new train service between Jaisalmer and Delhi on October 5, 2023
8. Hon’ble Prime Minister Shri Narendra Modi virtually laid the Foundation Stone and dedicted eight railway projects for Rajasthan on February 16, 2024
9. Hon’ble Prime Minister Shri Narendra Modi laid the foundation stone of 4 railway Doubling projects in Haryana at Rewari on February 16, 2024
10. Hon’ble Prime Minister, Shri Narendra Modi laid the Foundation and Dedicated to the Nation Railway Infrastructure Projects worth over Rs. 41,000 crore through video conferencing on 26th February 2024

11. Hon'ble Prime Minister Shri Narendra Modi laid the foundation stone and and dedicated railway projects, rail development works, and passenger amenities costing more than Rs. 85 thousand crore on 12.03.2024

(12). Press Release

Total Press Release issued - 1189

(13). Rejoinder - 08

(14). Video Releases - 389

(15). Press Conference - 26 (HQ & Divisions)

(16). Social Media (Followers as on 31.03.2024)

1. Facebook - 257943 Followers
2. Twitter – 191567 Followers
3. Instagram - 8087 Followers
4. YouTube - 4005

Law Cell

Required information for position of consolidated court cases of various courts i.e. Supreme Court, High Courts, National Commission, State Commission, District Forum, Railway Claim Tribunal, Central Administrative Tribunal and District Courts are as under:-

Opening Balance as on 01.04.2023	Cases Accrued during the year April 2023 to March 2024	Decided the cases during the year April 2023 to March 2024		Closing Balance as on 31.03.2024
		Won	Lost	
3874	1093	664	285	4018

In reference to above, progress of Confidential Cell for the year 2023-24 is as under:

1. Ministry of Railways has implemented online filing of APARs from 2017-18 of all Railway officers on SPARROW, an application developed by National Informatics Centre. SPARROW is a user friendly interactive application software programme which keeps the confidentiality of the work which can be logged-in each time by using NIC mail IDs with Password or with adhar based e-sign and the access to the system is OTP protected which is received on the user's mobile number registered with PIMS. The officers reported upon process the APAR by filling in the self appraisals and thereafter forwarded as per workflow to the respective reporting/reviewing/accepting authorities in the system. SPARROW is also facilitating the officers reported upon for submitting online representation, if any, for requesting to upgrade the grading or to remove any adverse entry given by the authorities. This office also facilitated the officers in updating their mobile number by sending details to Railway Board, so that OTP and communication could be done with the officer to get the access each time and facilitate finalization of APARs.

2. The creation of NIC mail IDs upon direct fresh appointment of officers at NWR or through promotion in Group 'B' is a year round process as facilitated by this office by sending such request to Railway Board and filling in their details on PIMS after creation of their NIC mail IDs. Thereafter, the work of generation of APARs at SPARROW has been carried out at Confidential Cell for these officers posted at Headquarters/divisions/independent units-NWR. Necessary assistance has also been provided by Confidential Cell to all the concerned officers/staff for filling up of APARs by officers in respective capacity of officer Reported Upon/Reporting Authority/Reviewing Authority/Accepting Authority. This office also forwarded the officers' request to Railway Board for re-activating their Nic Mail Id or cancelling the Nic Mail Id where different IDs have been issued for SPARROW and for E-Office.


3. Confidential Cell/HQ/NWR had generated online filling of 1443 APARs of 994 officers for year 2023-24. Out of which, 706 APARs are in process at various levels (self appraisal /reporting/reviewing/accepting).

4. The filing of Immovable Property Return (IPR) from officers is mandatory on SPARROW in its IPR module. The Confidential Cell/HQ/NWR has made its efforts to pursue and to assist/guide the officers to fill-up/upload their Annual Immovable Property Return on SPARROW through their account. Presently, total no. of IPR uploaded for 01.01.2024 on SPARROW under IPR module is 753.

5. Confidential Cell has also identified 369 dossiers & 34 files/registers upto 2013-14 for weeding out as per GOI Record Retention Schedule. NOC has been sought from Personnel, Vig & Law Deptt.

In reference to above the desired information is as under:-

Work Study Cell is functioning with following organization structure:

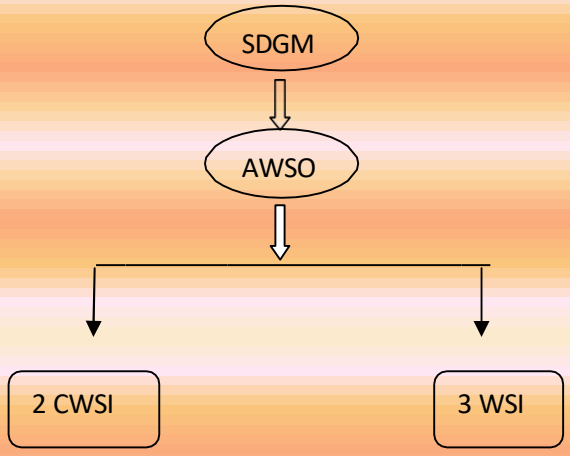

The comparative figures of financial year2023-24 with 2022-23 are as under:-

Sr. No.	Description	2022-23	2023-24
1.	No. of Work Studies completed	11	18
2.	Target for surrendering the posts given by Railway Board	650	1182
3.	Target achieved	550	168
4.	Posts identified as surplus	442	631
5.	Surrenders pending for acceptance	530	993
6.	Surrenders pending for implementation	530	993
7.	Annual Recurring Savings (Rs.)	1815.57 (Lac.)	414.36 (Lac.)

RAILWAY USERS' CONSULTATIVE COMMITTEE

(A) Zonal Railway Users' Consultative Committee & Divisional Railway Users' Consultative Committee, North Western Railway:

These committees are consultative in character. The object is to provide frequent opportunities for consultation on matters relating to the service provided by Railways & devising ways & means of effecting improvement.

The Zonal Railway Users' Consultative Committee at HQ level & Divisional Railway User's Consultative Committee on various Divisions of NWR have been reconstituted for the term from Nil (ZRUCC) & 05.9.23 /07.2.24/12.5.23/02.2.24/08.9.23/12.5.23(DRUCC).

Areas of Committees on NWR is as under :

1. HQ Level (ZRUCC)
2. Ajmer Division (DRUCC)
3. Jodhpur Division (DRUCC)
4. Jaipur Division (DRUCC)
5. Bikaner Division (DRUCC)

Details of ZRUCC/DRUCC Meeting held from 01.04.23 to 31.3.2024

Meeting	HQ/Division	No. of Meetings	Dates of Meeting
ZRUCC	NWR-HQ-JP	01	Nil
DRUCC	Ajmer	02	05.9.2023 & 07.02.2024
	Bikaner	02	12.5.2023 & 02.2.2024
	Jodhpur	01	08.9.2023
	Jaipur	01	12.5.2023

(B) The number of PREM meeting held at Zonal/Divisional level of this Railway during the year 2023-2024 is given below:-

Meeting	HQ/Division	No. of Meetings	Dates of Meeting
Zonal	NWR-HQ-JP	Nil	Nil
Division	Ajmer	Nil	Nil
	Bikaner	01	12.1.2024
	Jodhpur	02	30.10.2023 & 21.12.2023
	Jaipur	Nil	Nil

(c) General Manager's Annual Inspection

In reference to above subject matter that GM Annual Inspection has been dispensed by Railway Boards letter No. 2022/CC/Inspection/Genl. Date-31.12.2022.

Sr. No.	Division	Date	Section/Station
1	Ajmer Division	Nil	Nil
2	Bikaner Division	Nil	Nil
3	Jodhpur Division	Nil	Nil
4	Jaipur Division	Nil	Nil
5	Ajmer Workshop	Nil	Nil
6	Bikaner Workshop	Nil	Nil
7	Jodhpur Workshop	Nil	Nil

Statement showing Receipt & Disposal of RTI/Appeal cases during the period from 01.4.2023 to 31.3.2024


Sr. No.		Unit	OA/FA O/B 01.4.2023	Receipt during the year	Total	Disposed	Closing Balance 31.3.2024
1	OA	HQ	209	2875	3084	2954	130
	FA		6	82	88	79	9
2	OA	JP Div.	40	1740	1780	1709	71
	FA		5	171	176	164	12
3	OA	Aii Div.	40	1715	1755	1733	22
	FA		0	147	147	146	1
4	OA	JU	36	1085	1121	1088	33
	FA	Div.	9	124	133	131	3
5	OA	BKN	84	1948	2032	1983	49
	FA	Div.	14	135	149	144	5
6	OA	AII W/s	13	499	512	493	19
	FA		2	39	41	38	3
7	OA	JU	6	175	181	168	13
	FA	W/s.	0	13	13	12	1
8	OA	BKN	12	176	188	155	33
	FA	W/s.	3	8	11	11	0
9	OA	ZTC	2	179	181	180	1
	FA		0	6	6	6	0
TOTAL	OA		442	10392	10834	10463	371
	FA		39	725	764	731	33
II Appeals			0	44	44	39	5

Achievements / High Lights

The comparative statement showing the cases received and disposed off during the period from 01.04.23 to 31.03.24

S.N.	Received from	Total for received during the yr 01.04.23 to 31.03.24	Disposed off during yr 01.04.23 to 31.03.24	Pending As on 31.03.24	Achievement in % age.
1	PRESIDENT SECRETARIAT	22	17	5	77%
2	PMO Cases	430	420	10	98%
3	Spl. Monitaring cases	0	0	0	0%
4	State Government	58	58	0	100%
4	DPG (Cabinet Sec.)	34	34	0	100%
5	DOP&PW	379	374	5	99%
6	DOAR&PG	16	16	0	100%
7	Others {MORLY .PG cases} CA III	2205	2141	64	97%
8	MP-MLA cases	146	132	14	90%
9	CPGRAMS- Appeal	906	901	5	99%
	TOTAL -	4146	4093	103	99%

PERIOD	**NO. OF COMPLAINTS RECEIVED**	NO. OF COMPLAINTS DISPOSED OFF
2022-2023 (1.4.22 to 31.3.23)	**2694**	2600
2023-2024 (1.4.23 to 31.3.24)	**4146**	4093
Variation in %	**54%**	57%

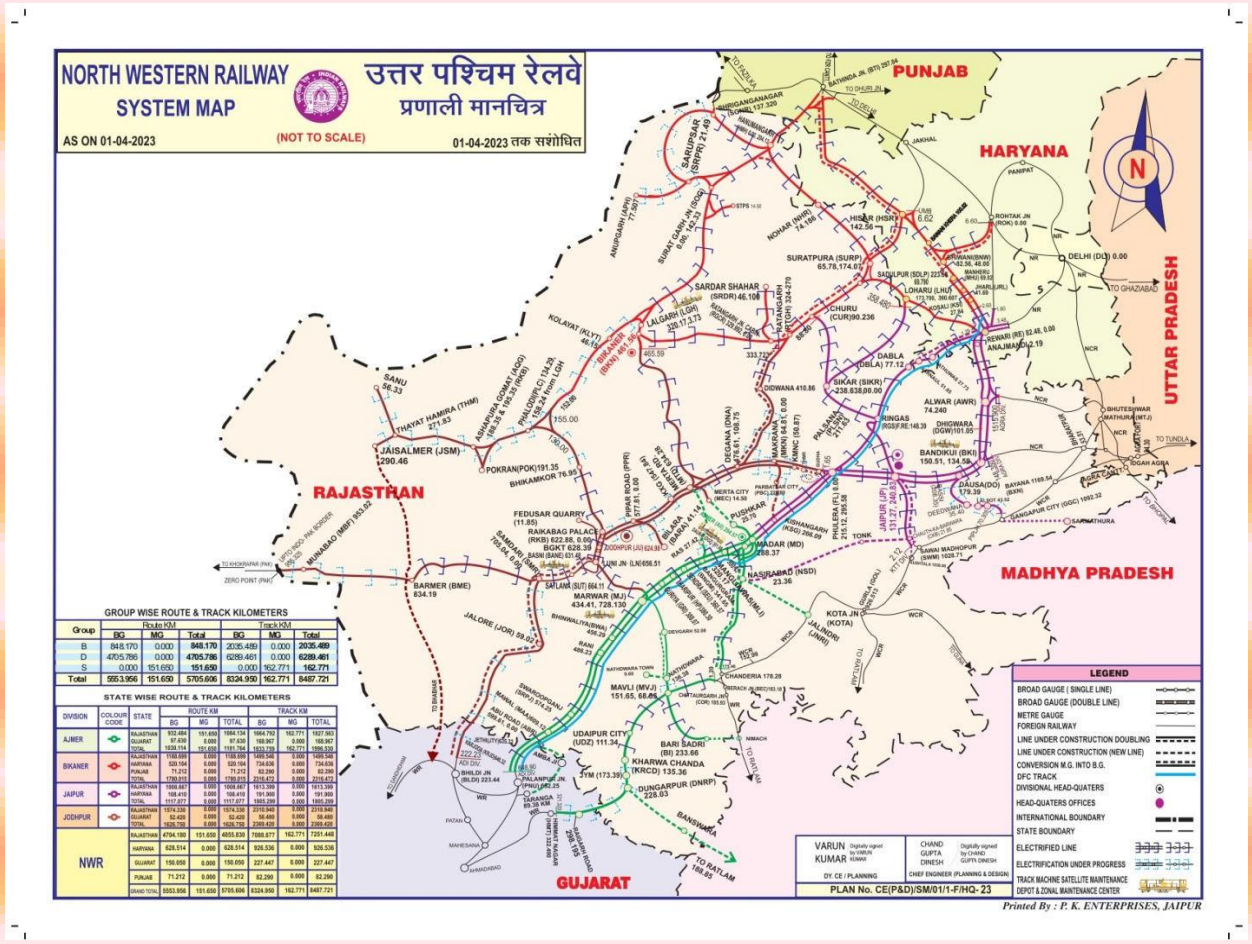

GROUP WISE ROUTE & TRACK KILOMETERS

Group	Route KM			Track KM		
	BG	MG	Total	BG	MG	Total
B	848.170	0.000	848.170	2035.489	0.000	2035.489
D	4705.786	0.000	4705.786	6289.461	0.000	6289.461
S	0.000	151.650	151.650	0.000	162.771	162.771
Total	5553.956	151.650	5705.606	8324.950	162.771	8487.721

STATE WISE ROUTE & TRACK KILOMETERS

DIVISION	COLOUR CODE	STATE	ROUTE KM			TRACK KM		
			BG	MG	TOTAL	BG	MG	TOTAL
AJMER		RAJASTHAN	932.484	151.650	1084.134	1664.792	162.771	1827.563
		GUJARAT	97.630	0.000	97.630	168.967	0.000	168.967
		TOTAL	1030.114	151.650	1181.764	1833.759	162.771	1996.530
BIKANER		RAJASTHAN	1168.699	0.000	1168.699	1495.548	0.000	1495.548
		HARYANA	520.104	0.000	520.104	734.636	0.000	734.636
		PUNJAB	71.212	0.000	71.212	82.290	0.000	82.290
		TOTAL	1760.015	0.000	1760.015	2312.473	0.000	2312.473
JAIPUR		RAJASTHAN	1008.867	0.000	1008.867	1613.399	0.000	1613.399
		HARYANA	108.410	0.000	108.410	191.969	0.000	191.969
		TOTAL	1117.077	0.000	1117.077	1805.299	0.000	1805.299
JODHPUR		RAJASTHAN	1574.330	0.000	1574.330	2310.940	0.000	2310.940
		GUJARAT	52.420	0.000	52.420	58.480	0.000	58.480
		TOTAL	1626.750	0.000	1626.750	2369.420	0.000	2369.420
NWR		RAJASTHAN	4704.180	151.650	4855.830	7888.677	162.771	7251.448
		HARYANA	628.514	0.000	628.514	926.536	0.000	926.536
		GUJARAT	150.050	0.000	150.050	227.447	0.000	227.447
		PUNJAB	71.212	0.000	71.212	82.290	0.000	82.290
		GRAND TOTAL	5553.956	151.650	5705.606	8324.950	162.771	8487.721
